

BOND UPDATE #172

9.9.22

Here's what is going on with our bond projects.

Enjoy!

1. Our new gym hosted its first official FHS athletics match Thursday night! Our Golden Eagles volleyball team defeated Lynden Christian in a five-set thriller. Here's to many more victories in our new Athletic Wing!
2. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Athletic Wing

- Now that wall painting in the Auxiliary Gym is complete, final finishes such as wall panels, padding, scoreboards and shot clocks will begin installation next week.
- In the kitchen area, crews formed and poured foundations for the sub-structure that will support the various kitchen hoods, ceilings, lights and fire sprinklers.

Academic Wing & Commons

- Ceiling grid and cabinet installation is underway on the third floor, and crews are making good progress.
- Light fixtures are almost complete on the second floor.
- Glass installation is nearly finished on the first floor, and making progress across the second floor.
- Bathroom partitions and accessories are being installed on the second floor. This work should be close to completion next week.
- The entryway doors for the elevator have been installed, and the front wall of the elevator shaft is now enclosed. Crews are now working on completing the elevator cab, which is the part of the elevator that passengers ride in.
- Final flooring work in the Academic Wing is slated to begin in late September or early October. Once this starts, the area will begin to look almost finished.


CTE Village

- The wall panels on the Agriculture Science and Aquaculture buildings have been installed. The buildings are getting ready to receive siding, doors and windows.


Site Work

- The underground stormwater detention system north of the new gym had most of its components installed last week; this week, the system is being covered in gravel. Soon, the area will be ready to start the construction of the final new bus loop.


- Crews have begun forming and pouring the curbs and gutters in the new staff parking area south of the Academic Wing.
 - The service entrance area to the east of the kitchen will begin having final preparations made to prepare the area for the final pavement in early October.
3. At the end of this week’s update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
 4. Below is the FHS project timeline as of July 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

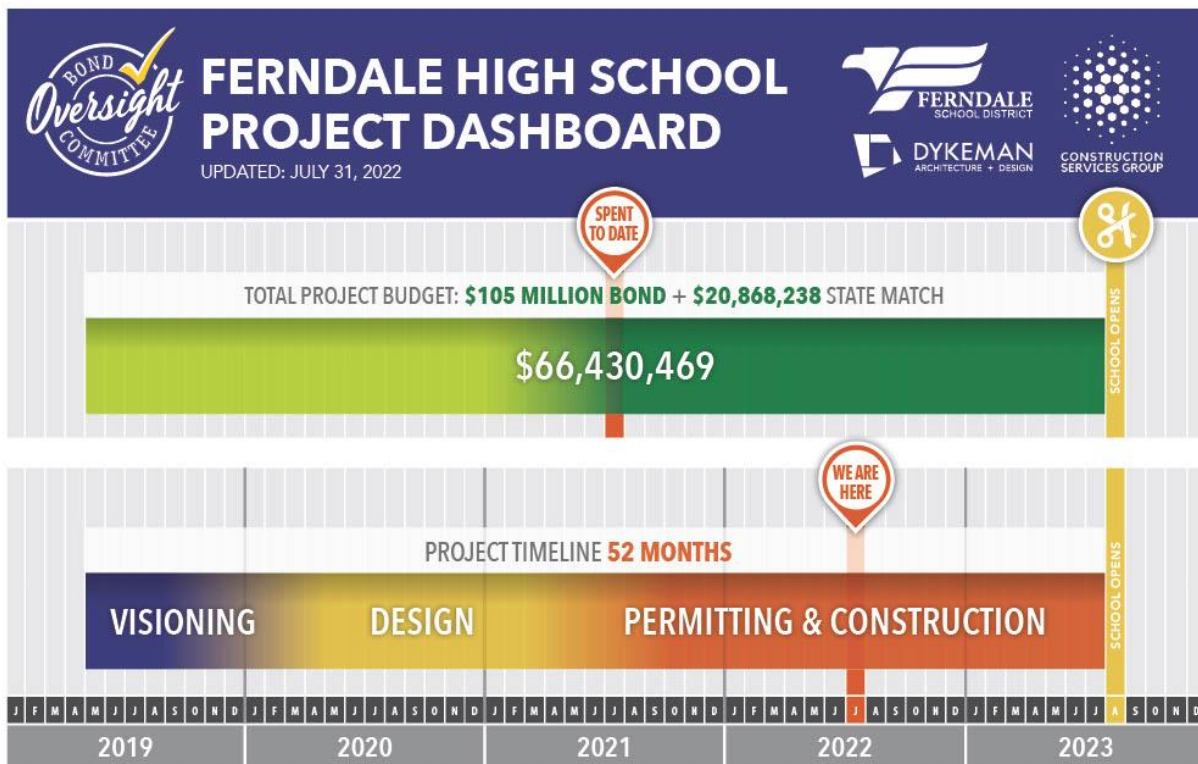

5. Below is a map showing the various components of the new FHS campus and when they’ll be completed.

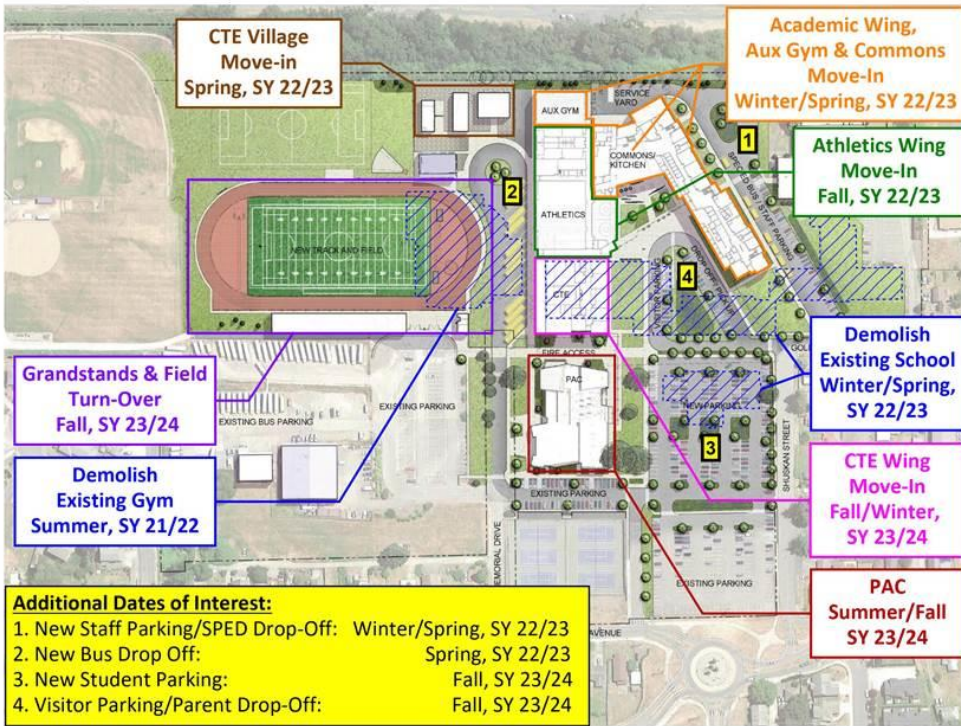

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Auxiliary Gym walls are painted and ready for final finishes



Forming for substructure foundations in the kitchen area



Entryway door and front wall of the elevator being installed



Underwater stormwater storage system on the north side of the new gym receiving its final topping of gravel



Curbs and gutters being formed at the staff parking area south of the Academic Wing



Wall panel installation at the Agriculture Science building
