

Crown Point Community School Corporation Construction Projects

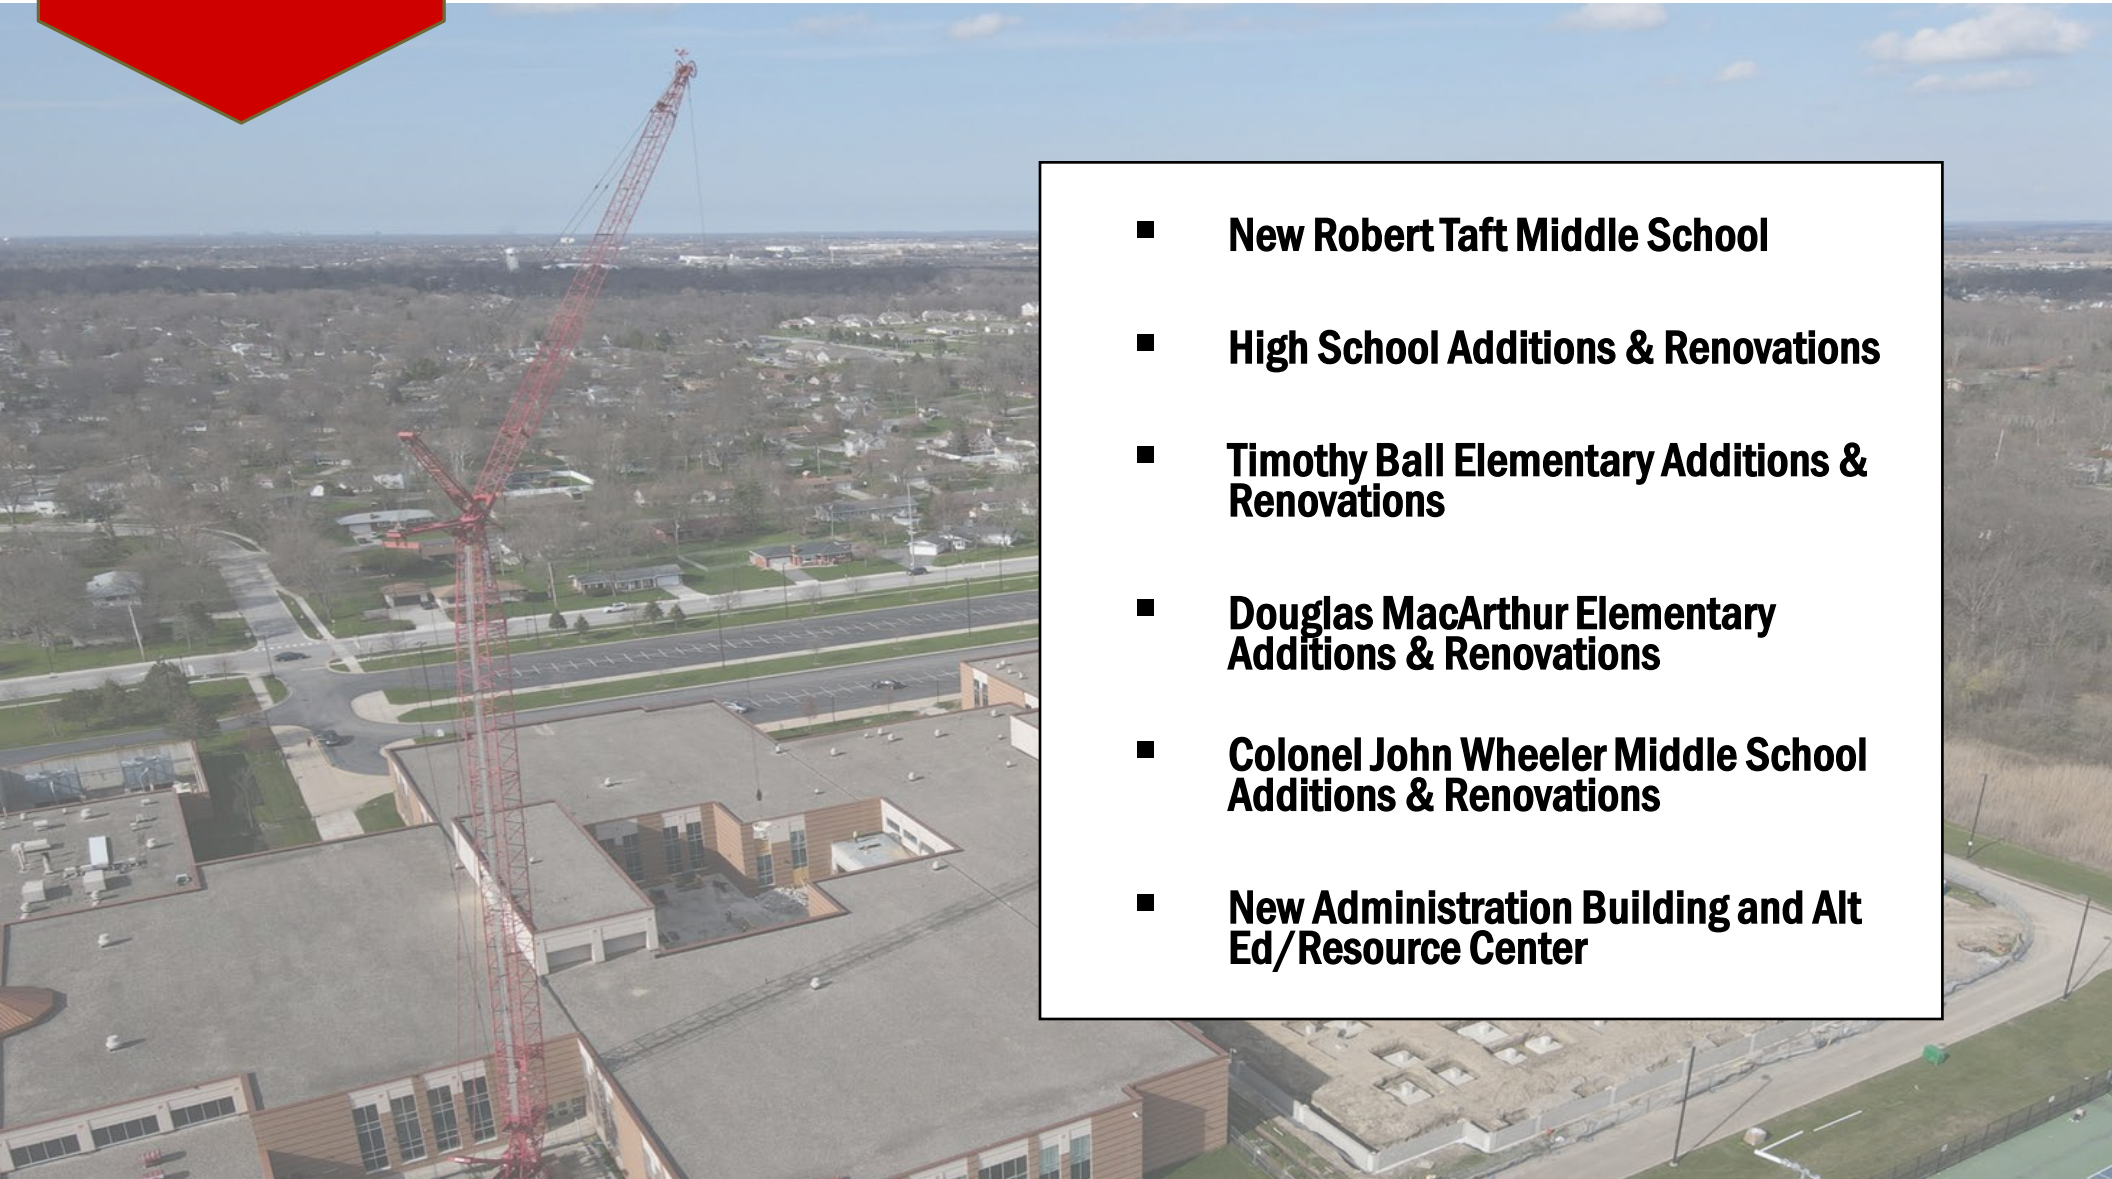
Board Report September 26, 2022



Table of Contents

Crown Point Community School Corporation Construction Projects

Board Report
September 26, 2022

- 
- **New Robert Taft Middle School**
 - **High School Additions & Renovations**
 - **Timothy Ball Elementary Additions & Renovations**
 - **Douglas MacArthur Elementary Additions & Renovations**
 - **Colonel John Wheeler Middle School Additions & Renovations**
 - **New Administration Building and Alt Ed/Resource Center**



Progress Photographs



New Robert A. Taft Middle School:

- Completed metal stud framing in the academic wing
- Completed electrical and plumbing rough-ins in the academic wing
- Completed piping and grading of west and east ponds
- Started on facebrick around the academic wing
- Started on metal stud framing in Unit A
- Started grading and concrete curbs along 121st Ave

Auditorium and Performing Arts CMU Walls



Progress Photographs



Front Aerial

New Robert A. Taft Middle School:

Next Four Weeks

- Complete facebrick around academic wing
- Complete interior CMU walls in Unit F
- Complete setting structural steel
- Continue load bearing CMU walls in Unit J and Unit K
- Continue roofing membrane
- Continue to install exterior windows
- Begin installing interior drywall in academic wing



Progress Photographs



Classroom Addition CMU Walls

High School Additions & Renovations:

- Completed erection of structural steel for classroom addition
- Poured slab-on-grade for classroom addition
- Completed setting structural steel for Unit F (courtyard infill)
- Began setting structural steel for athletic addition
- Began prepping performing arts addition for structural steel



Progress Photographs



Athletic Addition Structural Steel

High School Additions and Renovations:

Next Four Weeks

- Complete erection of structural steel for athletic addition
- Complete erection of structural steel for performing arts addition
- Pour slab-on-deck for classroom addition
- Pour slab-on-grade for performing arts addition
- Begin overhead mechanical piping in classroom addition



Progress Photographs



Pre-K and Gymnasium Addition

Timothy Ball Additions & Renovations:

- Completed roofing of classroom addition
- Completed interior metal stud framing in classroom addition
- Poured slab-on-grade for east additions
- Continued laying masonry bearing CMU walls for gymnasium
- Began erection of structural steel for kindergarten wing
- Began installation of windows in classroom addition
- Began above ceiling mechanical piping in classroom addition



Progress Photographs



Kindergarten Slab-on-Grade

Timothy Ball Additions and Renovations:

Next Four Weeks

- Complete structural steel in kindergarten addition
- Complete installation of windows in classroom addition
- Begin erection of structural steel for gymnasium addition
- Begin erection of structural steel for pre-kindergarten wing
- Begin exterior wall framing of kindergarten addition
- Begin roofing of kindergarten addition



Progress Photographs



Classroom Addition Structural Steel

Douglas MacArthur Additions & Renovations:

- Completed underground electric and plumbing for classroom addition
- Completed above ceiling mechanical piping from boiler room to classroom addition
- Poured slab-on-grade for classroom addition
- Began concrete footings and piers for mechanical penthouse and gymnasium addition
- Began erection of structural steel for classroom addition and mechanical penthouse



Progress Photographs



Gymnasium Addition Footings

Douglas MacArthur Additions and Renovations:

Next Four Weeks

- Complete gymnasium addition footings and foundations
- Pour slab-on-deck for mechanical penthouse
- Begin load bearing CMU walls for gymnasium addition
- Begin exterior metal stud framing of classroom addition
- Begin electrical and plumbing rough-ins at classroom addition



Progress Photographs



Auditorium Addition Footings

John Wheeler Additions & Renovations:

- Completed site utilities throughout entire site
- Completed binder for new south parking lots
- Completed concrete footings for auditorium addition
- Completed Unit D restroom tile and fixtures



Progress Photographs



New South Parking Lots

John Wheeler Additions and Renovations:

Next Four Weeks

- Complete footings and foundations in classroom addition
- Begin exterior CMU walls for classroom and auditorium additions
- Begin underground electrical and plumbing in auditorium addition
- Begin erecting structural steel for auditorium addition



Progress Photographs



New Administration Building and Alt Ed/Resource Center:

- Completed pouring concrete footings and piers
- Completed underground electrical work
- Completed underground plumbing work
- Completed grading for slab-on-grade
- Completed CMU foundations and elevator shaft
- Continued installing new storm system
- Began setting structural steel

New Administration Center Structural Steel



Progress Photographs



New Administration Center Overhead

New Administration Building and Alt Ed/Resource Center :

Next Four Weeks

- Complete setting structural steel
- Pour slab-on-grade
- Begin installation of new sanitary line
- Begin installation of new water lines
