

# BOND UPDATE #175

9.30.22

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

## Auxiliary Gym and Kitchen

- Crews began installing the wood flooring in the Auxiliary Gym this week. This pushes us very close to completion.
- Wall framing in the kitchen area has made a lot of progress this week, and the substructure which will carry the ceiling lights and exhaust hoods is almost finished. Plumbers and electricians are ready to start installing their in-wall items next week.

## Academic Wing & Commons

- Cabinets, casework and trim have made good progress across the third floor. This should be complete in a couple of weeks.
- Light fixtures are substantially complete on the second floor and should start being installed on the third floor sometime next week.
- Grinding and polishing of the concrete corridor floors on the first floor is set to begin in the first week of October. A week or so later, the carpet installation will start, and the Academic Wing will start having an almost-finished feel.
- Now that stair treads have been installed in the primary stairwell, final finishes are underway in all three stairwells in the Academic Wing.
- We are very close to having the exterior finishes complete. It's starting to look like a completed building on the outside!
- The main window wall in the Commons Area is now having the sun shades installed. It's close to completion.


## CTE Village

- Metal siding is underway on the Agriculture Science building and is almost complete. Interior walls are now being framed, and electrical/mechanical infrastructure installation will begin soon.


## Site Work

- Exterior light pole bases have been installed around the new bus loop area on the north side of the new gym. Curb and gutter installation will start soon in this area, and that is the final prep before laying asphalt paving.
- The last few sidewalks and curbs have been poured around the staff parking area south of the Academic Wing.


- The kitchen service entrance area east of the Athletic Wing has now had sidewalks poured, and crews are readying the area for asphalt.
  - All three of the above mentioned areas will be ready for asphalt paving in mid-October.
2. At the end of this week’s update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
  3. Below is the FHS project timeline as of August 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

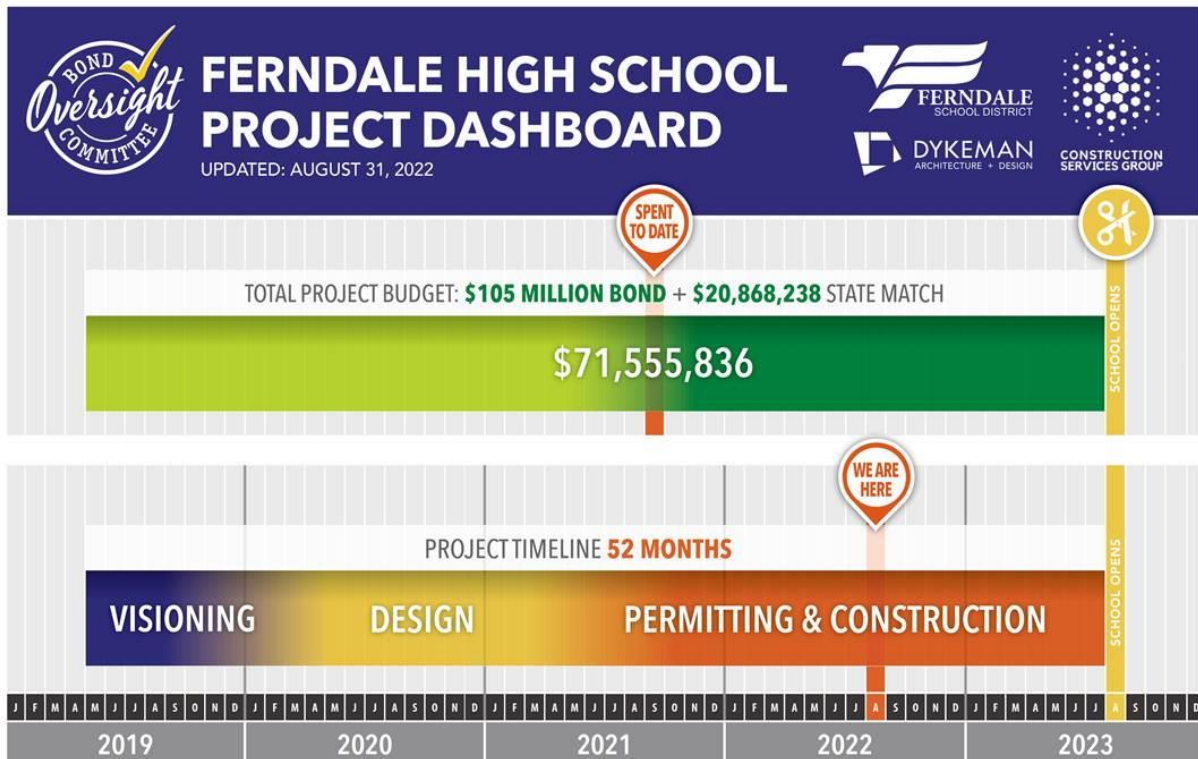

4. Below is a map showing the various components of the new FHS campus and when they’ll be completed.

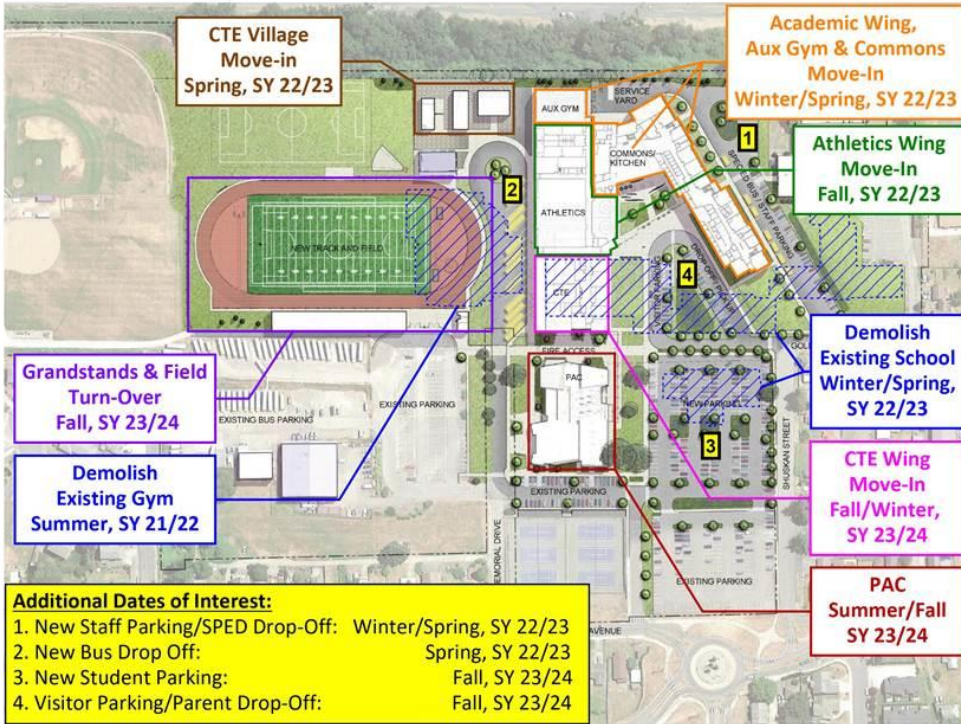

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



**Flooring installation in the Auxiliary Gym**





**Framed walls at the serving area of the new kitchen**



**Sun shade installation in the commons area**



**Whiteboard installation in the Academic Wing**





**Final sidewalks being poured in the staff parking area south of the Academic Wing**





**Sidewalks being poured in the kitchen service yard area**
