

BOND UPDATE #176

10.7.22

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Auxiliary Gym and Kitchen

- The wood flooring in the Auxiliary Gym is now installed and sanding is complete. Crews are beginning to lay out the court game lines.
- Wall framing is close to wrapping up in the kitchen area, and the plumbers and electricians will start installing their in-wall items over the next couple of weeks. The walk-in coolers should begin installation next week.

Academic Wing & Commons


- The first floor is now completely into the final finishes:
 - The corridor floors are being ground and polished.
 - Carpet and rubberized flooring will begin installation next week.
 - Work on the final door hardware is underway, as well as the final painting work.
 - The Culinary Arts area now has all cabinets installed, and the final work on the ceiling should occur next week.
- The second floor has crews working on finishes that need to be completed prior to final flooring work starting in a couple of weeks:
 - Ceiling tile installation work is ongoing and should wrap up over the next couple of weeks.
 - Light fixtures continue to be installed. This should be close to complete next week.
 - Door installation is ongoing and is getting close to receiving the final hardware.
- The third floor is seeing the following activities:
 - The final cabinets are being installed. This work should be finished in a couple of weeks.
 - Light fixture installation is ongoing and should be complete around the end of next week.
 - Ceiling final cover inspections will occur in the middle of October, and then the area will be ready for final ceiling tile installation.

CTE Village


- The Agriculture Science Building is now having the heating equipment installed. This should take a week or two.
- Crews are installing siding on the Aquaculture Building. It's starting to look like a finished product on the outside.
- The Greenhouse is currently sitting idle, waiting for the delivery of the new plexiglass panels that will form the exterior shell of the building. Those panels were ordered recently.

Site Work

- Final prep work for asphalt is underway on the bus loop to the north, the parking area to the south, and the service yard to the east. There's a good chance asphalt work will begin later next week.
2. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
 3. Below is the FHS project timeline as of August 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

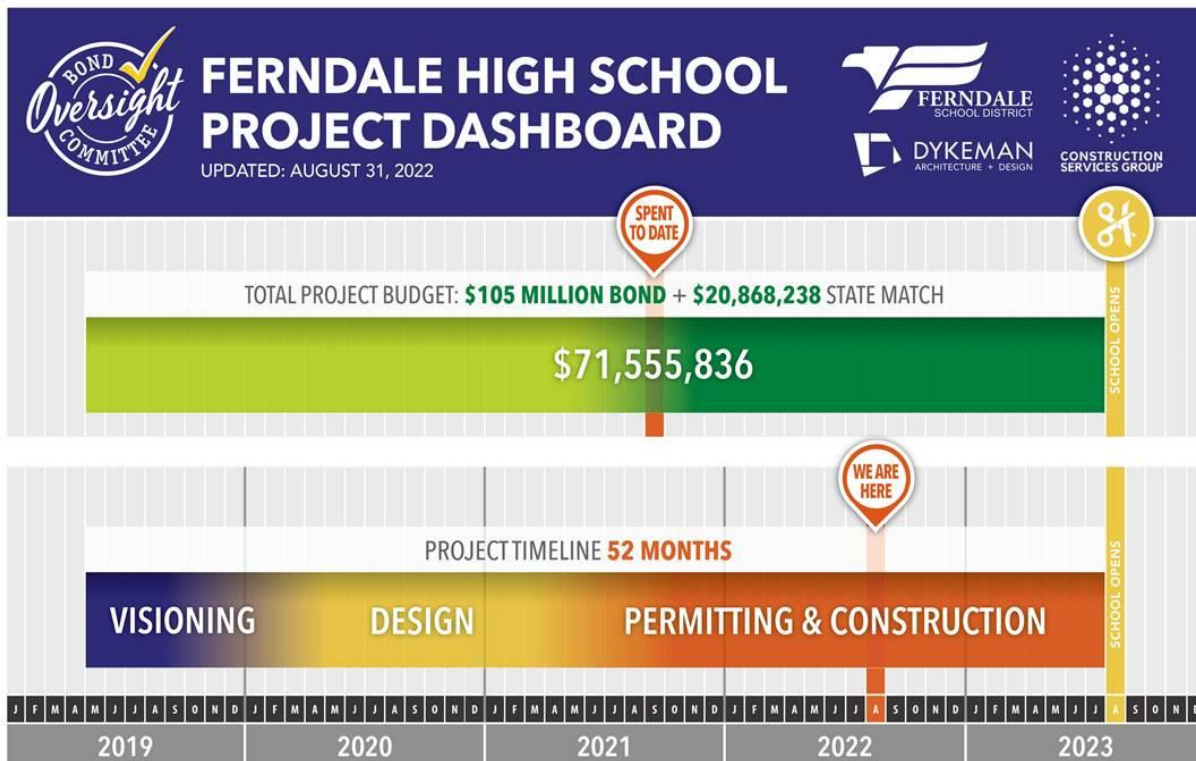

4. Below is a map showing the various components of the new FHS campus and when they'll be completed.

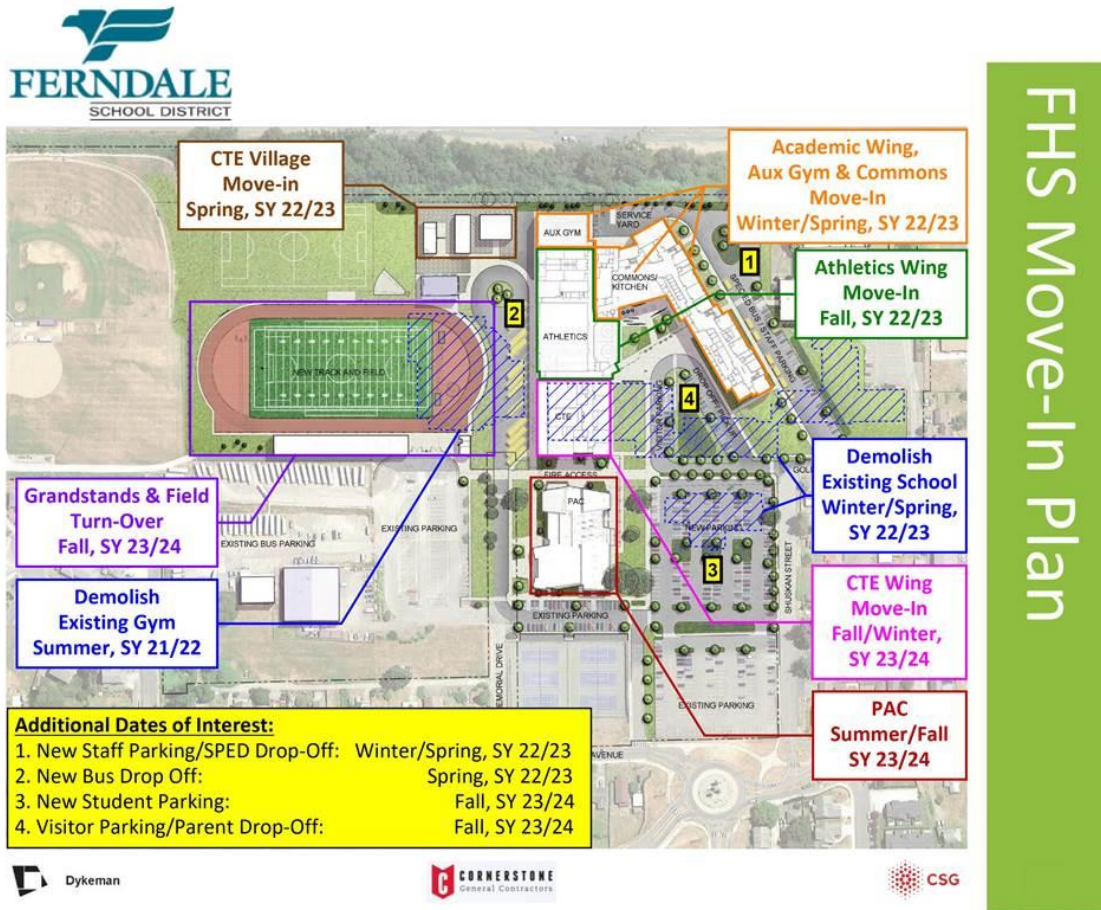

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Final sanding of the wood flooring in the Auxiliary Gym



Sunshade installation on the commons area window wall that faces the west



Concrete grinding and polishing of the Level 1 corridors



Fire extinguisher cabinet installation on the first floor corridor



Ductwork installation in the Aquaculture Building



Final prep work for asphalt in the new bus loop north of the new building



Final prep work for asphalt in the parking lot south of the new building



Final prep work for asphalt in the service yard east of the new building
