

BOND UPDATE #178

10.21.22

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. The Ferndale School Board will hold their next regular meeting at 6 p.m. Tuesday at Mountain View. The Board will receive an update on bond-related capital projects.
2. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Auxiliary Gym and Kitchen

- The game lines in the Auxiliary Gym were completed this week. The space is set to be turned over to the school in November.
- Walk-in coolers are now installed in the kitchen, and the electricians and plumbers should be complete with their items soon. This will allow sheetrock installation to begin next week.

Academic Wing & Commons


- The first floor is now completely into the final finishes:
 - Carpet installation is ongoing and should be wrapped up in early November.
 - Work on the final door hardware, and door painting, is ongoing and should wrap up in the next couple of weeks.
 - The Culinary Arts area had ceiling tiles installed this week, and flooring work should begin next week.
- The second floor is transitioning into final finishes:
 - The final ceiling tiles on this floor are now substantially complete.
 - Grinding and polishing of the corridor floors started this week, and crews are making good progress.
 - The carpet on this floor should begin installation over the next few weeks.
- The third floor is seeing the following activities:
 - The final cabinets have primarily been installed this week.
 - Light fixture installation is now finished on this floor.
 - Final ceiling tile installation has begun and will be ongoing over the next several weeks.
 - The contractor is targeting early November to start the corridor floor grinding and polishing process.

CTE Village


- The Agriculture Science Building will have its final electrical and plumbing items placed in the walls, and it should be ready for sheetrock and plywood over the next couple of weeks.
- The Aquaculture Building is now having heating equipment installed. Plumbing and electrical work should get started over the next couple of weeks.

Site Work

- The contractors are now setting their sights on the old Aquaculture Building. Demolition of this building will begin in early November, allowing for the area to be prepared for the concrete slab where the emergency generator will be located.
3. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
 4. Below is the FHS project timeline as of August 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

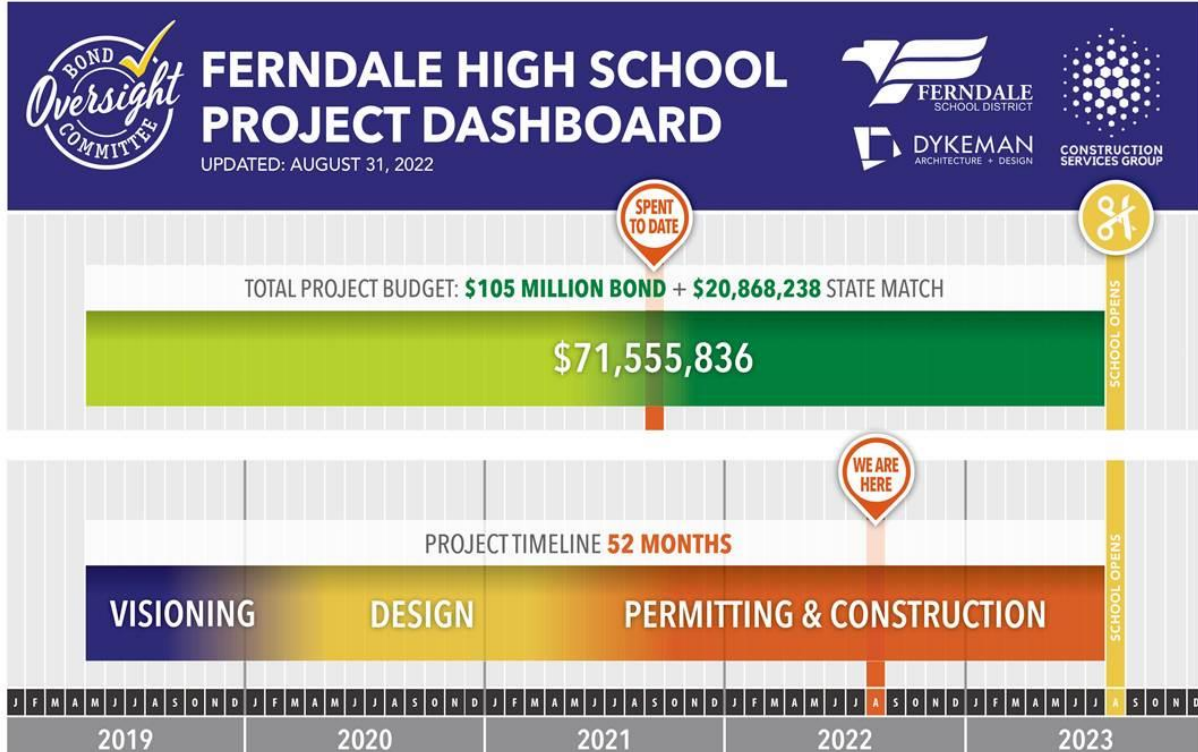

5. Below is a map showing the various components of the new FHS campus and when they'll be completed.

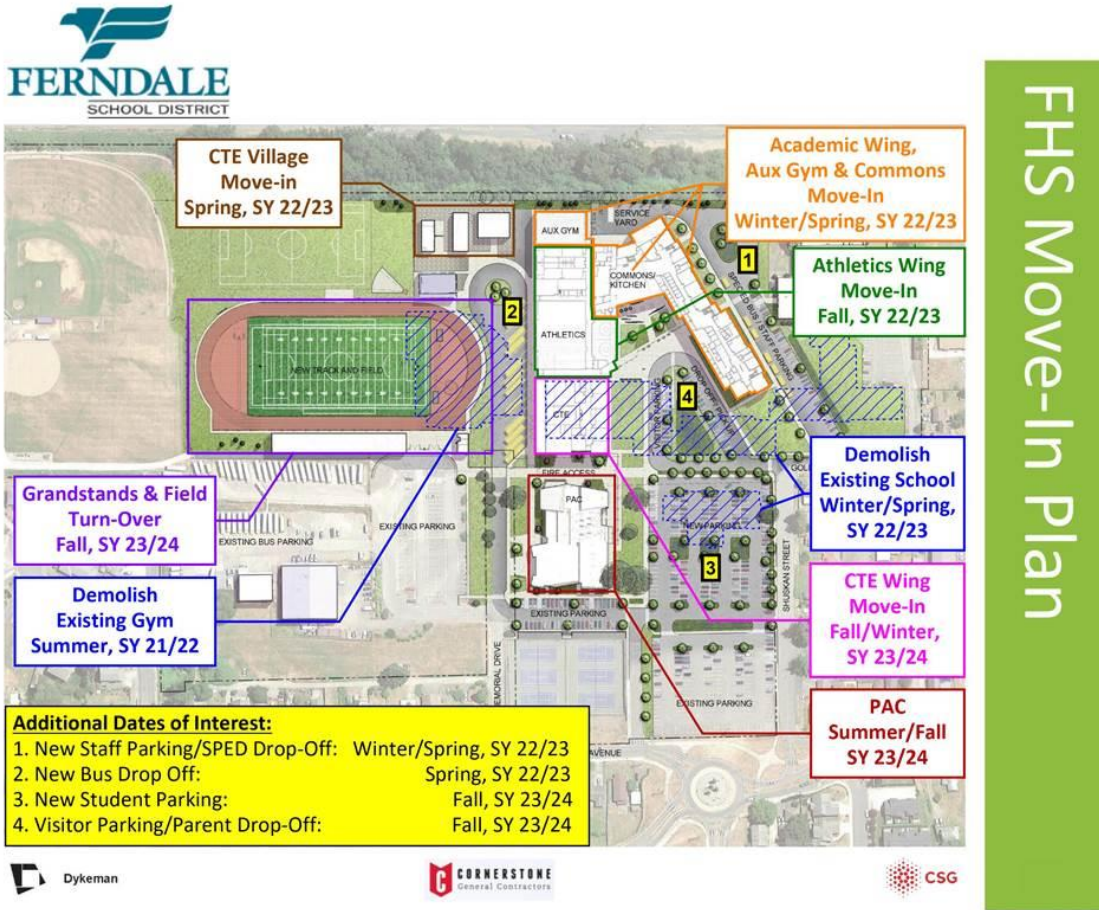

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Game lines in the Auxiliary Gym are taped out and ready for paint



The walk-in cooler in the Kitchen Area is now in place



Carpet installation in the new administrative space



Flooring installation in the staff work room



Temporary crosshatching for the ADA crossing in the parking area south of the Academic Wing
