

BOND UPDATE #180

11.4.22

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Auxiliary Gym and Kitchen

- The Auxiliary Gym has now been turned over to the high school for use, and activities are now taking place in the area. It hosted its first freshman-team volleyball game this week!
- The kitchen area is now being painted while cooking line equipment is being installed.

Academic Wing & Commons

- The first floor is now completely into the final finishes:
 - Flooring work is making good progress. The first sample classroom for teacher training has now been completed.
 - Work on the final door hardware, and door painting, is ongoing and should wrap up very soon.
 - Now that a lot of carpet has been installed on this floor, crews are installing baseboard and making good progress.
 - Final clean up on this floor should get started over the next week or so.
- The second floor is transitioning into final finishes:
 - The final ceiling tiles on this floor are now substantially complete.
 - Grinding and polishing work on the corridor floors has made good progress. Crews should be ready to move up to the third floor next week.


- Crews should begin installing carpet next week.
- The third floor is seeing the following activities:
 - Final bathroom accessories are being installed. This work should be complete in about a week.
 - Tackable wall coverings are being placed on the walls across this floor. Crews plan to be finished with this work next week.
 - Final ceiling tile installation is ongoing.

CTE Village


- Crews began installing plywood and sheetrock on the walls this week in the Agricultural Building. This work should be completed early next week.
- The Aquaculture Building is now having electrical and plumbing items installed in the wall. It's also getting ready for plywood and sheetrock the week after next.

Site Work


- The old Aquaculture Building has been demolished and hauled off-site. Contractors will now start prepping that area for the emergency generator.
2. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
 3. Below is the FHS project timeline as of August 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

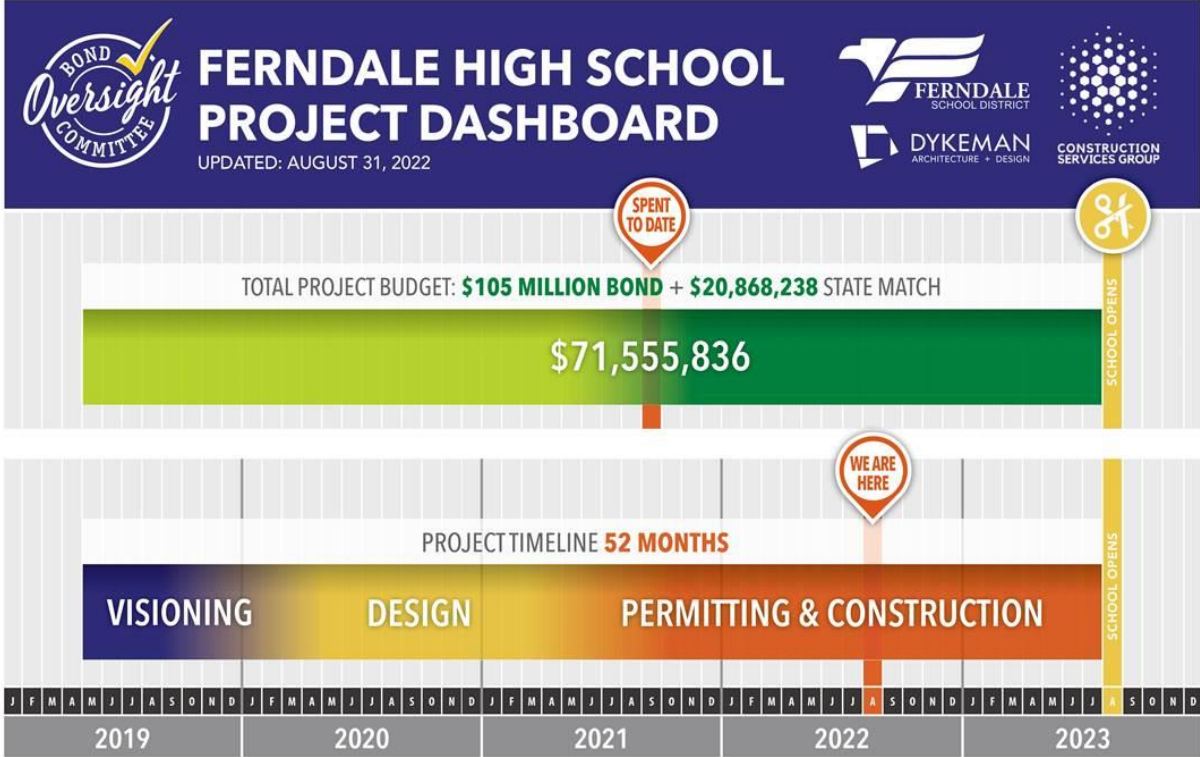

- Below is a map showing the various components of the new FHS campus and when they'll be completed.

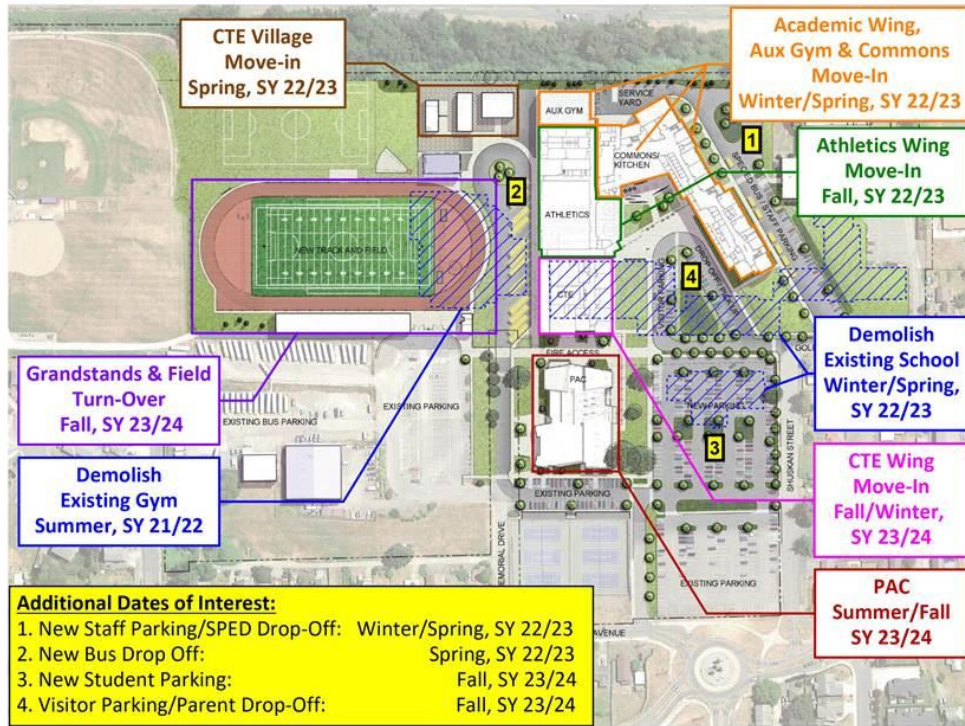

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Kitchen line equipment is being installed



Crews installing wainscoting (decorative wall panels) in Academic Wing



Finishing touches like corner guard installations are happening in the Academic Wing



Carpet being installed in one of the general education classrooms



The old Aquaculture Building is gone! Crews will now start prepping this area for the Emergency Generator.
