

John Diemer Elementary

Construction Report 10/21/2022

This Week

November 14th – November 18th

- Begin final clean in 2nd floor classrooms
- Begin Playground equipment install
- Continue flooring install throughout building
- Continue finishes install in Area A




Final clean classrooms

Next Week


November 21st – November 25th

- Begin Gym Floor finishing process
- Begin furniture install
- Continue finishes install
- Install asphalt topcoat
- Begin Continue landscaping work

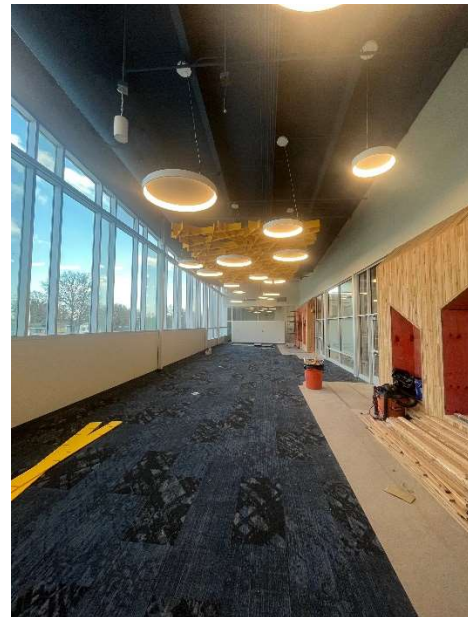


Media Center

John Diemer Elementary Construction Report 10/21/2022

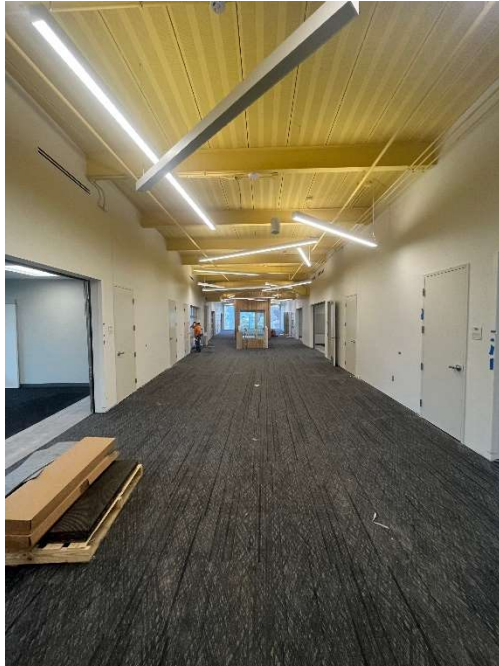

2nd floor corridor area D

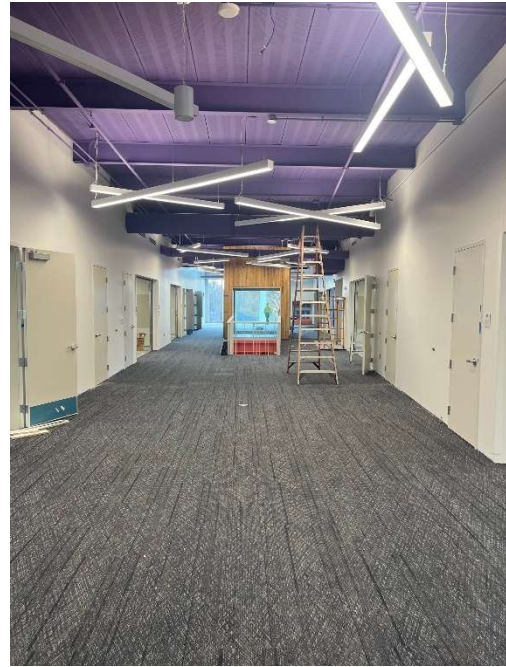

2nd floor corridor area A



Begin playground equipment install



East side exterior

John Diemer Elementary Construction Report 10/15/21

This Week

October 11th – October 15th

- Begin Footings in Area D
- Complete Storm Line in Area D



Overview of Jobsite

Next Week

October 18th – October 22nd

- Complete Footings in Area D and B
- Complete Sanitary in Area D
- Begin Sanitary and Storm in Area B



Building Pad

John Diemer Elementary Construction Report 10/15/21



Area D Footing Preparation



Footing Rebar



Area D Storm Line



North End Area D Footings

John Diemer Elementary Construction Report 10/01/21

This Week

September 27th – October 1st

- Finished Grading Around Jobsite
- Installed Electrical Underground From Power Pole to Transformer.



Overview of Jobsite

Next Week

September 20th – September 24th

- Begin Footings in Area D
- Complete Water Line and Fire Line Stub-Up's into the Building.



East Drive

John Diemer Elementary Construction Report 10/01/21



Sidewalk at NE Entrance



Test on RAP



West Drive



Building Pad

This Week

September 13th – September 17th

- Continued Site Utilities Throughout the Jobsite
- Began the Rammed Aggregate Pier Install
- Began Grading the South Parking Lot and East Drive



Overview of Jobsite

Next Week

September 20th – September 24th

- Continue Site Utilities
- Complete the Rammed Aggregate Pier Install
- Begin Grading the West Drive and Parking Lot



South Parking Lot

John Diemer Elementary Construction Report 09/17/21



East Drive



Test on RAP



RAP Install



Storm Inlet SW Corner
