

Crown Point Community School Corporation Construction Projects

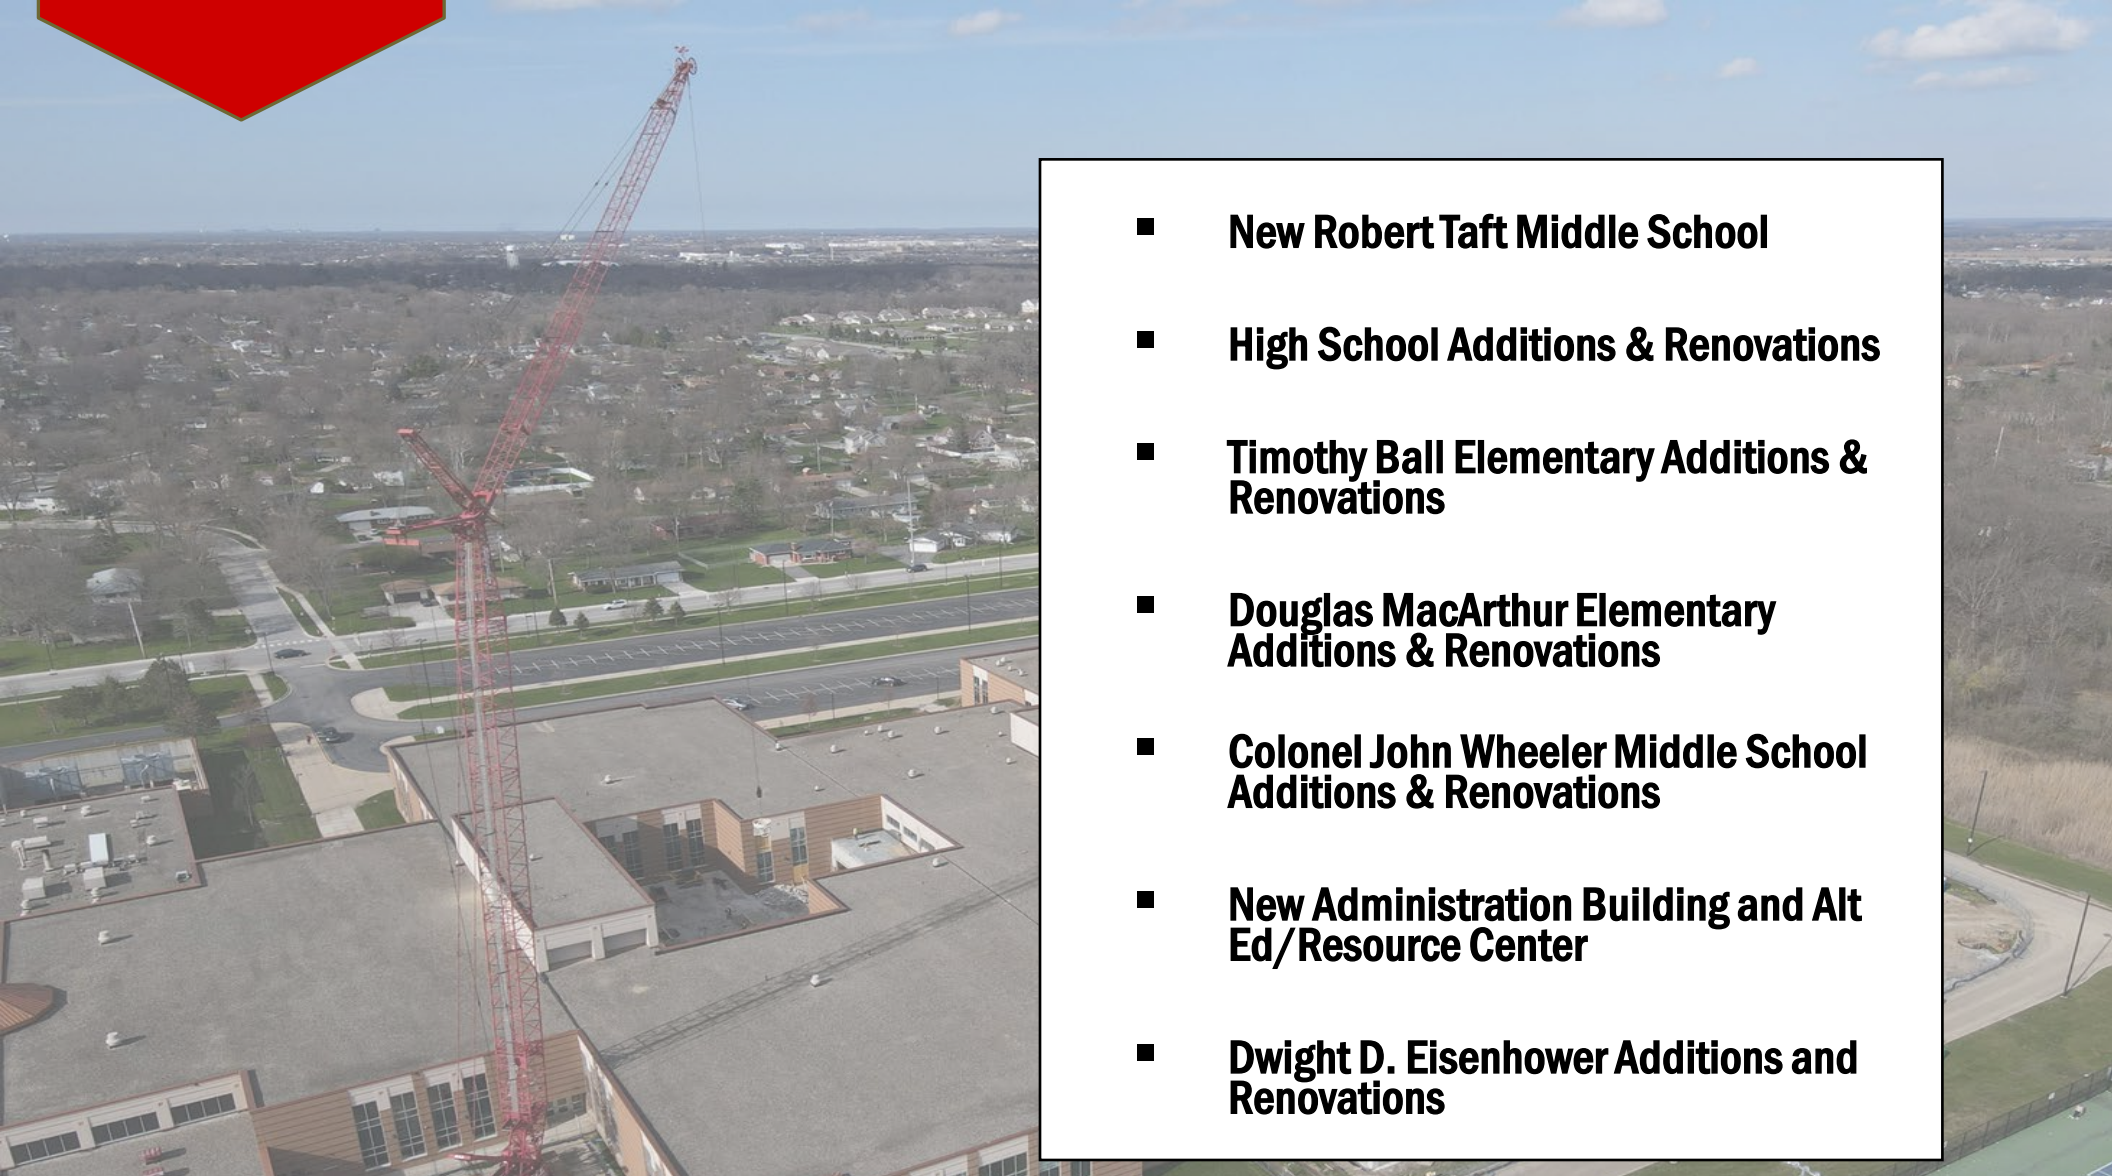
Board Report November 28, 2022



Table of Contents

Crown Point Community School Corporation Construction Projects

Board Report November 28, 2022

- 
- **New Robert Taft Middle School**
 - **High School Additions & Renovations**
 - **Timothy Ball Elementary Additions & Renovations**
 - **Douglas MacArthur Elementary Additions & Renovations**
 - **Colonel John Wheeler Middle School Additions & Renovations**
 - **New Administration Building and Alt Ed/Resource Center**
 - **Dwight D. Eisenhower Additions and Renovations**



Progress Photographs



**Auditorium and Performing Arts
CMU Walls and Facebrick**

New Robert A. Taft Middle School:

- Completed facebrick around Performing Arts and Auditorium
- Completed structural steel for Performing Arts and Main Gymnasium
- Completed installing temporary heat to building
- Completed footings and foundations for Community Building
- Continued roofing membrane
- Continued installing exterior windows
- Continued interior metal stud framing
- Began drywall in Academic wing
- Began spreading stone for turf Football Field



Progress Photographs



Academic Wing Drywall

New Robert A. Taft Middle School:

Next Four Weeks

- Complete remaining structural steel
- Complete remaining slab-on-grade concrete
- Complete all interior metal stud framing
- Complete roofing membrane
- Complete exterior facebrick
- Continue interior CMU walls
- Complete exterior window installation
- Continue installing metal panels on exterior
- Continue drywall in Academic wing
- Start drywall taping in Academic wing
- Begin painting in Academic wing
- Begin installing ceiling grid in Academic wing



Progress Photographs



High School Additions & Renovations:

- Completed interior CMU walls for classroom addition
- Completed roofing classroom addition
- Continued in wall plumbing and electrical rough-ins for classroom addition
- Continued overhead mechanical piping in classroom addition
- Continued roofing replacement of existing building
- Began ductwork in classroom addition
- Began exterior CMU walls for athletic addition

Athletic Addition Exterior CMU



Progress Photographs



Classroom Addition Roofing

High School Additions and Renovations:

Next Four Weeks

- Complete exterior CMU walls for athletic addition
- Complete in wall plumbing and electrical rough-ins for classroom addition
- Complete overhead mechanical piping in classroom addition
- Continue ductwork in classroom addition
- Continue roofing replacement of existing building
- Begin exterior CMU walls for Performing Arts addition



Progress Photographs



Timothy Ball Additions & Renovations:

- Completed roofing Pre-K and Gym additions
- Poured slab-on-grade in Gym addition
- Completed exterior framing in Kindergarten addition
- Completed drywall and tape in classroom addition
- Continued facebrick on Pre-K addition
- Began roofing Kindergarten addition
- Began installing ceiling grid in classroom addition

Kindergarten and Gym Addition Roofing



Progress Photographs



Pre-K Addition Exterior Walls

Timothy Ball Additions and Renovations:

Next Four Weeks

- Complete interior framing in Pre-K addition
- Complete exterior facebrick on Pre-K addition
- Complete roofing on Kindergarten addition
- Continue above ceiling mechanical piping in Pre-K addition
- Continue in wall plumbing and electrical rough-ins in Kindergarten addition
- Begin drywall and taping in Pre-K wing
- Begin painting in Gym addition
- Begin exterior facebrick on Kindergarten addition



Progress Photographs



Douglas MacArthur Additions & Renovations:

- Completed load bearing CMU walls for Gymnasium addition
- Completed exterior metal stud framing of classroom addition
- Completed setting trusses for classroom addition
- Completed setting steel joists and decking for Gym addition
- Continued electrical and plumbing rough-ins at classroom addition
- Began roofing Gym addition
- Began decking classroom addition

Classroom Addition Roof Trusses and Decking



Progress Photographs



Gymnasium Addition CMU Walls

Douglas MacArthur Additions and Renovations:

Next Four Weeks

- Complete roofing on Gym addition
- Complete decking and roofing on classroom addition
- Complete structural steel on Admin/Entrance
- Pour slab-on-grade for Gym addition
- Continue interior wall framing in classroom addition
- Begin exterior facebrick on Gym addition
- Begin exterior facebrick on classroom addition



Progress Photographs



Auditorium Addition Structural Steel

John Wheeler Additions & Renovations:

- Completed Phase 1 of erecting structural steel for Auditorium addition
- Continued exterior CMU walls for Auditorium addition
- Began erecting structural steel for classroom addition
- Began exterior CMU walls for classroom addition



Progress Photographs



Classroom Addition Footings

John Wheeler Additions and Renovations:

Next Four Weeks

- Complete erecting structural steel for Auditorium and classroom additions
- Complete exterior CMU walls for Auditorium and classroom additions
- Pour slab-on-grade for Auditorium addition
- Pour slab-on-grade and slab-on-deck for classroom addition
- Continue ductwork in boiler room
- Begin roofing Auditorium and classroom additions



Progress Photographs



New Administration Building and Alt Ed/Resource Center:

- Completed detailing structural steel
- Began pouring slab-on-grade
- Began exterior framing and sheeting
- Began installing temporary lights

New Administration Center Exterior Framing



Progress Photographs



New Administration Building and Alt Ed/Resource Center :

Next Four Weeks

- Complete pouring slab-on-grade
- Pour slab-on-deck
- Complete exterior metal stud framing
- Begin setting cold formed metal trusses
- Begin roofing low-roof area
- Begin exterior facebrick
- Begin interior metal stud framing
- Begin in wall plumbing and electrical rough-ins

New Administration Front Entrance



Progress Photographs



Dwight D. Eisenhower Elementary School Additions and Renovations :

- Completed site demolition
- Began site utilities
- Began grading for building pad
- Began digging and forming footings

Eisenhower Sitework



Progress Photographs



Dwight D. Eisenhower Elementary School **Additions and Renovations:**

Next Four Weeks

- Complete site utilities
- Complete excavation for footings
- Complete pouring footings
- Begin CMU foundations
- Begin grading for slab-on-grade

Classroom Addition Footings
