



Projects Update September 26, 2022

BHISD Bond Projects: Transportation Center Renovations; HS Additions; LSC Hall of Honor Update; Action Item – LSC Change Order #05



New Fuel Station and Building Renovations





cre₈

New Fuel Station and Building Renovations



Site Plan – Becky Nelson Transportation Center



cre₈



cre₈

Fueling Station – Canopy Near Completion – Underground Piping , Paving, Setting Tanks & Equipment to Follow





cre R Fueling Station – Canopy Complete– Underground Piping Complete, Paving, Setting Tanks & Equipment to Follow





Cre R Installed Diesel-Unleaded fuel tank on concrete base. Rebar for Propane tank is ready for concrete.





cre R Installed Diesel-Unleaded fuel tank on concrete base. Concrete paving now complete.







Propane piping utility trench ready for concrete.






cre₈

Fueling Station – Canopy Complete – All Concrete Now Complete for Piping Trenches and Drives



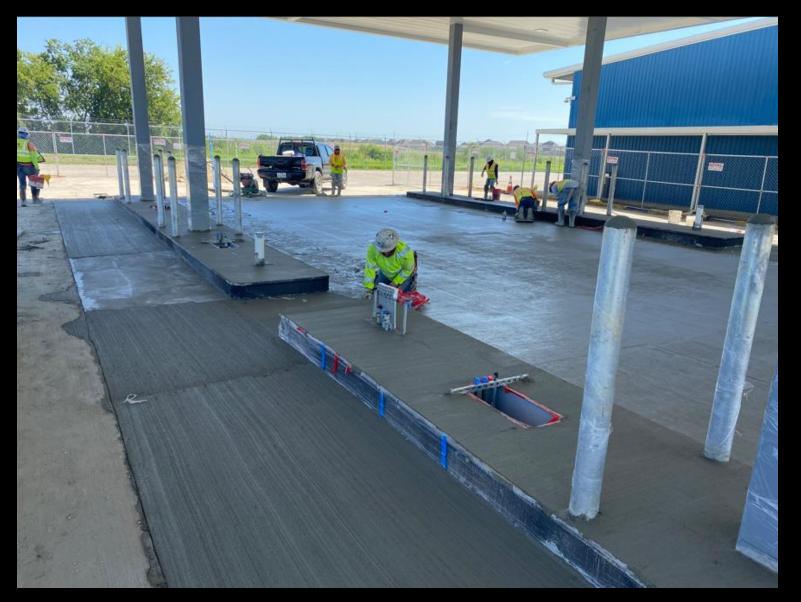

cre₈

Fueling Station – Canopy Complete – All Concrete Now Complete





cre₈

Fueling Station – Paving complete. Propane tank to be set soon, then dispensers ready to be set.





cre₈

Fueling Station – Ready for fuel dispensers to arrive this week.





cre₈

Building Renovations: Batt insulation installed. Working on hanging electrical conduit, ductwork straps and j-boxes.






Building Renovations: Ready for concrete pour.

cre₈



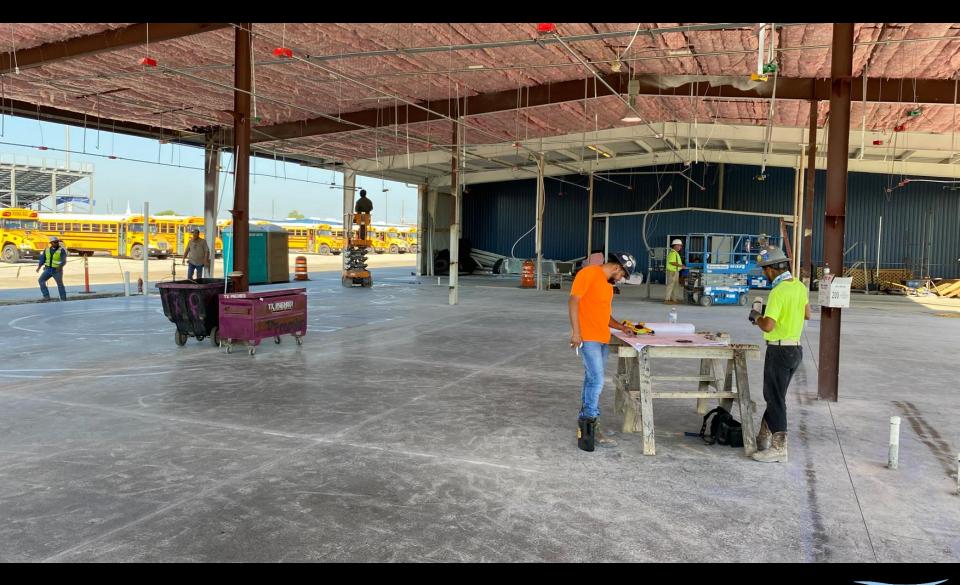


cre₈

Building Renovations: New concrete is poured; Electrical conduit installation in progress, HVAC ductwork installation this week.



BOND 2020: HS Additions and Parking Update

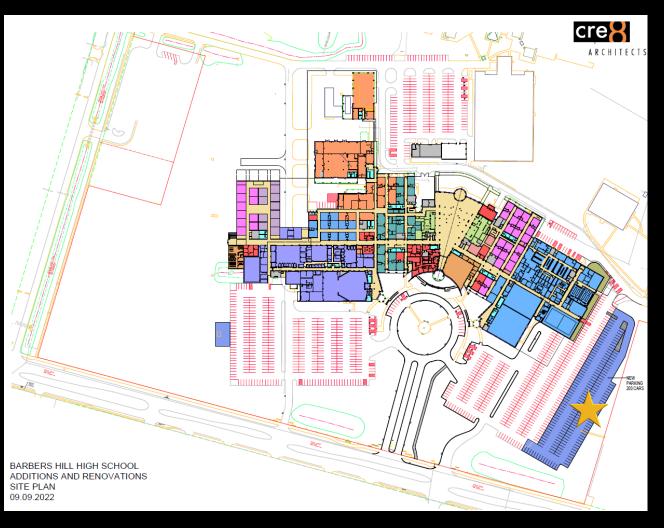

Early Release Package 1 Parking Addition:


- <u>9/23 Issue Drawings &</u> <u>Specifications to PCI;</u>
- 1st Advertisement;
- 2nd Advertisement;
- <u>10/11 Receive sub</u> <u>contractor bids;</u>
- 10/13 Review GMP with District;
- <u>10/24 Present for</u> <u>Board approval</u>

PROJECTED START DATE: 10/25/22 COMPLETION DATE: 02/17/23

Cre HS Building Addition: Conceptual Design is out for price estimate by PCI; Preparing to receive bids for parking lot addition next month.



BOND 2017: Hall of Honor Update - LSC

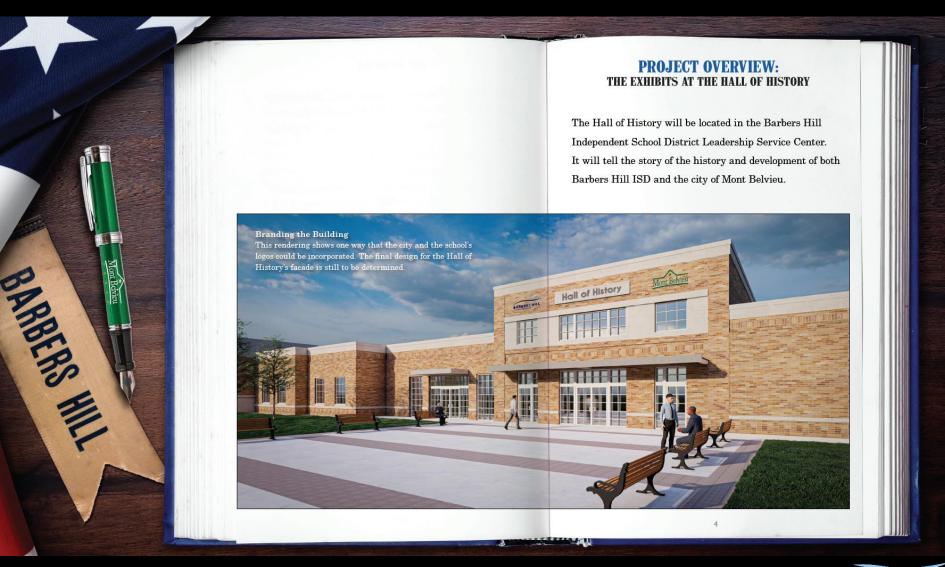



BOND 2017: Hall of Honor Update - LSC







Display installation in progress – artifacts will be placed once all of display cases are completely fabricated and installed.



THANK YOU

