

BOND UPDATE #188


1.20.23

Please note that I am resending this as the link in the last update wasn't connecting. How fortunate it is that it's an easy fix and I can send the email update again.


Here's what is going on with our bond projects.

Enjoy!
Kristi

1. The Bond Oversight Committee will hold their next meeting on Tuesday, January 24 at the Vista Middle School library. Topics of discussion will include an update on the artwork committee and a review of bond-related spending.
2. Finishing touches in the new Academic Wing are still ongoing, and should be finished by mid-February.
3. Hazardous materials are still being removed in the old building. It is scheduled to begin demolition this Monday.
4. Crews are still working on shaping the concrete around the football field. They're continuing to check off items that need to be done so the astroturf can be installed this summer. Framing work on the grandstands' concessions and restrooms continues, and exterior sheetrock installation began this week.
5. The Agricultural and Aquaculture buildings are nearly finished. They're scheduled to be used by January 30!
6. One item that's been affected by recent supply chain issues has been glass. The glass that is part of the stairwell guardrails has been on back order, but has now begun arriving. Crews are installing glass now as deliveries continue, and this process should be completed over the next couple weeks.
7. The long-awaited plexiglass panels for the greenhouse will arrive on Monday, and crews will begin installation then. This makes us one step closer to completing that building.
8. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://www.ferndalesd.org/Bond-2019)
9. Below is the FHS project timeline as of October 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

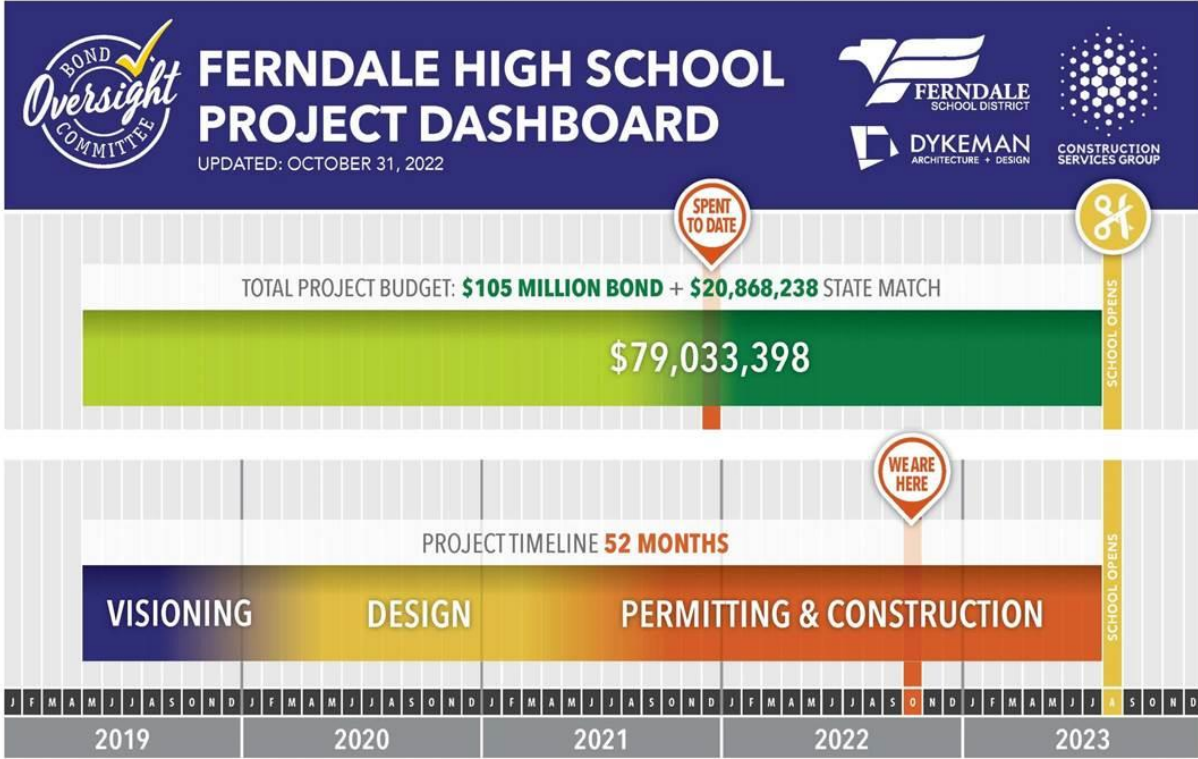

10. Below is a map showing the various components of the new FHS campus and when they'll be completed.

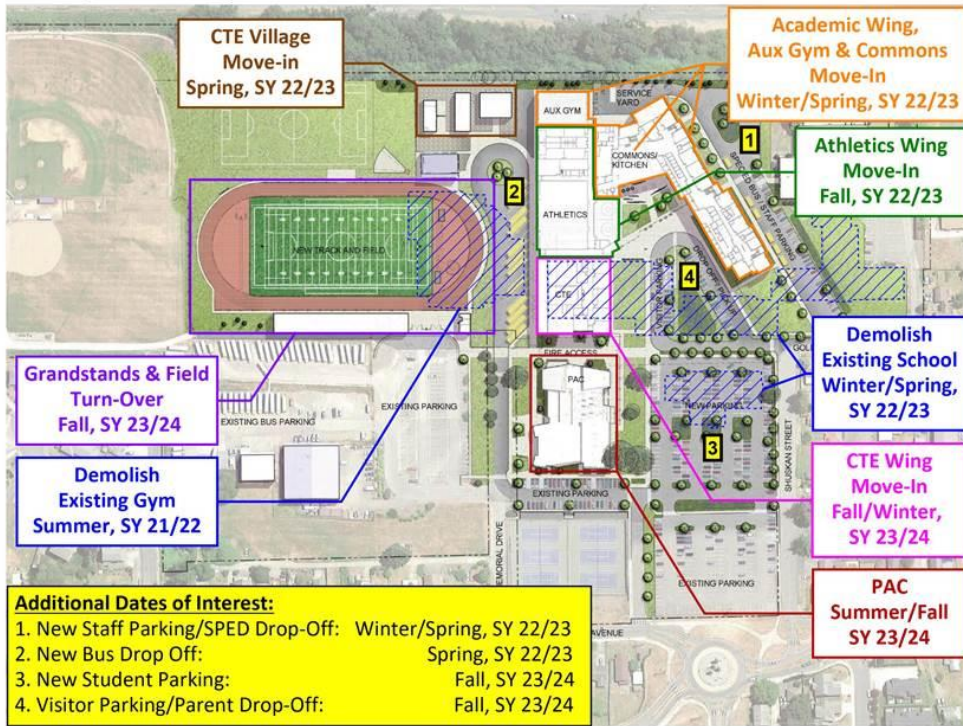

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Finishing touches in the Aquaculture Building



Ramp foundation between the weight room and new football field



Installation of the foundation that will support the ramp leading up to the grandstands



Exterior sheetrock being installed on the grandstands' concession area



Crews installing the glass guardrail panels at the Academic Wing central staircase
