


BOND UPDATE #189

1.27.23


Here's what is going on with our bond projects.

Enjoy!
Kristi


1. The Bond Oversight Committee met Tuesday. Topics of discussion included the new Academic Wing, an update on the artwork committee, and the demolition of the old FHS building.
2. The Ferndale School Board will receive an update on bond-funded projects at their upcoming regular meeting next Tuesday at Mountain View.
3. Finishing touches in the new Academic Wing, such as woodworking, are still ongoing in the evenings. This work should wrap up over the next couple of weeks.
4. The final building system commissioning will begin on February 13. Once this final check is complete, the contractor will make any needed corrections that are noted.
5. Crews are still working on shaping the concrete around the football field. The retaining wall around the long-jump area is now complete and has been backfilled with soil.
6. Hazardous material removal from the north end of the old FHS building is complete. This has allowed the contractor to pull down that portion of the building this week. Materials are still being removed from the rest of the old FHS building, and full demolition should begin on the week of Feb. 13.
7. The Agricultural and Aquaculture buildings received their final fire inspection earlier this week and will be turned over to the high school for use next Tuesday.
8. Crews continued to work on the grandstands' concessions and restrooms this week. Framing and sheetrock tasks are finished, and the area is now being worked on by plumbers and electricians.
9. Glass guardrail installation in the Academic Wing is ongoing and should be completed over the next three weeks.
10. The plexiglass panels for the greenhouse arrived this week and installation has begun.
11. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
12. Below is the FHS project timeline as of January 20. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

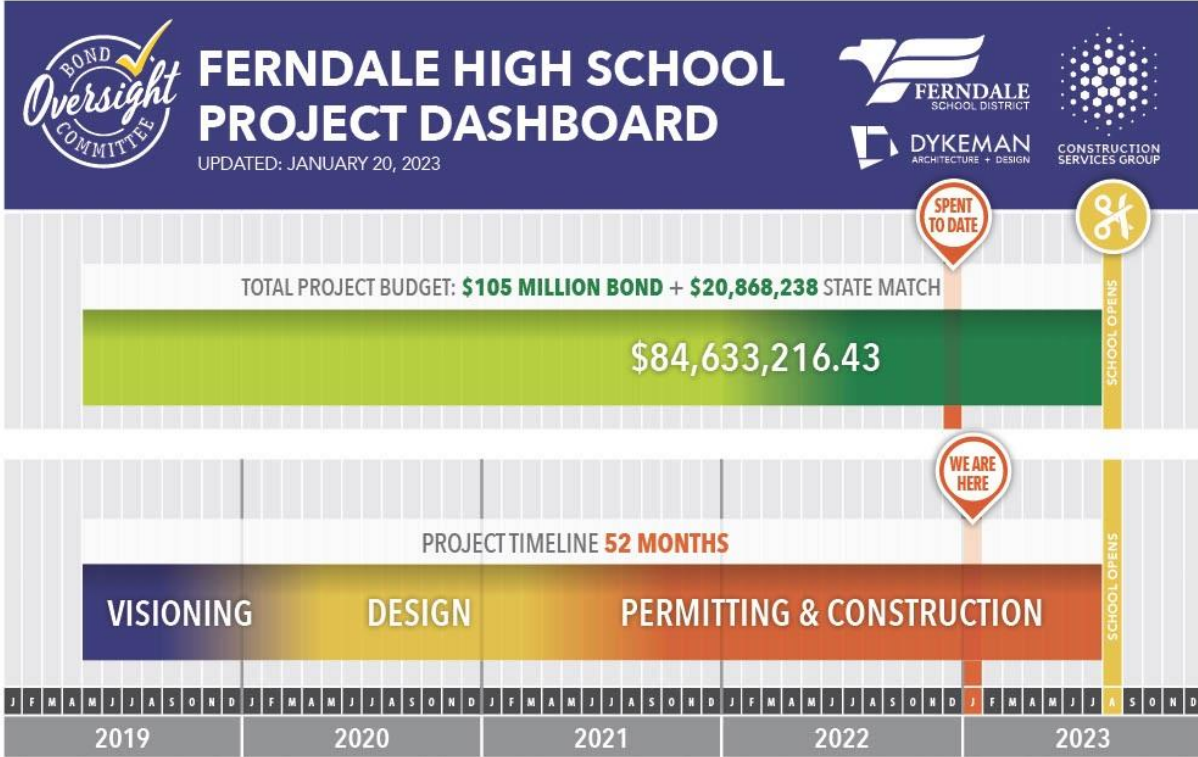

13. Below is a map showing the various components of the new FHS campus and when they'll be completed.

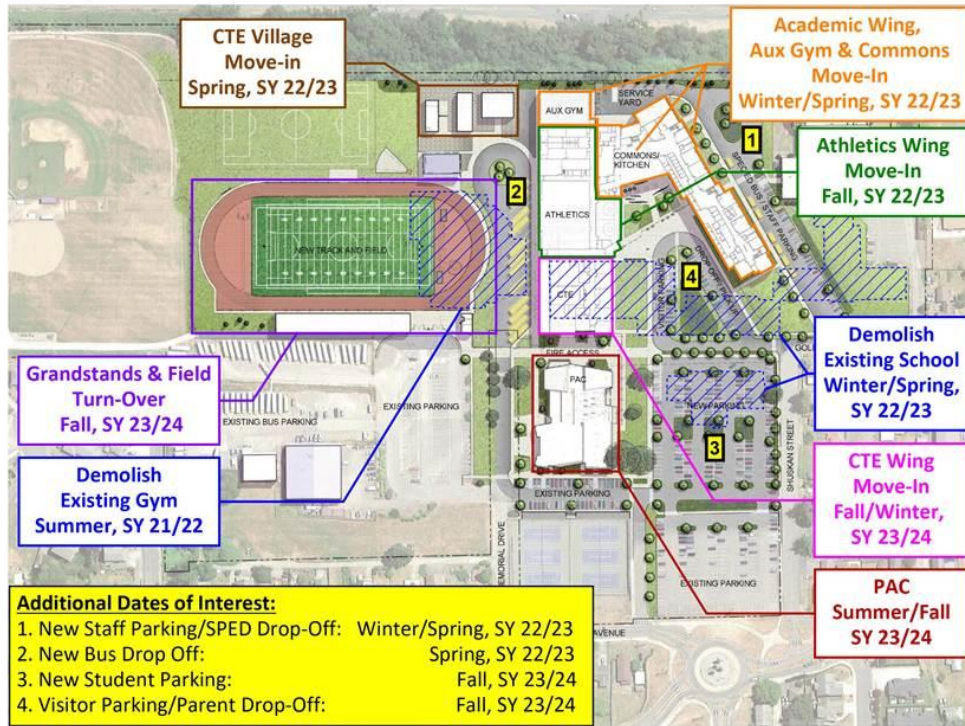

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Backfill at the retaining wall next to the long jump area



Track curb ongoing installation



The concession area under the football field grandstands has now had framing and exterior sheetrock completed



The north end of the old FHS is gone – this will allow construction of the CTE Wing to begin



Greenhouse plexiglass panel installation is now underway
