


BOND UPDATE #190

2.3.23


Here's what is going on with our bond projects. It is such an exciting time!

Enjoy!
Kristi


1. The Ferndale School Board heard an update on bond-related projects at their regular meeting Tuesday. Topics of discussion included students' and staff's reactions to the new Academic Wing, the smooth transition to the new building and the demolition of the old FHS building.
2. The materials are now available for the final corridor ceilings around the gym. Contractors are finalizing an installation schedule, and soon those areas will be finished.
3. The reclaimed wood flooring from the old gym has now been installed around the display cases outside the new gym.
4. The final building system commissioning will begin on February 13. Once this final check is complete, the contractor will make any needed corrections that are noted.
5. The gravel needed for the football field turf this summer has now been fully poured and set.
6. Hazardous material has been removed from most of the old FHS building; crews are currently removing material from the final portion, Old Main. This work will likely be completed over the next week.
7. Much of the old school has now been demolished. Crews will begin demolishing Old Main on the week of Feb. 13.
8. The Agricultural and Aquaculture buildings have now been turned over to the school for use. Ag Science classes are already working on plans on how to decorate and use the building.
9. Plumbing is being installed in the interior of the grandstands' concessions and restrooms, while crews are preparing for masonry to begin on the exterior.
10. Glass guardrail installation in the Academic Wing is ongoing and should be completed over the next couple weeks.
11. Crews are still installing plexiglass panels on the Greenhouse. This work should be finished over the next week.
12. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
13. Below is the FHS project timeline as of January 20. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

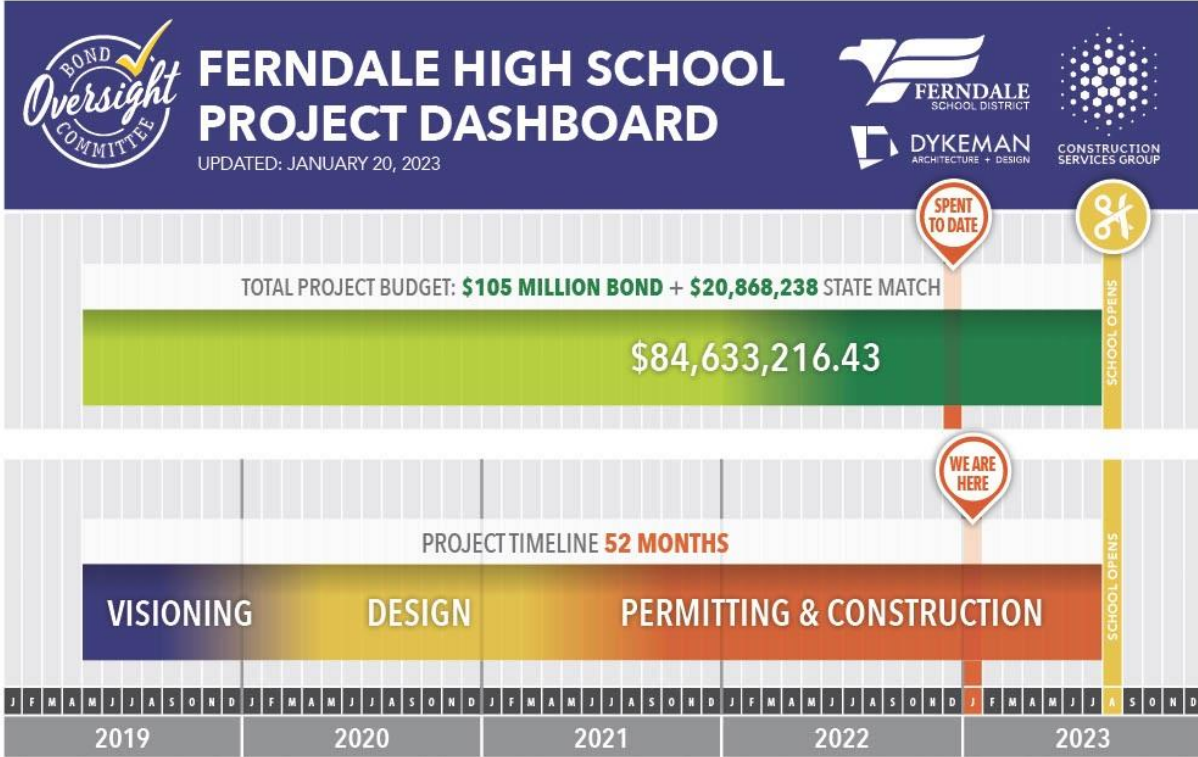

14. Below is a map showing the various components of the new FHS campus and when they'll be completed.

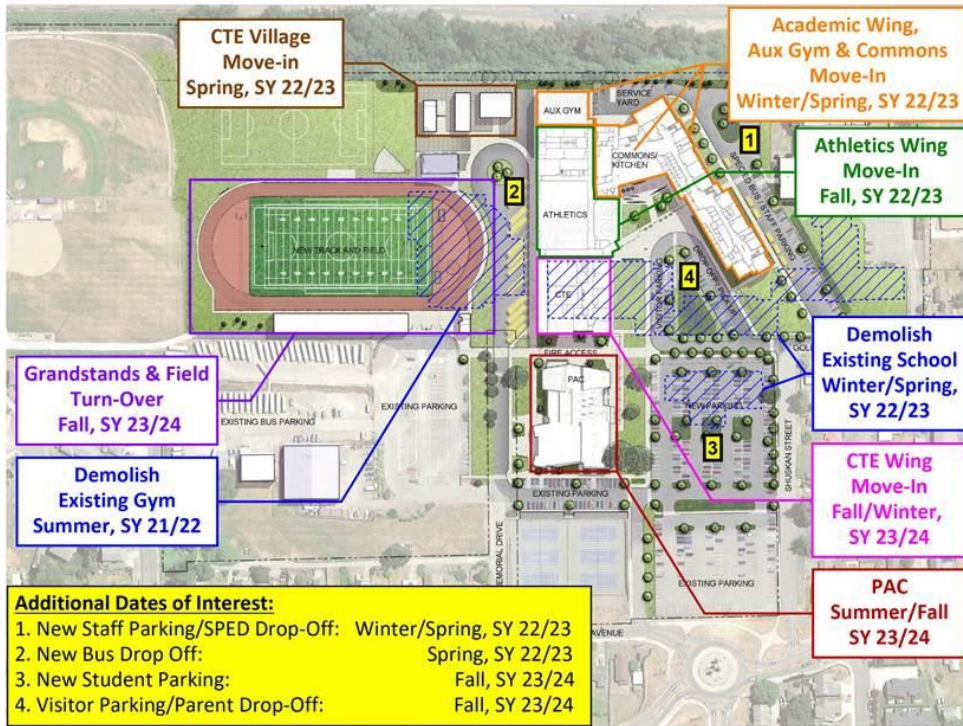

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Reclaimed flooring from the old gym installed around Athletic Wing display case



Final gravel being installed on the football field



Agriculture Science classroom is ready!



Plumbing being installed in the Grandstand bathrooms



Exterior work around the Grandstand concessions area



Greenhouse plexiglass panels being installed
