


BOND UPDATE #191

2.10.23



Here's what is going on with our bond projects. It is such an exciting time!

Enjoy!
Kristi

1. Final ceiling installation work in the corridors around the Main Gym is now scheduled for spring break while the students are away.
2. Glass guardrail installation is ongoing in the new main building and is very close to completion.
3. Soon, crews will start assembling the covered walkway between the main entrance and the Athletic Wing. Eventually, a decorative fence will be installed under the canopy, which will form the secured perimeter around the Commons' courtyard.
4. Crews have now built up the pad that the new CTE Wing will sit on with structural sand & gravel. This prepares the area for geopier installation to begin next week, which will stabilize the foundation.
5. Crews continued working on the Grandstands' concessions & restrooms, and roofing work has now started. Masonry work likely will get rolling next week.
6. The plexiglass for the Greenhouse is now completely installed!
7. Hazardous material from the old cafeteria was removed and the structure was demolished this week. By next week, it will be completely gone. Hazardous material continues to be removed in Old Main, and this work likely will run through most of next week. Tentatively, Old Main will be demolished the week of the 20th.
8. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://www.ferndalesd.org/bond-2019)
9. Below is the FHS project timeline as of January 20. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

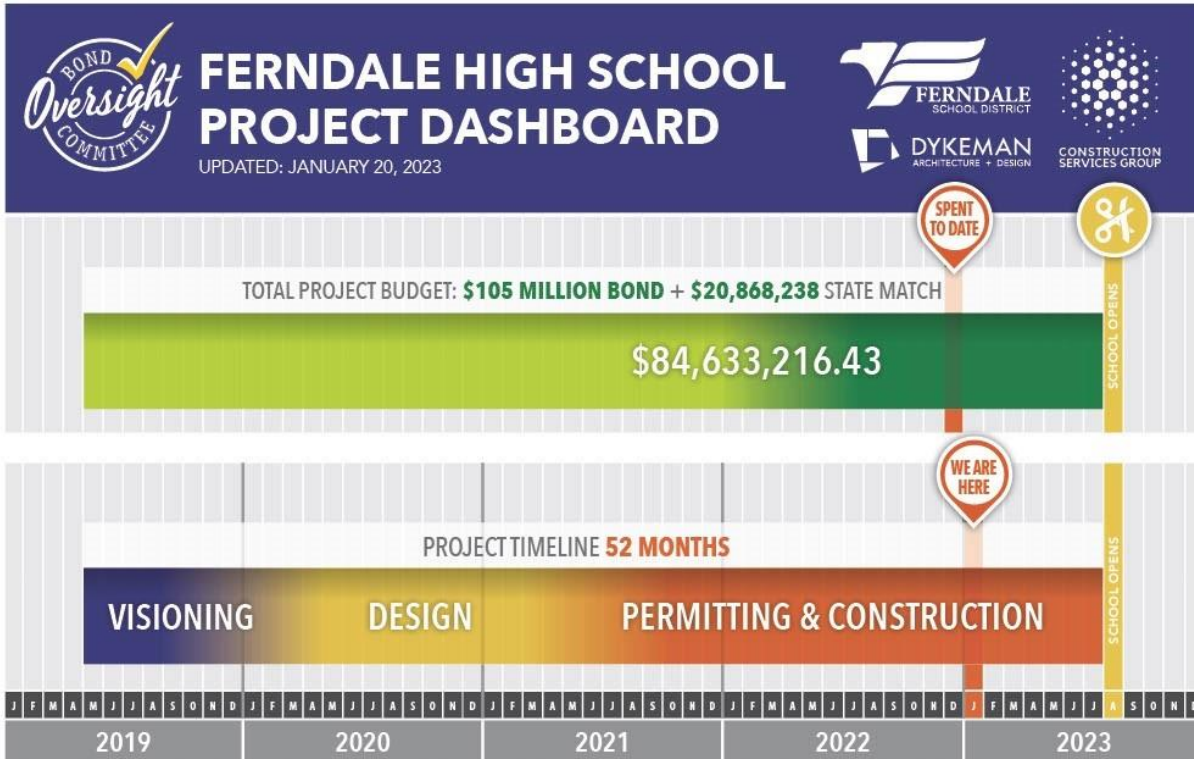

10. Below is a map showing the various components of the new FHS campus and when they'll be completed.

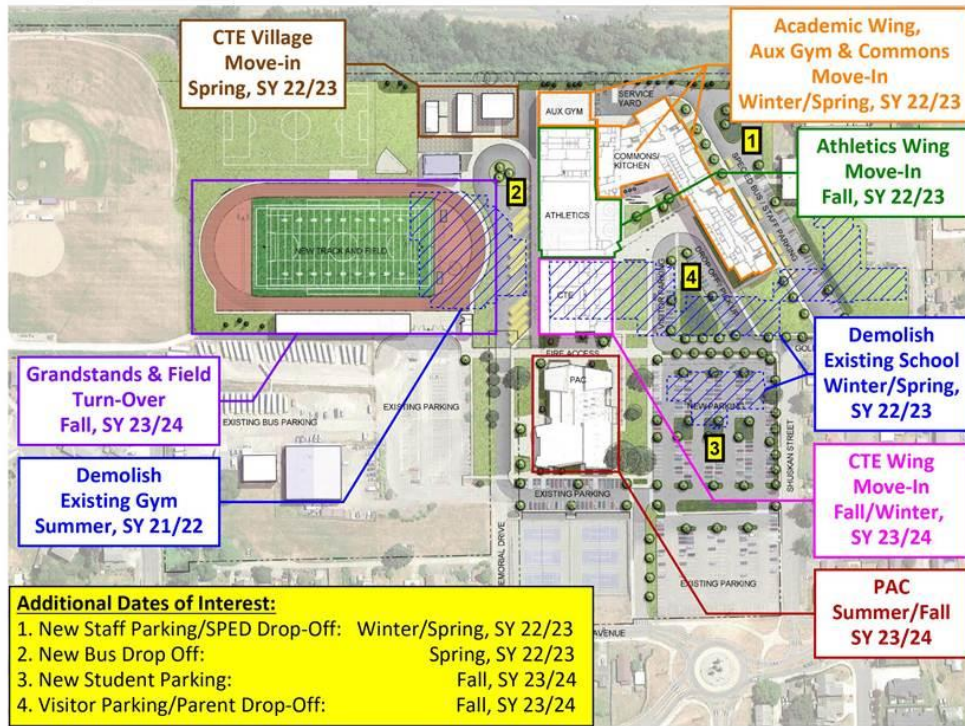

FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



The concrete barrier between the track and the Grandstands is now installed



Much of the old FHS building is now demolished




Now that the old building is gone, crews are preparing the pad for the CTE Wing



The old cafeteria is almost gone – this will allow site work to begin in that area



The new plexiglass on the Greenhouse has been installed

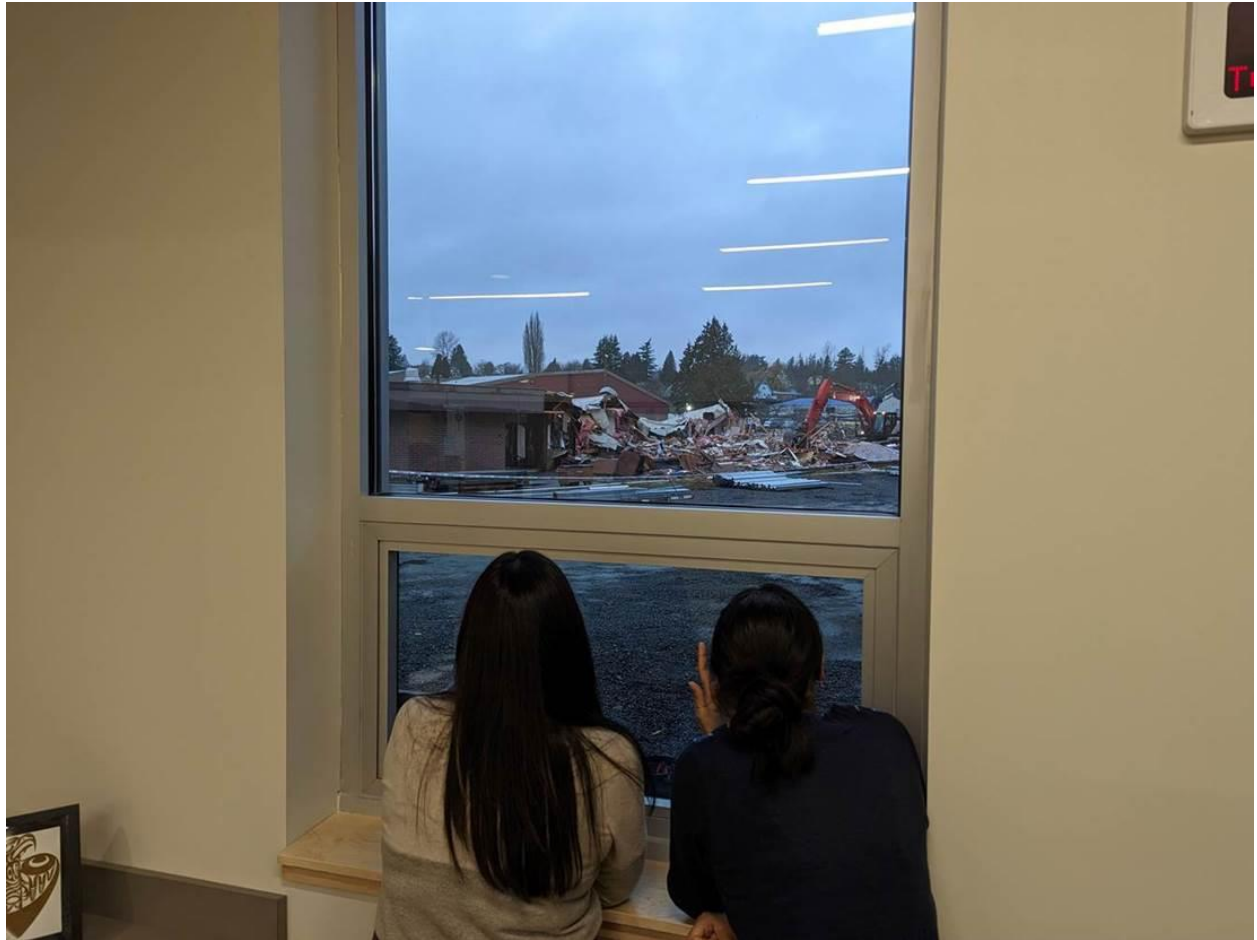

FHS students get a front-row seat to the old building's demolition
