


BOND UPDATE #193

2.24.23


Here's what is going on with our bond projects.

Enjoy!
Kristi

1. This week, the Ferndale High Artwork Selection Committee led local curator Tami Landis on a tour of the new FHS building, to determine where artwork could be placed. In the spring, Landis will return with recommendations for artwork, and the Committee will decide which pieces will be added.
2. Much of the concrete work between the football field and the weight room area is almost complete! That area is now being prepared for crews to pour the sidewalks.
3. Crews are almost finished assembling the framework for the courtyard's covered walkway, which will connect the Academic Wing's main entry to the Athletic and CTE wings. Next, crews will install decking in preparation for roofing.
4. Geopier installation beneath the foundation of the new CTE Wing continues this week. This work should be nearly complete in about a week.
5. Roofing work is ongoing on the concessions and restrooms underneath the Grandstands.
6. Crews are now installing ventilation equipment and piping in the new Greenhouse.
7. The hazardous material removal process at Old Main was completed yesterday. Crews will begin pulling down the building today or Monday.
8. The Ferndale School Board will receive an update on bond-related projects at their next regular meeting on Tuesday, February 28 at Mountain View.
9. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://www.ferndalesd.org/Bond-2019)
10. Below is the FHS project timeline as of January 20. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

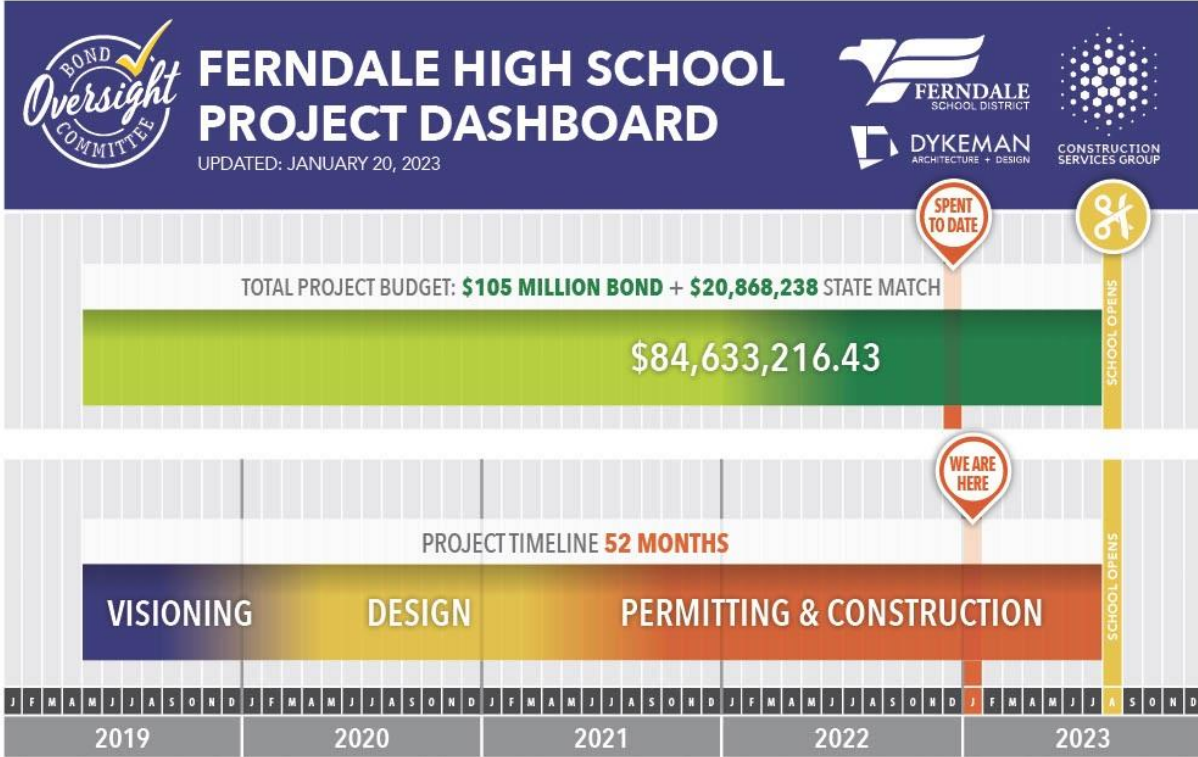

11. Below is a map showing the various components of the new FHS campus and when they'll be completed.

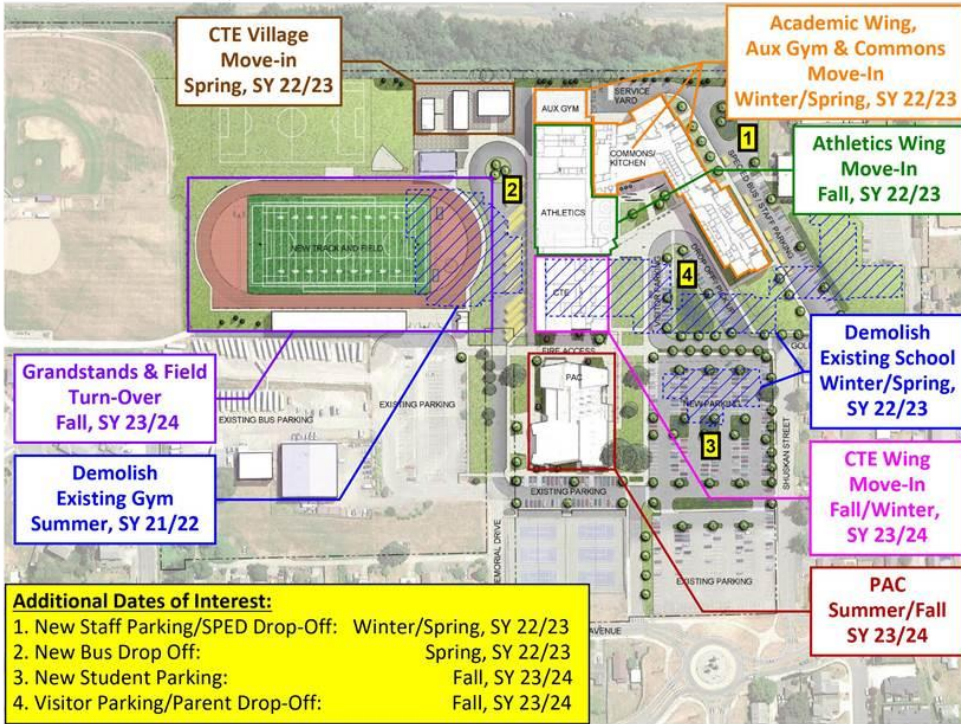

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



The wall separating the weight room from the track is now complete




The framework of the canopy between the main entrance and the Athletic/CTE wings is almost complete and ready for decking



Bench and table installation in the common area courtyard



Geopier installation at the CTE Wing site

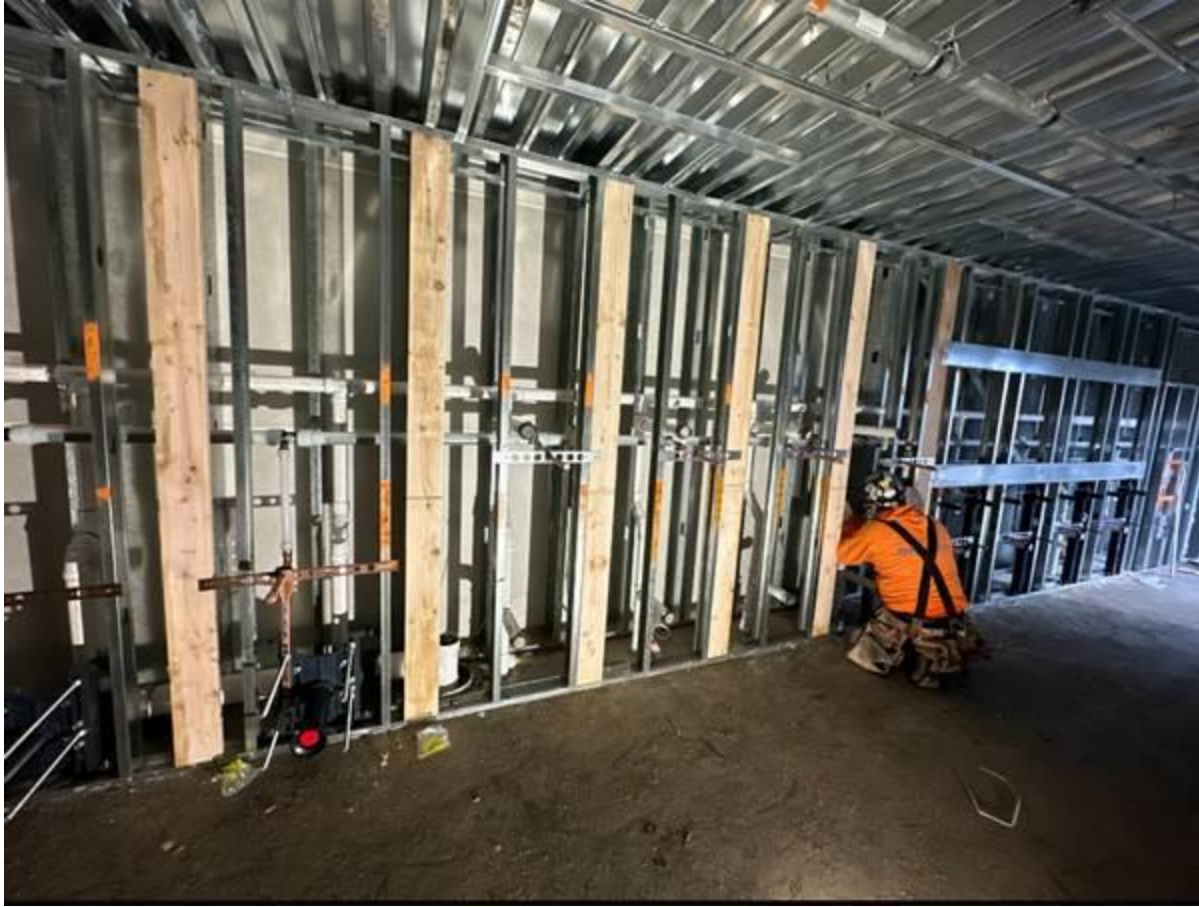

Backing for bathroom stall partitions being installed in the Grandstand



Fire sprinkler piping in the Grandstands' restrooms/concessions area
