



Little Elm ISD
BOND
2017

Bond Committee Meeting
January 23, 2019, 6:00 PM
Zellars Center for Leadership and Learning



Bond Committee Agenda

- Introductions – Rod Reeves
- Committee Objectives
- Instructional Design Update – Dr. Cyndy Mika
- Jerry R. Walker & Lowell H. Strike Middle School Update - Rick Martin
- High School Athletic Field Replacements – Rick Martin
- Roof Replacements – Rick Martin
- Athletic Complex Scoreboard Replacements – Rick Martin
- Future Planning Discussions – Rick Martin
- Questions and Answers



Bond Committee Objectives

- **Ensure transparency between LEISD Leadership and Community Members:**
 - Bond Planning
 - Bond Financials
 - Construction Updates
- **Obtain feedback from the Community**
 - Bond Planning
 - Bond Financials
 - Construction Updates



Instructional Design Update





Instructional Design Update





Instructional Design Update





Instructional Design Update



BOND CONSTRUCTION PROGRAM UPDATE



January 23, 2019



Program Milestones

FUNDING

Phase I Sale – May 2018	\$150 Million
Phase IB Sale – August 2018	\$ 25 Million
Phase II Sale – May 2020	\$48.5 Million (estimated)
Phase III Sale– May 2022	<u>\$ 11.5 Million (estimated)</u>
Total Program	\$ 235 Million



Jerry R. Walker Middle School

- Completed Plans in November 2018
- Board approved Budget (\$68,538,650) & Balfour Beatty GMP (\$56,130,622) in December 2018
- Issued the NTP January 3, 2019
- Conducted the PreCon Conference on January 16, 2019



You're invited to a groundbreaking event!

Please join us as we break ground for
JERRY R. WALKER MIDDLE SCHOOL



Monday, February 4 at 9:00 a.m.



Lowell H. Strike Middle School

- Completed Plans in November 2018
- Board approved Budget (\$67,513,977) & Cadence McShane GMP (\$56,189,819) in December 2018
- Issued the NTP December 27, 2018
- Conducted the PreCon Conference on January 16, 2019



You're invited to a groundbreaking event!

Please join us as we break ground for
LOWELL H. STRIKE MIDDLE SCHOOL

Monday, February 4 at 10:30 a.m.





High School Athletic Fields


- Board approved budget (\$8,480,300) to replace the football field & track, softball field, baseball field, & other improvements to this area of the campus in October of 2018
- Issued NTP November 15, 2018
- Work will progress as required to accommodate sports schedules, starting with the football field and track areas currently under construction
- Design work on a new concourse and concessions stand will continue with construction expected to take place this Summer





Roof Replacements


- Board approved \$2,136,720, for roof replacements @Brent, Chavez and Zellars at the December 2018 Board meeting
- Work is expected to begin as soon as classes are dismissed this Spring
- NTP's will be issued in time to secure materials to start installations in June

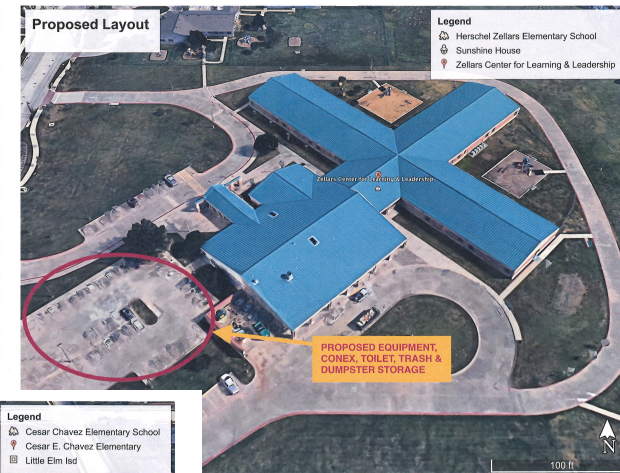



Athletic Complex Scoreboards

- Board approved \$1,007,346 to replace the scoreboards and time clocks at the November 2018 Board Meeting
- NTP was issued December 10, 2018
- Signs are being manufactured and are scheduled to be installed in March of 2019

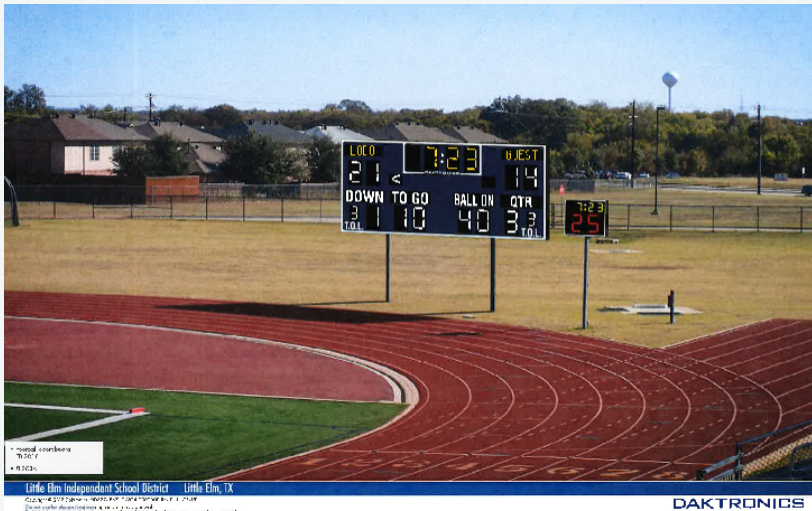

- Overall Dimensions
30'4.0" Tall x 31'6.4" Wide
- 2000HD Series Sound System
- Optional: Freeform Lighting Elements
- Logo Display @ @
- 15HD Video Display
480 lines of resolution x
624 columns of resolution
Active Area: 24' x 31'2"
- Opt- 15HD Video Display
950 lines of resolution x
728 columns of resolution
Active Area: 24' x 31'2"

Little Elm Independent School District Little Elm, TX

Do not use for design/engineering or ad copy approval.
The details and expressions shown are conceptual in nature, confidential and proprietary. Final design and appearance may differ from artwork shown.
Do not reproduce by any means without the expressed written consent of Daktronics, Inc.

DAKTRONICS



Future Planning Discussions

Remaining Phase IB projects in the Planning Stages include:

- LEHS CTE area renovations/upgrades
- Additional land purchase/exchange
- 12 new busses
- Misc. Stadium Complex improvements
- Misc. Safety & Security improvements
- Misc. HVAC equipment replacements
- Misc. Technology Improvements



Future Meeting Dates

- **Wednesday, May 29, 2019 – 6:00 p.m. Zellars Center For Learning & Leadership**
- **Wednesday, September 18, 2019 – 6:00 p.m. Zellars Center for Learning & Leadership**



Upcoming Events

- **Jerry R. Walker Middle School Ground Breaking –**
Monday, February 4, 2019 – 9:00 a.m. 633 French Settlement
- **Lowell H. Strike Middle School Ground Breaking –**
Monday, February 4, 2019 – 10:30 a.m. Construction site off of Lebanon Road

Please visit our Construction Website:

littleelmisd.net – Support Services – Construction Services

