



Del Valle ISD Bond Project Updates for Feb 2023

Smith Elementary Opened August 2022



Smith Elementary Updates

- Final facility review and inspections are underway for warranty service
- All parking lots are complete
- Door hardware and added door installation scheduled for Spring 2023
- Access control programming and camera installation is ongoing
- Graphics are being completed for all areas of the campus
- Grounds and site work continues around the campus





Smith ES front parking, back parking, and the playground areas are complete with additional landscaping continuing for the campus.



Child Development Center - South Location



CDC - South Location

- Expected completion is Summer 2023
- Concrete pad has been poured and steel erection has begun for the building
- Site coordination is going well with the start of the second semester at Smith ES
- Utilities and site work for driveways and parking lot are continuing





Hornsby Dunlap Elementary Opened Feb 2023



Hornsby Dunlap Updates

- Ribbon Cutting and opening occurred on January 2, 2023
- Great opening for the students and campus staff
- Final inspections and project punch list is ongoing





Child Development Center - North Location



CDC - North Location

- Renovation process is underway to convert the building in the CDC
- Project completion is anticipated for Summer 2023
- Mechanical upgrades and replacements are ongoing





Del Valle Middle School



Del Valle MS Update

- Roofing and vertical walls are continuing progress
- Interior walls are being framed and sheetrock has started
- Electrical, plumbing, and mechanical trades are continuing progress
- Steel structure is wrapping up
- Windows are being installed
- Main utility connections are underway



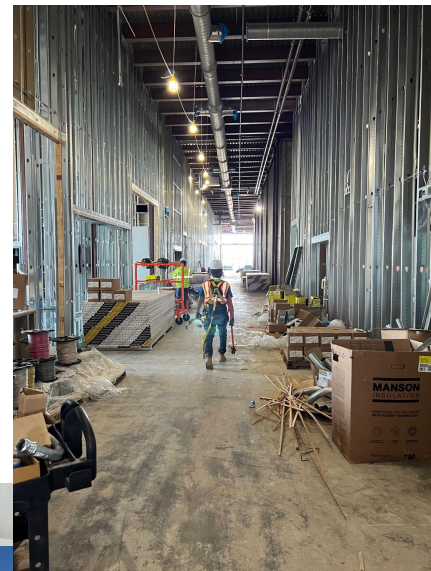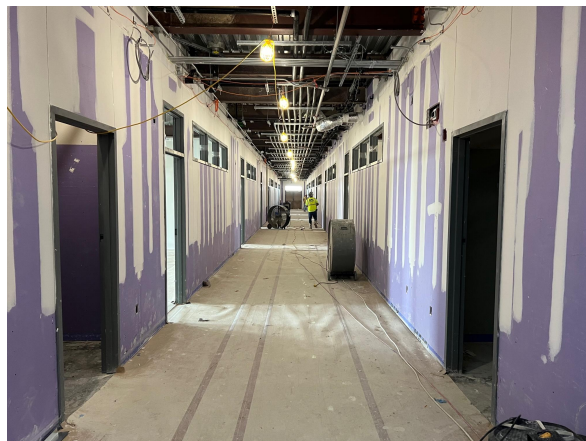



Child Development Center - Central Location



CDC - Central Updates

- Building pad is completed and steel structure installation is underway
- Site work and stormwater pond work is ongoing
- Mechanical and electrical systems are being installed
- Underground utilities are underway





Administration Building Addition



Admin Building Addition Updates

- Building structure is complete with steel structure and roof deck complete
- Wall frames are under construction
- Mechanical systems are being installed
- Electrical component installation is ongoing
- Connection to the existing building is complete
- Project is expected to be completed Fall 2023





Hillcrest Front Entrance Renovation



Hillcrest Front Entrance Update

- Site work and new stone is complete
- Canopy is expected to be completed during Spring 2023
- Front counter and tile is complete
- Added access control is underway
- Flooring is complete for the front office and main campus





Del Valle High School Front Entrance Renovation



Del Valle High School Front Entrance

- Front counter and replacement lighting are complete
- New doors and access control are complete
- Flooring and graphics are complete
- Entrance canopy is complete
- Additional modifications are pending until Summer 2023






Operations Facility



Operations Facility Updates

- Building pad and steel erection is complete
- 2nd Floor mezzanine structure is underway
- Wall and roof installation continues
- Mechanical systems and elevator installation is ongoing
- Utility connection and site work is ongoing
- Expected completion late Fall 2023



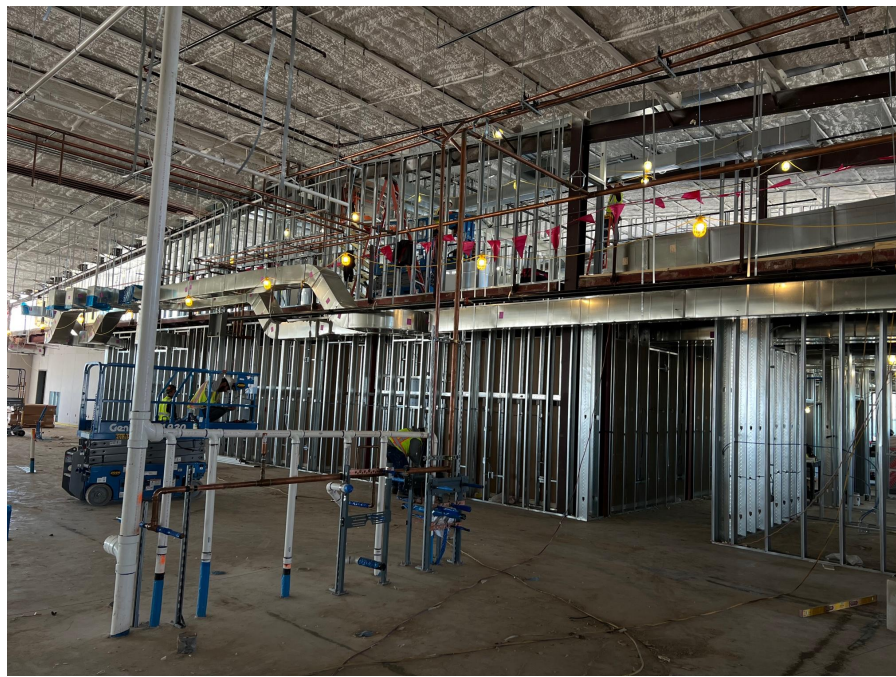





Del Valle Early College High School P-Tech Center



Del Valle ECHS P-Tech Center

- Permit is in final review for the building
- Expected permit approval in Spring 2023 with site work starting in Summer 2023
- Ross Road expansion is pending City of Austin, Texas Department of Transportation and Travis County coordination (DVISD is hosting a community meeting on Jan. 18 at the Opportunity Center)



Del Valle ISD HS #2



Del Valle ISD HS #2

- Land purchase is finalized
- Site development design is continuing
- Structural and geotechnical testing is ongoing
- Permit process is being reviewed with the reviewers from the City and County
- Cost estimates and design revisions are continuing

