

Bond Program Status Report

Through January 2023

809,606,256

800,658,765

8,947,491


2014 Bond Program Executive Summary

January 2023

Bond Program Funding Total

Program Estimate at Complete (EAC)

Projected Program Reserve Estimate at Complete

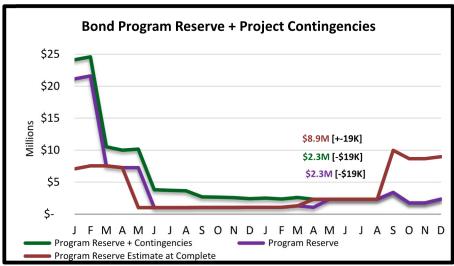

Bond Program Reserve = Funding available but not yet allocated to a specific project

Budget Perspective

This month the overall Program Reserve and Program Reserve EAC both decreased.

• Program Reserve and Program Reserve EAC decreased by \$19K. Increase of \$56K for SB1149 funds received; \$75K decrease for Security Upgrades cost increase.

Schedule Perspective


- Final bids are in for Classroom Walls Phase 3 and 2023 HVAC projects at McKinley, Findley and Nancy Ryles. Ramping up for Summer work.
- All Summer 2022 projects are now substantially complete.

Challenges and Opportunities


• We are seeing unprecedented levels of material cost escalation as well as very long lead times. We have been working to extend our project planning cycles to account for these delays.

2014 Construction Bond Program

Equity Performance January 2023 Report

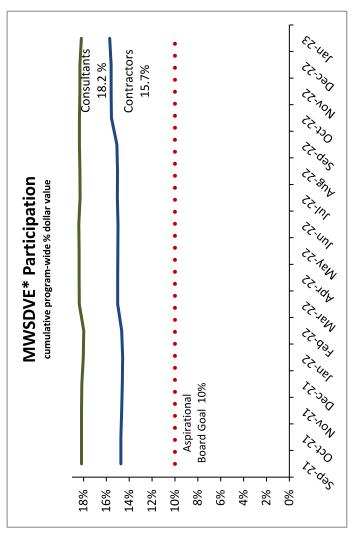

^{*}Minority, Women and Service Disabled Veteran Owned Enterprises

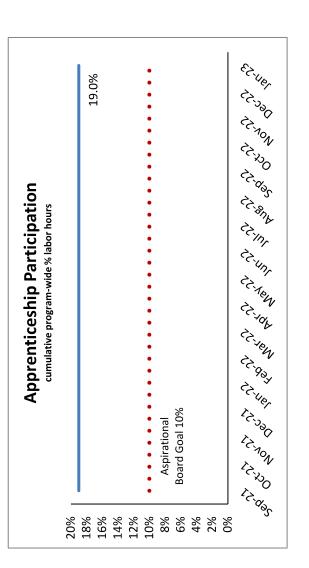

| Project List | ginal Budget Ilocations | Revised Approved Current Budget | _ | Dec-22 @ Comp | J | an-23 Est @ Comp | Net Conti | ngency Balance | Budget Summary Notes |
|---|----------------------------|---------------------------------------|------|------------------|----|---------------------|-----------|----------------|---|
| | | | | | | | | | |
| ACMA Replacement | \$ 28,300,000 | \$ 36,522,767 | \$ | 36,522,767 | \$ | 36,522,767 | | | |
| AHS Title IX Compliance | \$ 2,000,000 | \$ 3,453,433 | \$ | 3,453,433 | \$ | 3,453,433 | | | Completed; Final Cost |
| Capital Center Improvements & Data Center | \$ 5,000,000 | \$ 12,820,187 | \$ | 12,820,187 | \$ | 12,820,187 | | , | Completed; Final Cost |
| District-Wide ADA Compliance | \$ 2,000,000 | \$ 1,523,777 | \$ | 1,523,777 | \$ | 1,523,777 | | | Projects in Process; budget 52% complete |
| District-Wide Communication System | \$ 7,200,000 | \$ 5,282,072 | \$ | 5,282,072 | \$ | 5,282,072 | | | Completed; Final Cost |
| District-Wide Facility Repairs | \$ 98,000,000 | \$ 121,538,970 | \$ 1 | 14,912,036 | \$ | 114,912,036 | | | Budget decr \$300K for barn demo; Budget incr 333K for McKinley roof (trans Seismic); Reduced EAC by \$6.6M |
| District-Wide HVAC Controls | \$ 800,000 | \$ 800,000 | \$ | 800,000 | \$ | 800,000 | | | Projects in Process; budget 53% complete |
| Domestic / Fire Line Separation | \$ 800,000 | (Budget moved to Facilities Repair | | | | | | | |
| Five Oaks MS Renovation & Expansion | \$ 21,100,000 | \$ 28,185,712 | \$ | 28,185,712 | \$ | 28,185,712 | | | Completed; Final Cost; Project closed out, add'l savings of \$10,142. |
| Green Energy Technology | \$ 5,000,000 | (Budget Moved to Other Projects) | | | | | | | Scope completed via new schools and rebuilds |
| Hazeldale K-5 Replacement | \$ 24,600,000 | \$ 31,504,982 | \$ | 31,504,982 | \$ | 31,504,982 | | | Completed; Final Cost |
| IT Data Center @ Capital Center | \$ 2,900,000 | (Budget Moved to CC Project) | | | | | | | Scope completed via Capital Center Improvements |
| Kitchen Improvements | \$ 800,000 | \$ 977,120 | \$ | 977,120 | \$ | 977,120 | | | Projects in Process; budget 80% complete |
| Land for new K-5 @ So. Cooper Mountain | \$ 3,000,000 | \$ 8,072,659 | \$ | 8,072,659 | \$ | 8,072,659 | | | Completed; Adding \$300k to budget for horse barn demo |
| Maintenance Facility Improvements Phase I | \$ 10,000,000 | \$ 11,263,990 | \$ | 11,263,990 | \$ | 11,263,990 | | | In Close-Out; |
| McKay ADA Improvements | \$ 400,000 | \$ 634,540 | \$ | 634,540 | \$ | 634,540 | | | Completed; Final Cost |
| New HS: Mountainside | \$ 109,000,000 | \$ 184,135,294 | \$ 1 | 84,135,294 | \$ | 184,135,294 | | | In Close-Out; |
| New ES: Sato K5 | \$ 25,000,000 | \$ 38,097,642 | \$ | 38,097,642 | \$ | 38,097,642 | | | Completed; Final Cost |
| New MS: Tumwater | \$ 51,600,000 | \$ 61,691,096 | \$ | 61,691,096 | \$ | 61,691,096 | | | Construction completed 2016; |
| Raleigh Hills K-8 Improvements | \$ 9,700,000 | \$ 1,419,490 | \$ | 1,419,490 | \$ | 1,419,490 | | | Completed; Final Cost |
| Raleigh Hills K-8 Conceptual Design | \$ - | \$ 1,000,000 | \$ | 1,000,000 | \$ | 1,000,000 | | | Funding Raleigh Hills Replacement with additional funds from 2022 Bond |
| Raleigh Hills K-8 Improvements | \$ - | \$ 10,821,753 | \$ | 10,821,753 | \$ | 10,821,753 | | | Funding Raleigh Hills Replacement with additional funds from 2022 Bond |
| Security Upgrades | \$ 10,000,000 | \$ 18,833,530 | \$ | 18,758,530 | \$ | 18,833,530 | | | Projects in Process; budget 96% complete; added \$375K for SHS vestibule |
| Seismic Upgrades | \$ 4,200,000 | \$ 25,865,072 | \$ | 25,865,072 | \$ | 25,865,072 | | | Projects in Process; budget 86% complete |

| Project List | | al Budget cations | Revised Approved Current Budget | | Dec-22 st @ Comp | Já | an-23 Est @ Comp | Net Contingency Balance | | Budget Summary Notes |
|--------------------------------------|--------|----------------------|------------------------------------|------|---------------------|----|---------------------|-------------------------|--------------|---|
| | | | | | | | | | | |
| SHS Title IX Compliance | \$ | 2,000,000 | \$ 4,294,693 | \$ | 4,294,693 | \$ | 4,294,693 | | | Completed; Final Cost (Adjusted cost by \$9K) |
| Springville K-8 Improvements | \$ | 2,000,000 | \$ 510,016 | \$ | 510,016 | \$ | 510,016 | | | Completed; Final Cost |
| Vose K-5 Replacement | \$ | 24,800,000 | \$ 33,846,280 | \$ | 33,846,280 | \$ | 33,846,280 | | | Completed; Final Cost |
| William Walker K-5 Replacement | \$ | 24,600,000 | \$ 34,626,711 | \$ | 34,626,711 | \$ | 34,626,711 | | | Completed; Final Cost |
| Added Projects | \$ | - | \$ 13,841,010 | \$ | 13,841,010 | \$ | 13,841,010 | | | Vose budget reduced by \$950K; 2.3M added to Classroom walls from Prog Reserve |
| Program Contingency | \$ | 45,400,000 | | | | | | | | |
| Program Inflation | \$ | 52,800,000 | | | | | | | | |
| Pre-Bond Expenditure Reimbursements | \$ | 1,000,000 | \$ 998,828 | \$ | 998,828 | \$ | 998,828 | | • | Completed; Final Cost |
| Bond Management Costs | \$ | 20,000,000 | \$ 30,990,506 | \$ | 30,990,506 | \$ | 30,990,506 | | | |
| Bond Issuance Costs | \$ | 6,000,000 | \$ 3,733,569 | \$ | 3,733,569 | \$ | 3,733,569 | | | Completed; Final Costs (\$266K moved to PR) |
| Construction Subtotal | \$ 60 | 0,000,000 | \$ 727,285,699 | \$ 7 | 20,583,765 | \$ | 720,658,765 | | | |
| Learning Technology | \$ | 56,000,000 | \$ 56,000,000 | \$ | 56,000,000 | \$ | 56,000,000 | | | |
| Critical Equipment | \$ | 24,000,000 | \$ 24,000,000 | \$ | 24,000,000 | \$ | 24,000,000 | | | |
| Tech & Equip Subtotal | \$ 8 | 80,000,000 | \$ 80,000,000 | \$ | 80,000,000 | \$ | 80,000,000 | | | |
| Grand Totals | \$ 68 | 80,000,000 | \$ 807,285,699 | \$ 8 | 300,583,765 | \$ | 800,658,765 | \$ - | | |
| Added Funding to Bond Program | | | | | | | | | | |
| Bond Premium (First Bond Sale) | \$ | 63,295,961 | | | | | | | | |
| Bond Premium (Second Bond Sale) | \$ | 30,270,107 | | | | | | | | |
| Interest Earnings (First Bond Sale) | \$ | 5,340,214 | | | | | | | | |
| Interest Earnings (Second Bond Sale) | \$ | 14,190,118 | | | | | | | | |
| Other Additional Funding (see Tab) | \$ | 16,509,856 | | | | | | | | Increased SB1149 \$56,100 |
| Grand Total Added Funding | \$ 129 | 9,606,256 | | | | L | | | | |
| GRAND TOTAL 2014 BOND FUNDING | \$ 809 | 9,606,256 | | | | | | | | Increase in added funding. |
| Program Reserve | | | \$ 2,320,557 | | | | | | | Overall decrease of approx \$19k; Increase of \$56K for SB1149 funds received; \$75l decrease for Security Upgrades cost increase |
| Program Reserve EAC | | | | | | | | | \$ 8,947,491 | Overall decrease of approx \$19k; Increase of \$56K for SB1149 funds received; \$75k decrease for Security Upgrades cost increase |

| ource | | Funding | Assigned to Projects | Assigned to gram Reserve | Budget Summary Notes |
|--|----|--------------|-----------------------|-----------------------------|--|
| | | | | | |
| Remaining 2006 Bond Savings | \$ | 576,615 | Mountainside HS | \$ - | |
| Capital Center Rent Revenue Balance | \$ | 433,385 | Mountainside HS | \$ - | |
| Construction Excise Tax Revenue | \$ | 1,130,655 | Capital Center | \$ = | |
| Construction Excise Tax Revenue forecasted to 2021 | \$ | 5,021,577 | | \$5,021,577 | |
| THPRD reimb. | \$ | 449,783 | | \$ 449,783 | |
| SB 1149 reimb. | \$ | 3,638,600 | District-wide Repairs | \$ 248,828 | Whitford \$26,800/Highland Park \$29,300 |
| ETO reimb. | \$ | 1,637,959 | District-wide Repairs | \$ 1,450,880 | |
| Facility grants | \$ | 3,027,507 | | \$ 3,027,507 | |
| Sato: TVWD Reimbursement | \$ | 593,774 | Sato K-5 | \$ - | |
| | | | | | |
| TOTAL | | \$16,509,856 | | \$10,198,575 | |

| Added Projects | Approved by & Date | Original Budget | Revised Approved Current Budget | Dec-22 Est @ Comp | Jan-23 Est @ Comp | | Budget Summary Notes |
|------------------------------------|---------------------|-----------------|------------------------------------|-------------------|-------------------|----------|---|
| | | | | | | <u> </u> | |
| Seclusion Rooms Alterations | Safety Comm 5/19/14 | | \$ 99,368 | \$ 99,368 | \$ 99,368 | | Completed; Final Cost |
| Portable Relocations 2014 | Sr LT 5/20/14 | \$ 17,956,364 | \$ 591,685 | \$ 591,685 | \$ 591,685 | | Completed; Final Cost |
| Portable Relocations 2015 | Sr LT 3/2015 | | \$ 294,257 | \$ 294,257 | \$ 294,257 | | Completed; Final Cost |
| Title IX Projects - Group II | Sr LT 3/2015 | | \$ 1,030,697 | \$ 1,030,697 | \$ 1,030,697 | | Completed; Final Cost |
| Classroom Door Locks | SB 6/18/18 | | \$ 2,179,293 | \$ 2,179,293 | \$ 2,179,293 | | Budget 85% complete; phase 2 work ongoing |
| Security Upgrades: Classroom Walls | SB 6/15/20 | | \$ 4,345,710 | \$ 4,345,710 | \$ 4,345,710 | | transfer of 2.3M from Program Reserve |
| Security Upgrades: Paging | SB 6/15/20 | | \$ 500,000 | \$ 500,000 | \$ 500,000 | | |
| Security Upgrades: Site Fencing | SB 6/15/20 | | \$ 1,700,000 | \$ 1,700,000 | \$ 1,700,000 | | |
| Vose Classroom Addition | SB 6/21/21 | | \$ 2,950,000 | \$ 2,950,000 | \$ 2,950,000 | 0% | Transferred \$150K to Sato Classroom |
| Sato Classroom Addition | SB 2/28/22 | | \$ 150,000 | \$ 150,000 | \$ 150,000 | | Design approved at 2/28/22 SB Meeting. |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| Added Projects Total | | ¢ 47.056.264 | ¢ 42 944 040 | ¢ 42.044.040 | ¢ | | |
| Added Projects Total | | \$ 17,956,364 | \$ 13,841,010 | \$ 13,841,010 | \$ 13,841,010 | | |
| | | | | | | | |

| Project | Initial Budget | | | vised Approved urrent Budget | Dec-22 Est @ Comp | | J | Jan-23 Est @ Comp | | Net Contingency I | Balance | Budget Summary Notes |
|---|----------------|--------------------------|--|---------------------------------|----------------------|---------------|--|----------------------|----|-------------------|---------|--|
| | | | | | | | | | | | | |
| Completed Projects | \$ | 28,722,705 | \$ | 59,818,969 | \$ | 59,818,969 | \$ | 59,818,969 | | | | Completed; Final Cost |
| Projects in Close-out | \$ | 6,883,538 | \$ | 21,655,377 | \$ | 21,655,377 | \$ | 21,655,377 | \$ | - | 0.0% | |
| 2022 Repipes | \$ | - | \$ | 1,500,000 | \$ | 1,500,000 | \$ | 1,500,000 | \$ | 150,000 | 11.1% | |
| 2021 Roof Replacements | \$ | 1,972,000 | \$ | 5,100,797 | \$ | 5,100,797 | \$ | 5,100,797 | \$ | 124,566 | 2.5% | |
| Hiteon HVAC Controls Upgrade | \$ | 200,000 | \$ | 593,783 | \$ | 593,783 | \$ | 547,557 | \$ | - | 0.0% | |
| Raleigh Park Sewer | \$ | 47,000 | \$ | 100,000 | \$ | 100,000 | \$ | 72,072 | \$ | 10,650 | 11.9% | |
| ISB HVAC & Roof | \$ | 864,000 | \$ | 2,505,406 | \$ | 2,945,262 | \$ | 2,945,262 | | | 0.0% | |
| District-Wide Fire Alarm Resiliency | \$ | 1,303,000 | \$ | 2,474,120 | \$ | 2,474,120 | \$ | 2,474,120 | \$ | - | 0.0% | |
| 2022 Roof Replacements 1 (NR, McK, Findley) | \$ | 1,380,000 | \$ | 6,415,230 | \$ | 6,415,230 | \$ | 6,415,230 | \$ | 307,600 | 5.0% | McKinley bid received, \$1.6M increase |
| 2022 Roof Replacements 2 (Fir Grove, Grwy) | \$ | 277,000 | \$ | 1,792,200 | \$ | 1,792,200 | \$ | 1,792,200 | \$ | 58,576 | 3.4% | |
| 2022 HVAC Upgrades 1 (EH, Kinnaman, McK) | \$ | 882,000 | \$ | 114,080 | \$ | 114,080 | \$ | 114,080 | | | 0.0% | split funded with ESSER |
| 2022 HVAC Upgrades 2 (NR, Grwy, EIM, Stoller) | \$ | 1,712,000 | \$ | 97,600 | \$ | 741,000 | \$ | 741,000 | | | 0.0% | split funded with ESSER |
| Five Oaks Roof | \$ | - | \$ | 416,000 | \$ | 416,000 | \$ | 416,000 | \$ | 29,000 | 7.5% | |
| New Schools Post-Warranty Fund | \$ | - | \$ | 650,000 | \$ | 650,000 | \$ | 350,000 | | | | |
| Maint Dept Repair & Improvement & Other Projects* | \$ | 9,068,708 | \$ | 11,844,536 | \$ | 10,595,219 | \$ | 10,969,373 | | | | |
| Repair Projects Total | \$ | 53,311,951 | \$ | 114,559,411 | \$ | 114,912,036 | \$ | 114,912,036 | | | | |
| Repair Program Balance Available | \$ | 44,688,049 | \$ | 6,979,559 | | | | | | | | |
| Repair Program EAC Balance | \$ | = | | | | | | | | | | |
| Repair Program Budget (Less Transfers In/Out) | \$ | 98,000,000 | | 121,538,970 | | 114,912,036 | | | | | | |
| *Budget and Est @ Comp. will increase each month as addition | nal Mai | intenance Dept. | mana | aged Repair Projec | ts a | re scheduled. | | | | | | |
| Transfer Tracking | _ | 00 000 000 | | | | | _ | | | | | |
| Initial Budget Previous Transfers | \$ \$ | 98,000,000 22,091,701 | - | | | | | | - | | | |
| SB 1149 Reimbursements | \$ | 3,015,562 | | | | | <u> </u> | | | | | |
| ETO Reimbursements | \$ | 187.079 | - | | | | <u> </u> | | | | | |
| Funds transferred to Seismic- Bethany ES | \$ | (2,230,000) | - | | | | <u> </u> | | | | | |
| Funds transferred to Seismic-Bethany ES Funds transferred to Added Projects - Classroom Door Locks | \$ | (2,230,000) | | | | | \vdash | | | | | |
| Additional Funding - Elmonica Repipe - Approved 6.21.2021 | \$ | 500.000 | | | | | | | | | | |
| Funds transferred to Added Projects - Classroom Walls | \$ | (45,710) | | | | | | | | | | |
| Funds transferred to Added Frojects - Classicoth Walls Funds transferred from Five Oaks | \$ | 150,000 | 1 | | | | | | | | | |
| Funds transferred from tive data Funds transferred to Seismic- West TV ES | \$ | (460,827) | 1 | | | | | | | | | |
| Transfer from Seismic for Roof Repl - Group 1 | \$ | 247,273 | | | | | H | | | | | |
| Transfer from Five Oaks for Roof Project | \$ | 230,565 | | | | | <u> </u> | | | | | |
| Transfer to Land project for horse barn demo | \$ | (300,000) | | | | | \vdash | | | | | |
| Transfer from Seismic to McKinley roofing | \$ | 332,620 | | | | | T | | | | | |
| Balance | - | 121,538,970 | | | | | \vdash | | | | | |
| Balance | _ Ψ | 121,000,010 | | | | | | | 1 | | | <u> </u> |

| Seismic Projects | Original Budget | Revised Approved Current Budget | Dec-22 Est @ Comp | | Jan-23 Est @ Comp | Net Contingen | cy Balance | Budget Summary Notes |
|--|------------------------------|---|----------------------|-------|----------------------|---------------|------------|--|
| | | | | | | | | |
| A/E Scoping/Surveys | \$ - | \$ 244,603 | \$ 244, | 603 | \$ 244,603 | | | Completed; Final Cost (Budget increased 22k for grant adj) |
| Aloha HS | \$ 1,732,898 | \$ 17,976,438 | \$ 17,976, | 438 | \$ 17,976,438 | | | Completed; Final Cost |
| Beaver Acres ES | \$ 1,714,444 | \$ 5,926,866 | \$ 5,926, | 866 | \$ 5,926,866 | | | Completed; Final Cost |
| Beaverton HS | \$ 246,184 | (Budget Transferred to Seismic Program) | | | | | | Scope completed via BHS Gym Ceiling project |
| Cedar Mi ll ES | \$ 144,771 | (Budget Moved to Facility Repairs) | | | | | | Scope completed via Cedar Mill Roof & HVAC project |
| Cooper Mt. ES | \$ 361,703 | | \$ 2,683, | 463 | \$ 2,683,463 | | | Completed; Final Cost (Budget savings of \$46K) |
| Bethany ES | \$ - | \$ 4,930,811 | \$ 4,930, | 811 | \$ 4,930,811 | | 0.0% | In Close Out |
| Seismic Red Zones | \$ 1,635,632 | \$ 160,300 | \$ 160, | 300 | \$ 160,300 | | | |
| 2022 SRGP Planning | \$ - | \$ 100,000 | \$ 100, | 000 | \$ 100,000 | | | |
| West TV Seismic (Gym) | \$ - | \$ 597,827 | \$ 597, | 827 | \$ 597,827 | | 0.0% | In Close Out |
| Seismic Red Zones (Rock Creek/SHS) | \$ - | \$ 239,700 | \$ 239, | 700 | \$ 239,700 | | | Project is now under contract, bid results increase budget from seismic funding hold by about \$30K. |
| Seismic Funding Hold | \$ - | \$ 267,450 | \$ 267, | 450 | \$ 267,450 | | | transfer \$332,620 to McKinley Roofing for additional seismic |
| | | | | | | | | |
| (Projects Financially Complete) | | | | | | | | |
| Originals Products Total | \$ 5.835.632 | \$ 33,127,458 | l | 450 L | \$ 33,127,458 | | | |
| Seismic Projects Total | * 0,000,000 | | | | | | | |
| TAPS Seismic Grant | | \$ (22,545) | • | 545) | • • • | | | |
| AHS Seismic Rehabilitation Grant | | \$ (2,500,000) | • | - | | | | |
| Beaver Acres Seismic Rehabilitation Grant | | \$ (2,500,000) | • • • | | | | | |
| Cooper Mnt Seismic Rehabilitation Grant | | \$ (2,239,841) | | | | | | |
| Seismic Program Bond Cost Balance | \$ 4,200,000 | \$ 25,865,072 | \$ 25,865, | 072 | \$ 25,865,072 | | | |
| Seismic Program Less Transfers In/Out | \$ 25,865,072 | | | | | | | |
| Transfer Tracking | · · | | | | | | | |
| Initial Budget | \$ 4,200,000 | | | | | - | | |
| Program Escalation | \$ 1,006,740 | | | | | | | |
| AHS Roofing - From Facility Repairs | \$ 575,193 | | | _ | | | | |
| Beaver Acres Roofing - From Facility Repairs | \$ 1,138,000 \$ 3,477,807 | | | | | | | |
| AHS Roofing - Balance From Facility Repairs Program Reserve - Approved by School Board 6.18.1 | \$ 3,477,807 \$ 5,450,000 | | | | | | | |
| Transfer to Facility Repairs - Cedar Mill | \$ (166,052) | | | | | | | |
| | \$ 128,000 | | | | | | | |
| Program Reserve - Approved by School Board 10.28 | | | | | | | | |
| Beaver Acres Windows - From Facility Repairs | \$ 605,000 | | | | | | | |
| Beaver Acres Re-pipe - From Facility Repairs | \$ 489,500 | | | | | | | |
| Bethany Roof and HVAC Seismic Transfer | \$ 2,230,000 | | | | | ļ | | |
| West TV Seismic (Gym) Transfer Transfer to McKinky Reafing (2022 Reaf Phase 1) | \$ 460,827 \$ (247,273) | | | | | | | |
| Transfer to McKinley Roofing (2022 Roof Phase 1) Transfer to McKinley Roofing (addt'l seismic) | \$ (247,273) (332,620) | | | - | | + | | |
| Balance | | | | -+ | | + | | |
| Dalance | ψ 20,000,072 | | J | 1 | | I | | |
