


BOND UPDATE #194

3.3.23


Here's what is going on with our bond projects.

Enjoy!
Kristi


1. Crews finished constructing the ramp up to the Grandstands this week.
2. The roof decking is now being installed on the canopy connecting the Academic Wing's main entry to the CTE and Athletic wings.
3. Geopier installation wrapped up this week. Now, concrete crews can start forming the foundation for the new CTE Wing.
4. Crews continue to install plumbing and electrical equipment in the Grandstands' concessions and restrooms. Soon, this area will be ready for sheetrock work to begin.
5. Our team is making good progress on completing the Greenhouse. We're close to the finish line!
6. Old Main was demolished this week. Crews should have the rubble hauled off-site by early next week.
7. The Ferndale School Board received an update on bond-related items at their regular meeting Tuesday.
8. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
9. Below is the FHS project timeline as of January 20. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

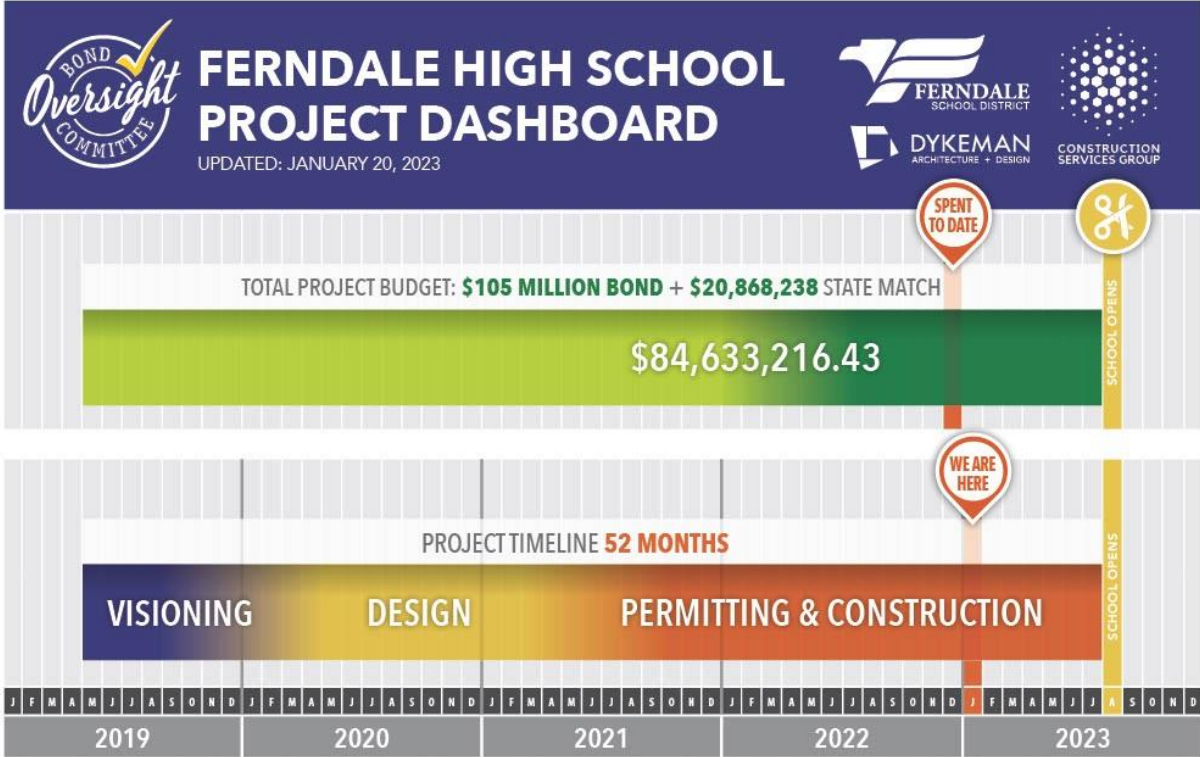

10. Below is a map showing the various components of the new FHS campus and when they'll be completed.

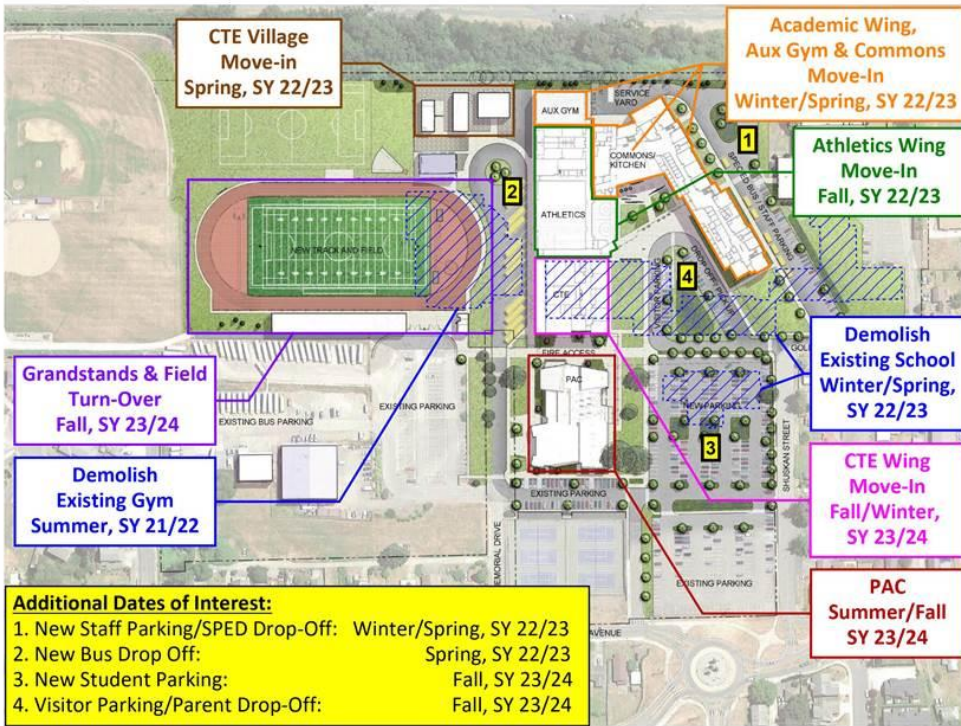

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



Crews making good progress on the Greenhouse



Excavating for and forming of the foundation under the new CTE Wing



The old campus is mostly gone, fully unveiling the new campus to passers-by on Vista Drive
