



**APRIL 2020
REFERENDUM**

Community-Led Process.
Community-Led Solution.


QUESTIONS? CONTACT:

Annette Deuman, Superintendent
referendum@columbus.k12.wi.us
920.350.0365



PROJECT PROGRESS REPORT

High School Library
renovation.

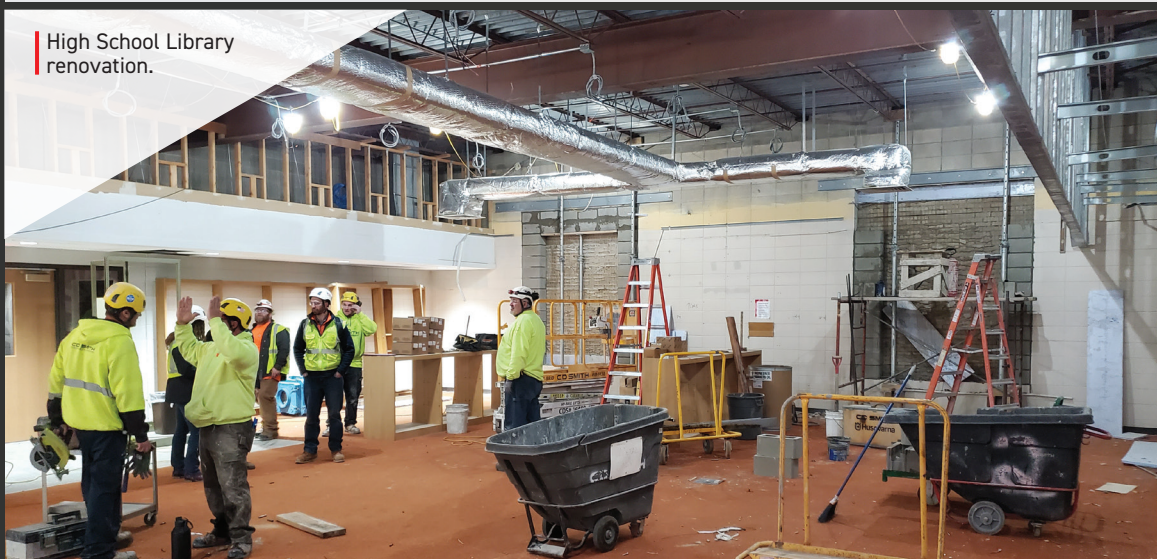

WHAT'S NEW

- The elementary school addition is nearing completion, and construction crews will begin renovating the existing building.
- Renovations are continuing in the high school library and STEAM areas.

CONSTRUCTION UPDATES

Elementary School

- Site work on the school grounds continues. A retaining wall behind the new gym is under construction, and grading behind the new classroom addition is complete.
- Installation of finishing touches in the new classroom wing, including metal lockers, acoustical ceilings, flooring, and toilet room finishings, continues.
- The elevator was installed.
- In the gymnasium, painting is complete, and the new gym equipment was installed.

High School

- Equipment is being moved into the new fitness room.
- Interior demolition has begun at the library to prepare for renovation, and portions of the exterior library wall have been removed for new window installation.

High School (continued)

- In the STEAM wing, new metal stud and concrete masonry walls are being constructed, and holes are being punched in existing walls to create openings, which will create transparency and connection between spaces.

WHAT'S NEXT?

Looking into the next month, the work schedule includes:

Elementary School

- A new storm sewer is being installed behind the new classroom addition where it is connected to Fountain Street.
- Installation of the wood gym floor will begin.
- Heating, ventilation, and air conditioning (HVAC) system startup will continue.
- Renovation in the existing building will begin after the completion of the school year.

High School

- Drywall installation will begin in the library and STEAM areas, starting with new soffits.
- Demolition in STEAM area toilet rooms will soon begin.
- Electrical work will take place in the library.
- Window frames will be delivered for the new exterior and interior openings.



APRIL 2020 REFERENDUM

Community-Led Process.
Community-Led Solution.

QUESTIONS? CONTACT:

Annette Deuman, Superintendent
referendum@columbus.k12.wi.us
920.350.0365



PROJECT **PROGRESS REPORT**

DISTRICT-WIDE UPDATES

- Construction at the elementary, middle, and high schools will complete in phases by August 2022.

New classroom wing at the Elementary School.



New classroom wing at the Elementary School.

