


BOND UPDATE #195

3.10.23



Here's what is going on with our bond projects.

Enjoy!
Kristi

1. Crews are making good progress on building the ramps, stairs and skirting on the front side of the Grandstands.
2. The rubberized layer underneath the football field's turf made its first appearance this week. This layer is widely used on football fields to create a softer landing for athletes after a tackle or fall.
3. Now that the roofing is finished for the Grandstands' concessions and restrooms, crews have started the sheetrock process.
4. The canopy connecting the Academic Wing's main entrance and the CTE/Athletic wings is now standing and ready for roofing work to begin.
5. Crews are now very close to completing the Greenhouse. The heater is currently back-ordered – but when that is installed, the building will be ready for school use.
6. Old Main rubble continued to be hauled off-site this week. This process is nearly finished.
7. Crews have began building the foundation of the CTE Wing.
8. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://ferndalesd.org/Bond2019)
9. Below is the FHS project timeline as of January 20. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

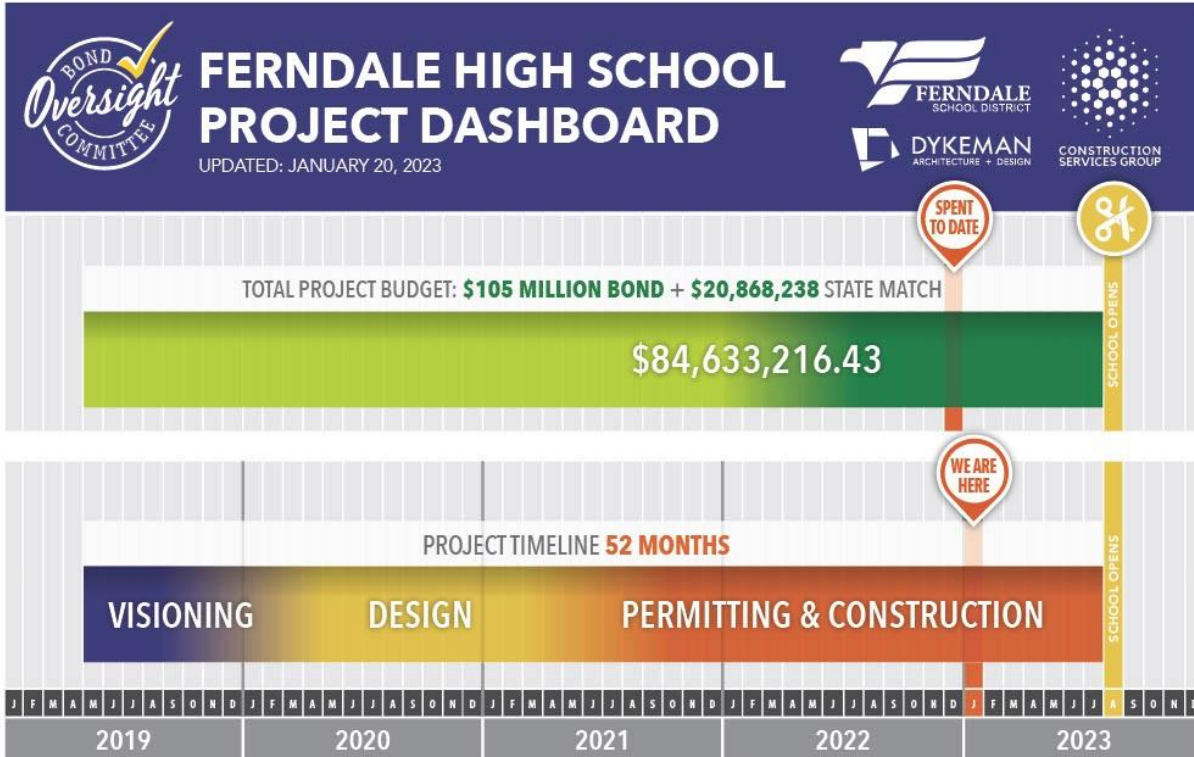

10. Below is a map showing the various components of the new FHS campus and when they'll be completed.

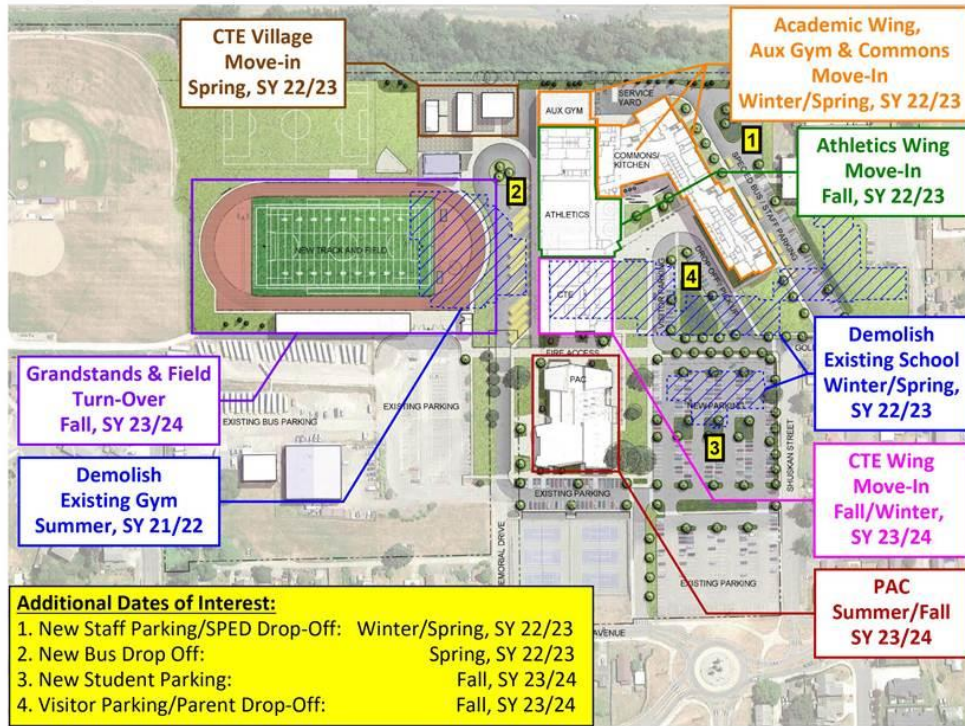

FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



View of the football field from the top of the Grandstands



The north end of the new FHS track



The Grandstands' final skirting was installed this week



Installation of the rubberized layer that will sit below the astroturf



Sheetrock installation in the Grandstand bathrooms began this week



Good progress being made on the new CTE Wing's foundation



Old Main is almost gone, closing an era of FHS
