BOND

2017
Spring Branch ISD



2017 Bond Program Bond Oversight Committee (BOC)

November 9, 2022

Agenda

- Introductions
- Communication Updates
- Finance Updates
- Career & Technology Education (CTE) Updates
- Fine & Performing Arts Updates
- Technology Updates
- Transportation Updates
- Planning & Construction Updates
- Questions from the BOC



Introductions:

District Staff

Dr. Jennifer Blaine Superintendent of Schools

Linda Buchman Associate Superintendent for Communications

Christine Porter Associate Superintendent for Finance

David Bender Comptroller

Kristin Craft Associate Superintendent of Academics

Christina Rice-Imumwen Director of Career and Technical Education (CTE)

Houston Hayes Director of Performing and Fine Arts

Christina Masick Associate Superintendent for Technology

Stephen Johnston Director of Customer Service
Sherri Lawson Director of Transportation

Travis T. Stanford Associate Superintendent for Operations

BOC Co-Chairs

Lewis Gissel - <u>lgissel3@gmail.com</u> Kathy Goss - <u>johngoss4@aol.com</u>



Communications Updates:

Upcoming Groundbreaking Ceremonies:

- Memorial Drive ES
- Woodview ES

Featured News:

2017 Bond continues to transform district with grand opening of Bunker Hill Elementary <a href="https://www.springbranchisd.com/news/read-more/~board/sbisd-post-board/post/2017-bond-delivers-elevated-teaching-and-learning-environments-sbisd-celebrates-grand-opening-of-new-bunker-hill-elementary

Community celebrates Northbrook High School's new classroom wing as part of 2017 Bond community-celebrates-northbrook-high-schools-new-classroom-wing-as-part-of-2017-bond

Spring Branch ISD sells \$307 million of bonds, proceeds to be used for school construction, technology, equipment and buses

https://www.springbranchisd.com/news/read-more/~board/sbisd-post-board/post/spring-branch-isd-sells-307-million-of-bonds-proceeds-to-be-used-for-school-construction-technology-equipment-and-buses

Finance Update as of September 30, 2022:

Expenditures

 July – September 2022
 \$ 13,180,662

 April – June 2022
 \$ 32,535,569

 Inception through Sept. 2022
 \$ 442,559,780

Interest Earnings

 July – September 2022
 \$ 964,785

 April – June 2022
 \$ 329,675

 Inception through Sept 2022
 \$ 12,489,029

Issuance

 Issued June 2018
 \$ 146,000,000

 Issued October 2019
 \$ 255,000,000

 Issuance November 2020
 \$ 169,000,000

 Authorized but Unissued
 \$ 328,400,000

Pending October 2022 Issuance \$142,204,000



Career and Technical Education (CTE) Updates:

- Campus Refresh on Computers/Printers
 - Camera's, Wacom Tablets, Printers and other equipment supporting our Digital Communications and STEM Programs of Study
 - NHS, SWHS, SHS,AOC, SWHS
 - Difference from previous quarter is \$44,649.99
 - 2022-2023 Pending: Guthrie classroom refresh

2022-2023 CTE 2017 Bond Projects Expenditures Update						
2017 Bond Project	Total Amount (21-22 4 th Quarter)	Total Amount (22-23 1 st Quarter)	Total Amount (22-23 New Quarter)			
Refresh Equipment for Current Programs	\$2,347,581.29	\$2,389,989.67	\$2,434,639.66			
Visioning the Future of CTE /Stantec Architecture, Inc.	\$685,525.00	\$685,525.00	\$685,525.00			
Total	\$3,033,106.29	\$3,075,514.67	\$3,120,164.66			



Fine and Performing Arts Updates:

Current Allocation

Uniforms:

- Stratford High School Band Completed and in use
- Northbrook Drill Team Completed and in use
- Northbrook Band Completed and in use

2022 School Year Allocation

- Memorial HS Band Uniforms Spring 2023
- Stratford Drill Team Uniforms Spring 2023
- Spring Woods HS Band Uniforms Spring 2022 In Design Phase

2024 School Year Allocation

Stage Curtain Replacement Secondary Campuses



Technology Updates:

Construction Moves

- Preparing Memorial Drive Elementary for move to South Transition Campus
- Preparing Woodview Elementary for move to East Transition Campus

Infrastructure

- Completed final component of the districtwide phone system modernization
 - Replaced Police Department phone recording system



Transportation Updates:

2017 BOND PROGRAM SCHOOL BUS REPLACEMENT SCHEDULE

SCHOOL YEAR	# OF BUSES SCHEDULED TO REPLACE	ADDITIONAL REG ED BUSES REQURIED FOR CAPACITY	# OF BUSES	REPLACEMENT AGE	ESTIMATED COST
2017/2018	0	0	0		0
2018/2019	19	6	25	15-17 yrs.	Less = \$521,477.00 (Grant Monies) = \$2,449,823.00
2019/2020	5 rolled over from 18-19	0	5	15-17 yrs.	Less = \$ 275,000 (Grant Monies)
2020/2021	0	0	0		0
2021/2022	7	4	11	18 yrs.	\$1,477,520.00
2022/2023	7	4	11	18 yrs.	\$1,443,365.00
2023/2024	8	3	11	18 yrs.	\$1,443,365.00
2024/2025	8	3	11	18 yrs.	\$1,443,365.00
2025/2026	8	3	11	18 yrs.	\$1,477,520.00
2026/2027	8	3	11	18 yrs.	\$1,511,675.00
Total	65	26	91		\$11,246,633.00

Transportation ordered 22 new buses February 2022. 7 of these buses have been received so far. All buses are anticipated to be delivered by Spring/Summer 2023.



Planning & Construction Updates:

The following Bond projects are currently underway:

- o **Pre-K Furniture:** Installation of student desk and tables to occur fall of 2022.
- Bunker Hill Elementary School Replacement Project: In Construction Phase Students and staff moved into the new campus August 2022. Playground installation and Phase 1 landscaping complete. Underground detention at Play Fields complete, with field irrigation and sod installation to begin in two weeks.
- Memorial Drive Elementary School Replacement Project: In Design Phase Project Advisory Team (PAT) meetings successfully completed. Students and staff will relocate to the South Transition Campus during the Construction Phase in December 2022.
- Nottingham Elementary School Replacement Project: Construction in process, staff and students remaining onsite during construction phase.
- Woodview Elementary School Replacement Project: In Design Phase PAT meetings successfully completed. Students and staff will relocate to the East Transition Campus during the Construction Phase in December 2022.
- Memorial Middle School Renovation Project: Renovations for summer of 2022 completed and additional renovation work planned for summer of 2023. Campus will be offline during 2022 & 2023 summer months.
- Memorial High School Addition and Renovation Project: Staff and students moved into new four-story tower January 2022. Demolition of the Aqua, White, and Green Wings completed summer of 2022. Installation of a new student drop-off, bus loop/staff parking and central courtyard completed. (Project to be completed by end of calendar year, 2022)
- Northbrook High School Addition and Renovation Project: Renovation scope complete. Staff and students moved into new 18 classroom and 2 Science Lab addition August 2022.
- o Stratford High School Addition and Renovation Project: Renovation scope complete. Auditorium completed.
- o Administration Building HVAC Renovation Project: Project to be completed by end of summer 2022.

Planning & Construction Updates:

School: Bunker Hill ES

Scope of Work: New Construction/Replacement Campus

Project Manager: Geoff Bay

Architect/Engineer: Stantec Architects - **Contractor**: Durotech

Status: Project is currently in Construction Phase.



Planning & Construction Updates:

School: Bunker Hill ES





Ribbon Cutting Ceremony held on held September 14, 2022

Planning & Construction Updates:

School: Bunker Hill ES





Public entrance to playground

Playground view from swing sets

Planning & Construction Updates:

School: Bunker Hill ES





Play structure for lower grades

Play structure for upper grades

Planning & Construction Updates:

School: Bunker Hill ES





Track and field detention

Planning & Construction Updates:

School: Nottingham ES

Scope of Work: New Construction/Replacement Campus

Project Manager: Noel Moreno

Architect/Engineer: PBK Architects - **Contractor**: Durotech

Status: Project is currently in Construction Phase.



Planning & Construction Updates:

School: Nottingham ES





Aerial view as of August 8, 2022

Aerial view as of October 3, 2022

Planning & Construction Updates:

School: Nottingham ES





Aerial view as of August 8, 2022

Aerial view as of October 3, 2022

Planning & Construction Updates:

School: Nottingham ES





Bus loop drive

Power trawlers stabilizing and smoothing slab

Planning & Construction Updates:

School: Memorial Drive ES

Scope of Work: New Construction/Replacement Campus

Project Manager: David Valerius

Architect/Engineer: Stantec Architects - **Contractor**: Marshall

Status: Project is currently in Design Phase.




Planning & Construction Updates:

School: Memorial Drive ES

- Memorial Drive ES will be the fourth school out of nine elementary school replacement projects in the 2017 Bond Program
- Students and staff will move offsite to the South Transition Campus during the construction phase
- The new Memorial Drive ES will be designed for 550 students
- Seven successful Project Advisory Team (PAT) meetings have been completed



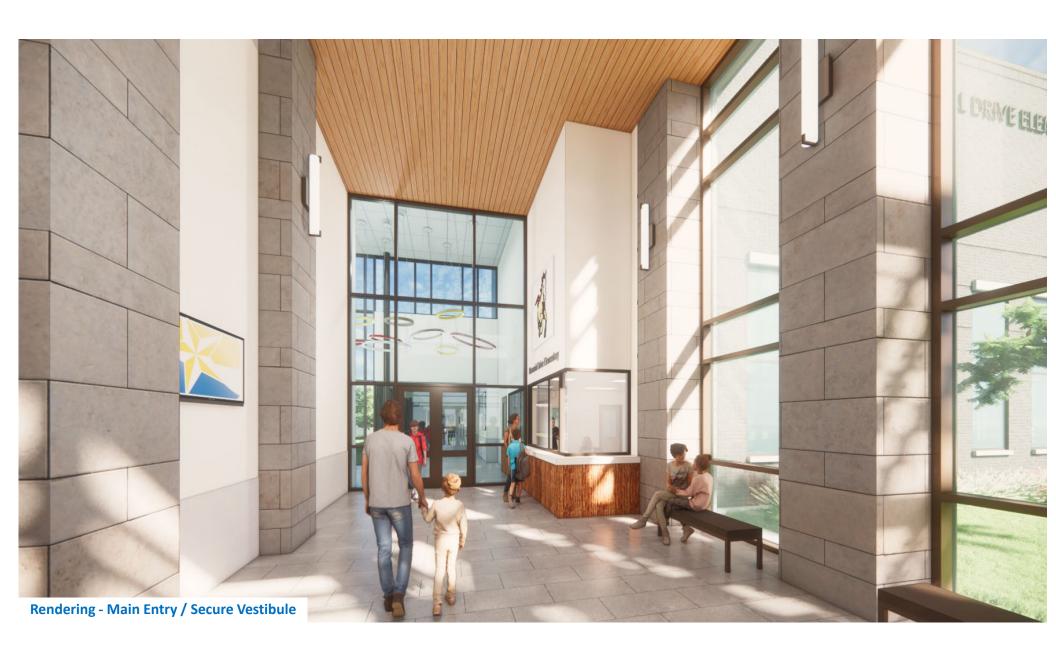









Planning & Construction Updates:

School: Sherwood ES

Scope of Work: New Construction/Replacement Campus

Project Manager: Alfonso Montoya

Architect/Engineer: TBD - Contractor: TBD

Status: Project is currently in Fact Finding Phase.



Planning & Construction Updates:

School: Sherwood ES

- Sherwood ES will be the sixth school out of nine elementary school replacement projects in the 2017 Bond Program
- Students and staff will remain onsite during the construction phase
- The new Sherwood ES will be designed for 600 students
- Project Advisory Team (PAT) meetings are projected to begin early 2023





Planning & Construction Updates:

School: Woodview ES

Scope of Work: New Construction/Replacement Campus

Project Manager: David Ramirez

Architect/Engineer: Stantec Architects - **Contractor**: Brookstone

Status: Project is currently in Design Phase.



Planning & Construction Updates:

School: Woodview ES

- Woodview ES will be the fifth school out of nine elementary school replacement projects in the 2017 Bond Program
- Students and staff will move offsite to the East Transition Campus during the construction phase
- The new Woodview ES will be designed for 700 students
- Six successful Project Advisory Team (PAT) meetings have been completed











Planning & Construction Updates:

School: Memorial MS – Phase 1
Scope of Work: Renovation Project
Project Manager: Noel Moreno

Architect/Engineer: PBK Architects - **Contractor**: Bass Construction

Status: Phase 1 complete. Phase 2 to begin Summer 2023.



Planning & Construction Updates:

School: Memorial HS

Scope of Work: Four Story Classroom Addition, System Upgrades and Renovation Project

Project Manager: David Valerius

Architect/Engineer: Stantec Architects - **Contractor**: Durotech

Status: Project is currently in Construction Phase.



Planning & Construction Updates:

School: Memorial HS



Aerial View of Memorial High School Campus

Planning & Construction Updates:

School: Memorial HS



Architectural Rendering of Mustangs which will be installed during 2022 Winter Break

Planning & Construction Updates:

School: Northbrook HS

Scope of Work: Classroom Additions and Renovation Project

Project Manager: David Valerius

Architect/Engineer: PBK Architects - Contractor: Satterfield & Pontikes

Status: Project is complete. Ribbon Cutting Ceremony held on September 28, 2022.













Spring Branch Independent School District




2022 Bond Updates:

Spring Branch ISD (SBISD) Board of Trustees voted unanimously to call a \$381.6 million bond election to appear on the May 7, 2022 ballot. Complete results show that voters in SBISD approved a \$381.6 million bond referendum (Propositions A & B) with 73 percent of the vote.

Current 2022 Bond Projects Underway

- Valley Oaks ES Addition and Renovation Project
- Agricultural Farm Addition and Renovation Project
- Guthrie Center New Construction/Replacement Campus

2022 Bond Planning Updates:

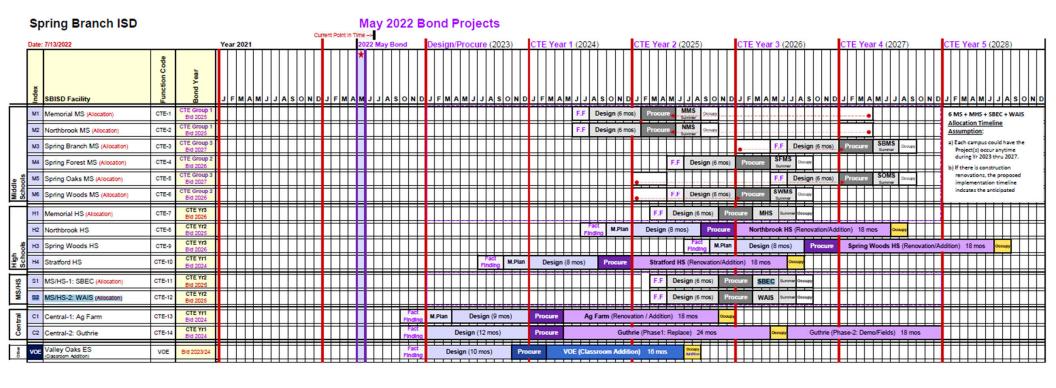



VALLEY OAKS Elementary School Additions

Project Advisory Team
November 2, 2022 3:45pm – 5:00pm
PAT meeting #3

OVERALL PROJECT SCOPE

VALLEY OAKS ES ADDITIONS

CLASSROOM AND CAFETERIA ADDITIONS WHILE THE SCHOOL IS IN OPERATION


OPENING OF FALL 2024





PAT GUIDING PRINCIPLES

We take these with us moving forward





RECAP FROM PAT#2

WE EXPLORED THE 2 OPTIONS BASED ON PAT #1 FEEDBACK





VALLEY OAKS ELEMENTARY SCHOOL ADDITIONS PAT # 2 REVIEW

RECAP FROM PAT#2

Here is what we heard...

- Admin support space provided
- Additional classroom
- · Preferable connection from existing to new
















PAT #2 RECAP

Poll Results

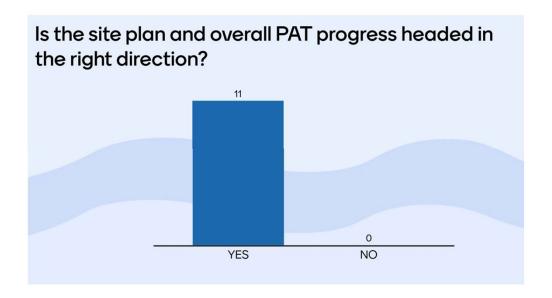

Questions from the Bond Oversight Committee





Thank You

The next quarterly BOC meeting will be held:

February 2023

Dinner will be served at 5:30 pm

Meeting will begin at 6:00 pm

