

CONSTRUCTION UPDATE WICHITA FALLS LEGACY HIGH SCHOOL September 30, 2022

Legend for Areas of Construction -

A - 9th Grade B – Commons C – Admin D – Science E – Cafeteria/Dining F – Fine Arts G – Fine Arts/Aud H – Kitchen J – Arena/Boy Athletics K- Girls Athletics L – Aux Gym/Storm Shelter M – Boys Athletics N – Weight Room P – 12^{th} Grade Q – Classrooms R – Chemistry Labs S- Science Labs T – Open above Commons U – Fine Arts V – Upper Auditorium Classrooms W – Above Arena

WORK IN PROGRESS

For the period covering 9/23/22 through 9/30/22, the following on-site activities were observed:

- Area M & G2 Poured
- Steel Erection @ E Continued
- Steel Erection @ D Underway
- Site Cut & Fill (North End & Detention Pond)
- Grease Trap Installed
- Mason Continuing @ Area F & J

LOOK A HEAD

The next two weeks activities are projected to include:

- Pour Area G3
- Decking @ E & D (Nelson Studs Starting)
- Continue Steel Erection @ D
- Continue RCP @ Detention Pond
- Continue CMU @ F/J/K
- Prep for Paving @ South Parking Lot

SITE AERIAL

Available via Dropbox Link https://bartlettcocke.box.com/s/j73qpuqcm9el76mbf8dhw6pht1hgf2w4





1







CONSTRUCTION UPDATE WICHITA FALLS LEGACY HIGH SCHOOL September 30, 2022



Area G2 Pour



Area M Slab Pour



Continue Cut & Fill Sitework near Construction Office





Area D & E Steel Erection



CMU Ongoing Area F





Continue Electrical Primary Feeder



2



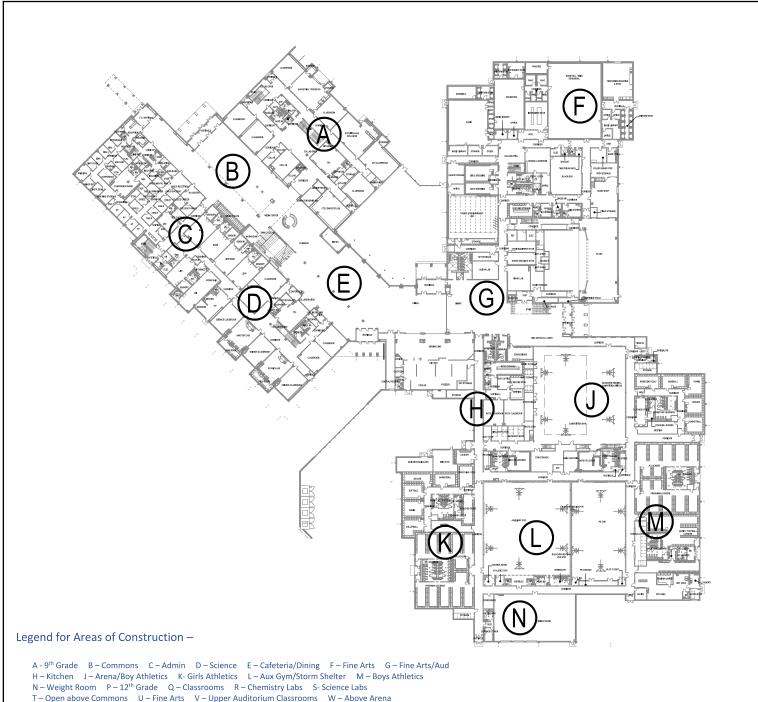



CD TO QC DRAFT COPY ONLY NOT FOR REGULATO APPROVAL, PERMITTI OR CONSTRUCTION

MASTER PLAN • LEVEL

1eet No

A1.1

ACKAGE VOLUME

HICH FOLLOW

12021

1 MASTER PLAN - LEVEL 1

PLAN

