


BOND UPDATE #199

4.7.23


Here's what is going on with our bond projects. Sorry for the delay, but hoped you all enjoyed Spring Break.

Enjoy!
Kristi


1. The press box in the Grandstands now has framed interior walls, and electricians are currently installing the wiring. Sheetrock work will begin once this wiring is completed.
2. Water-resistant wall coverings are nearly finished in the Grandstands' restrooms. Once they are ready, crews can install toilets, sinks and partitions.
3. The ceiling clouds in the corridors around the gym were installed over Spring Break this week. These fixtures reduce ambient noise and enhance the look of the corridors.
4. The gate to the student store in the cafeteria was installed this week. After the final appliances are in place, the store can be opened for use!
5. Sidewalks are now complete in the Commons' courtyard under the covered walkway.
6. Foundation, plumbing and electrical work are all making good progress in the new CTE Wing area. At the rate crews are progressing, they should begin work on the main framework for the structure in early May.
7. Crews have now begun assembling some of the steel framework for the new CTE Wing area.
8. The underground stormwater detention system under the new parent drop-off area is being installed this week. Soon, the entire system will be completed!
9. Activities have now started in preparation for the beginning of the seismic upgrade work in the Performing Arts Center auditorium.
10. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
11. Below is the FHS project timeline as of February 28. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

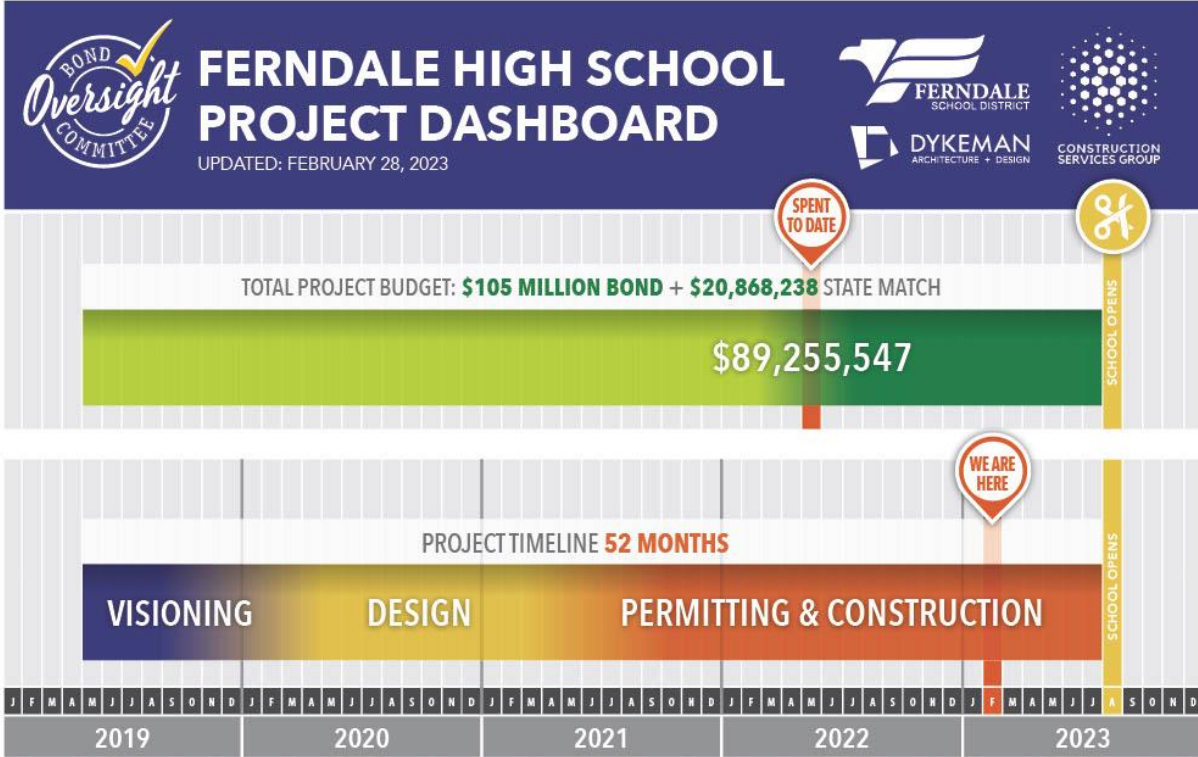

12. Below is a map showing the various components of the new FHS campus and when they'll be completed.

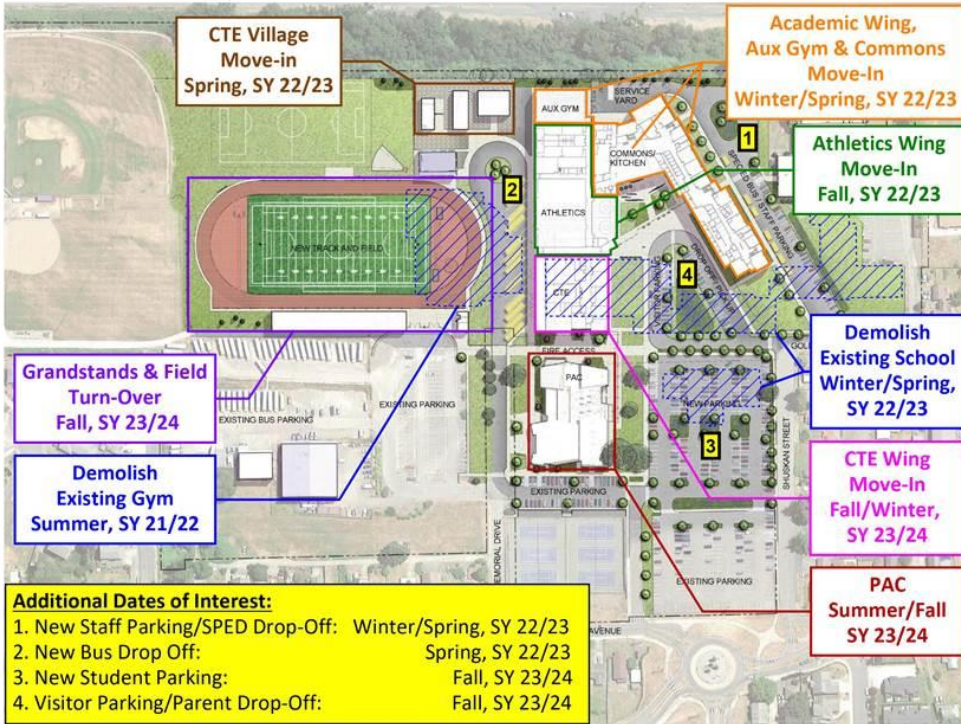

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



Ceiling cloud installation in the corridors around the gym



The student store gate is now in place



The foundation of the CTE Wing is close to completion



The underground rainwater detention system under the new family drop-off area



The PAC Auditorium seating and flooring are covered to protect it during seismic upgrade work
