


# BOND UPDATE #201

4.21.23


Here's what is going on with our bond projects.

Enjoy!  
Kristi


1. Crews are making great progress on our new athletics field – the lights are now completely installed, and Astroturf began to arrive this week for next week's installation. We cannot wait until this field can be used next school year for soccer and football games, graduations, and more. In particular, our FHS track team has been waiting a long time to host a true home meet in Ferndale – due to poor conditions, the old track was unsuitable for meets for years before construction began. This is an exciting time to be a Golden Eagle!
2. Toilets and sinks have now been installed in the Grandstands' restrooms. The toilet partitions will come next.
3. The ticket booth's structural steel was assembled this week. That small building is really starting to take shape.
4. The last of the sidewalks around the existing weight room were poured this week.
5. About 40% of the new CTE Wing's floor slab has now been poured. The rest of the slab should be poured at the end of the next week, and then structural steel assembly will begin.
6. Crews have now installed most of the underground stormwater detention system. The last system on the south side of the facility should be completed over the next few weeks.
7. Construction of the new concrete shear walls in the Performing Arts Center building continued this week. This is part of the building's seismic upgrade and will provide additional lateral stability to the PAC in case of an earthquake.
8. The Ferndale School Board will receive a bond update during their upcoming regular meeting on Tuesday, April 25 at 6 p.m. at Mountain View.
9. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://www.ferndalesd.org)
10. Below is the FHS project timeline as of March 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

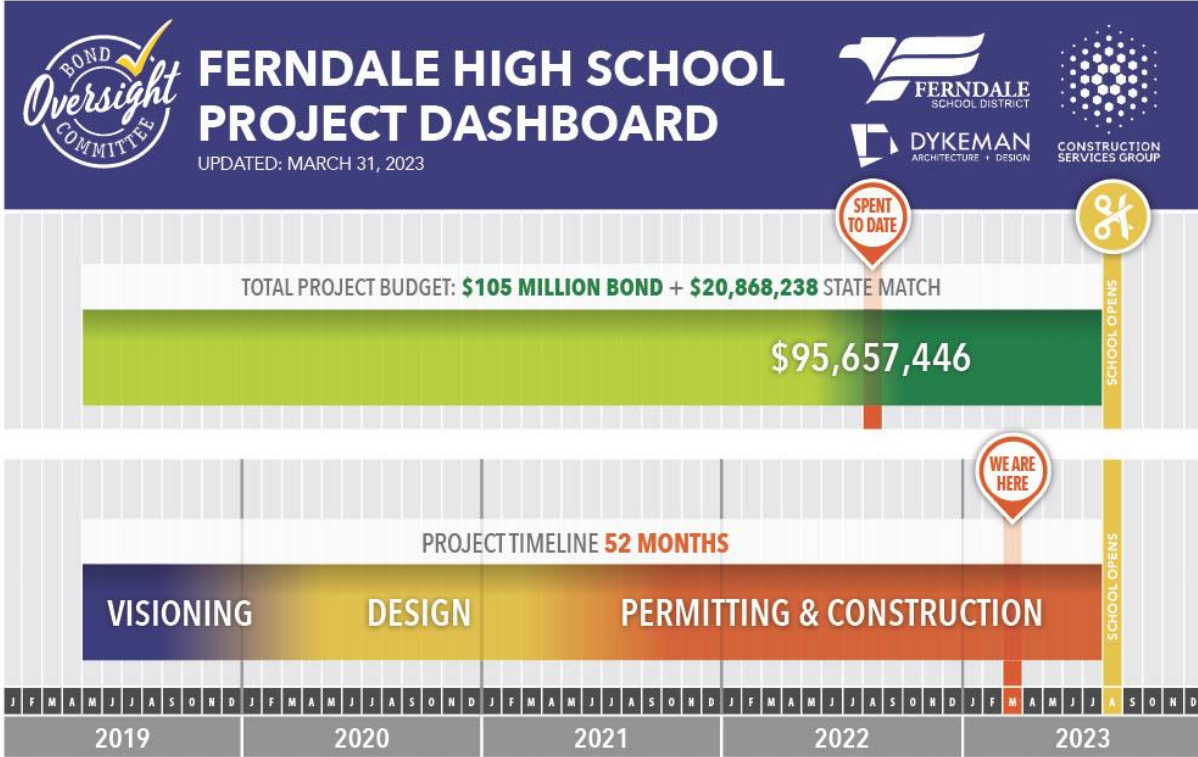

11. Below is a map showing the various components of the new FHS campus and when they'll be completed.

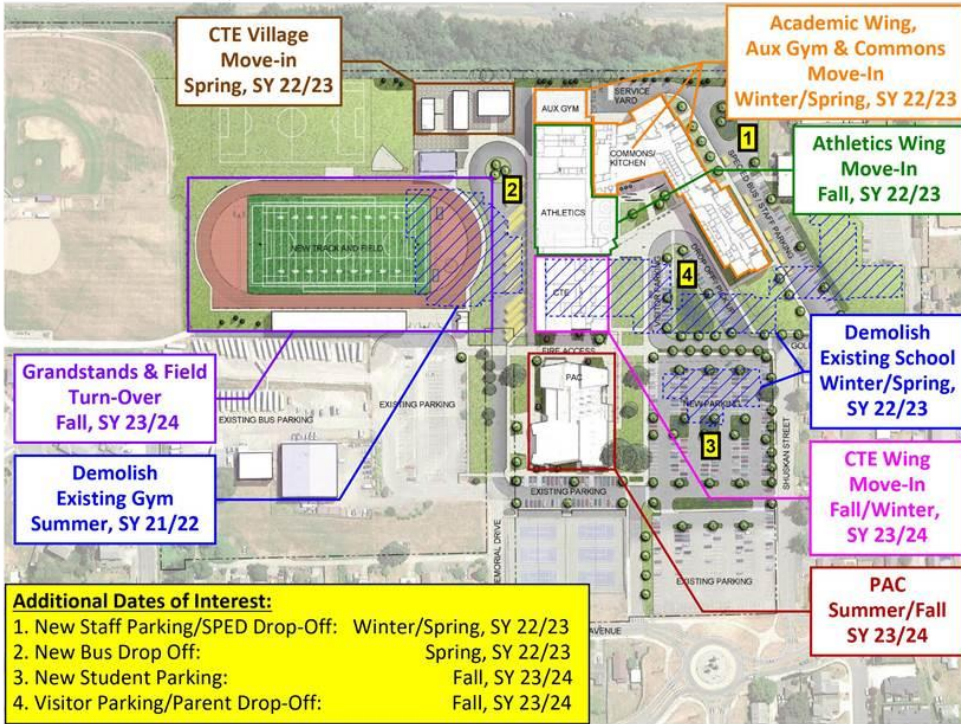

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



Sinks installed in the Grandstands' restrooms



Toilets installed in the Grandstands' restrooms



**Structural steel assembly at the new athletics field's ticket booth**



**New CTE Wing floor slab being poured**



**Underground stormwater detention system's ongoing installation**
