

BOND UPDATE #203


5.5.23

Here's what is going on with our bond projects.



Enjoy!

Kristi

1. Crews are putting the final finishes on the Grandstands' restrooms and concessions. Soon, these areas will be complete!
2. Gravel groundcover was installed this week in-between the existing weight room and the new CTE Village (where the Greenhouse, Agriculture Science class, etc. is located).
3. Crews continue to pour sidewalks around the athletic field in preparation for the new track.
4. The Astroturf is nearly ready at the athletic field – crews put on the finishing touches this week.
5. Roofing work on the ticket booth and covered courtyard canopy (between the Academic Wing and new CTE Wing/Athletic Wing) is now underway. This should be completed over the next couple of weeks.
6. The final prep work in the long jump area has begun.
7. Crews made great progress this week assembling the structural steel for the new CTE Wing. A second crane has been mobilized to speed up the process.
8. Crews continue to install stormwater components around the campus. These need to be in place before final prep work can begin for the new parking areas.
9. Work on the new concrete reinforcement walls in the Performing Arts Center continues.
10. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
11. Below is the FHS project timeline as of March 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

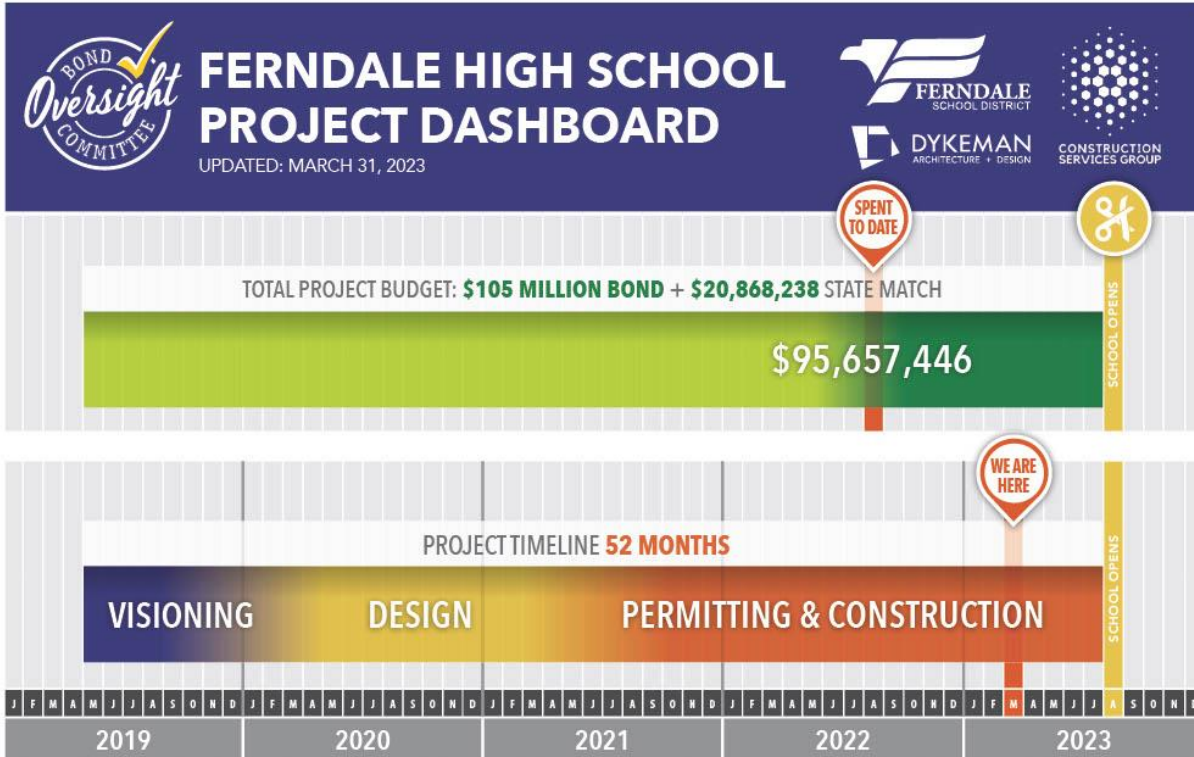

12. Below is a map showing the various components of the new FHS campus and when they'll be completed.

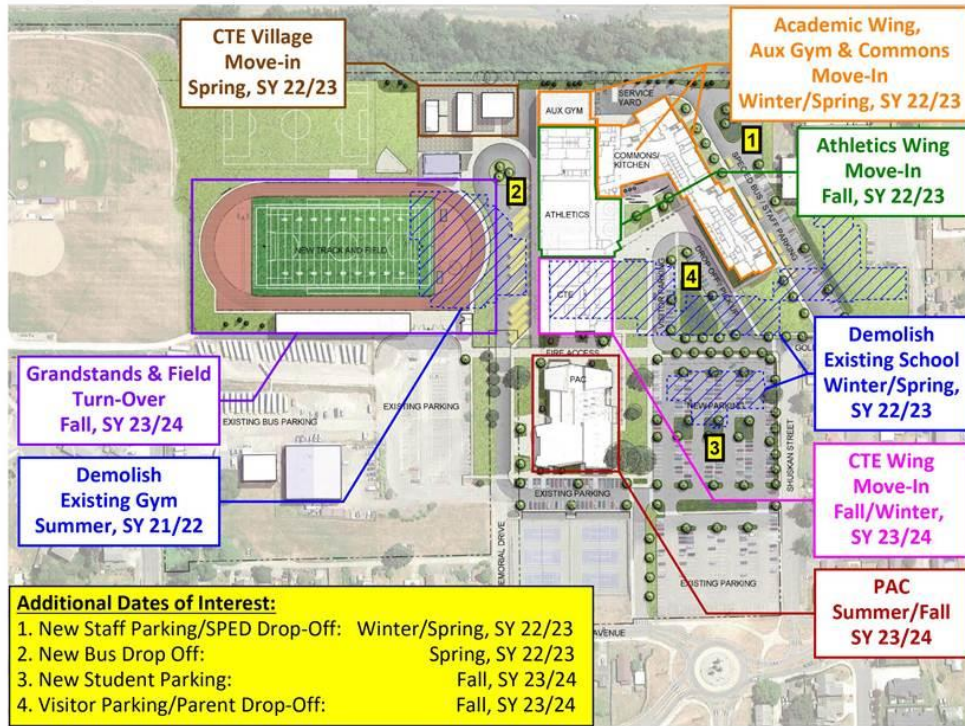

FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues. Have a wonderful weekend!

Kristi



Ground coverings between the existing weight room and CTE Village were installed this week



Athletic field turf is almost complete



This area at the north end of the new Grandstands will eventually become the long jump pits



The CTE Wing structural steel is making good progress



Concrete structures being installed for the underground stormwater system



Footings for the new shear walls in the Performing Arts Center
