


SCHOOL DISTRICT



School Site Improvement Projects

Business Services

Regular Board Meeting October 27, 2022



PROJECT COMPLETE LIST

2022-2023




Site	Item Description	Funding Source	Completed Date
Willow	Bottle Filling Stations	Adult ED	7/2022
Sparks ES	Carpet – Classroom 12	Facilities	7/2022
La Puente HS	Dream Center	Facilities	8/2022
Workman HS	Exterior Lighting at Lobo Lane	Facilities	8/2022
District Office	Flooring and Lights – Board Room	Facilities	8/2022
Lassalette	Front Exterior Turf	Facilities	7/2022
Sparks MS	Front Exterior Turf	Facilities	10/2022
Workman HS	Gym Restrooms ADA Upgrades	Facilities	7/2022
La Puente HS	Kitchen	COPS/Facilities	9/2022
Wing Lane	Parking Lot Striping	Facilities	8/2022
La Puente HS	Pool	COPS/Facilities	9/2022
Workman HS	Railing	Facilities	10/2022
Workman HS	Additional Exterior Lighting at Lobo Lane	Facilities	10/2022



Projects Completed as of October 27, 2022

La Puente HS – Dream Center New Carpet and Paint (8/2022)

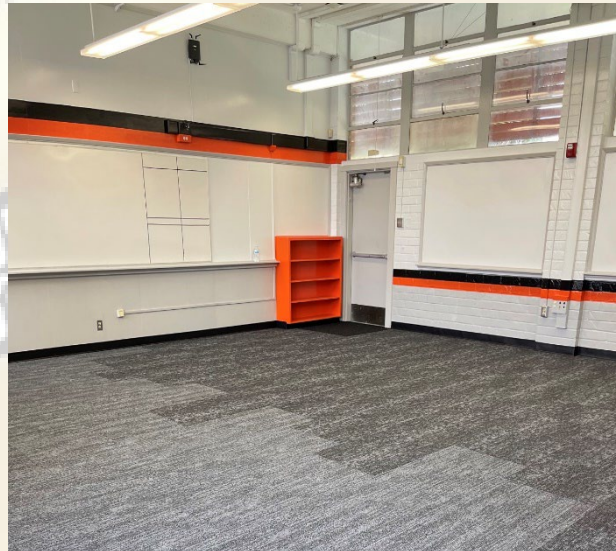

Projects Completed as of October 27, 2022


NEW!

Sparks MS – Front Exterior Turf (10/2022)




Projects Completed as of October 27, 2022

Workman HS – New Railing (10/2022)

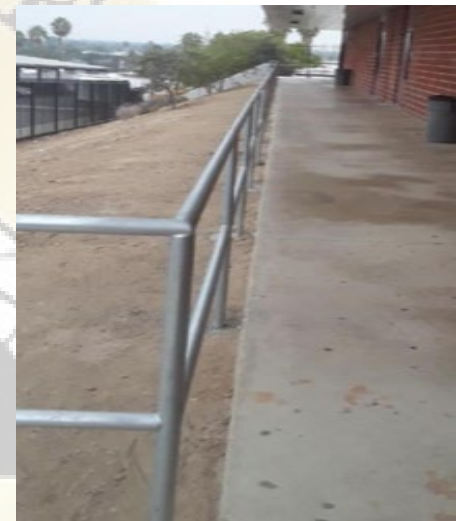

Projects Completed as of October 27, 2022

**Workman HS – – Additional Lights for Lobo Lane
(10/2022)**

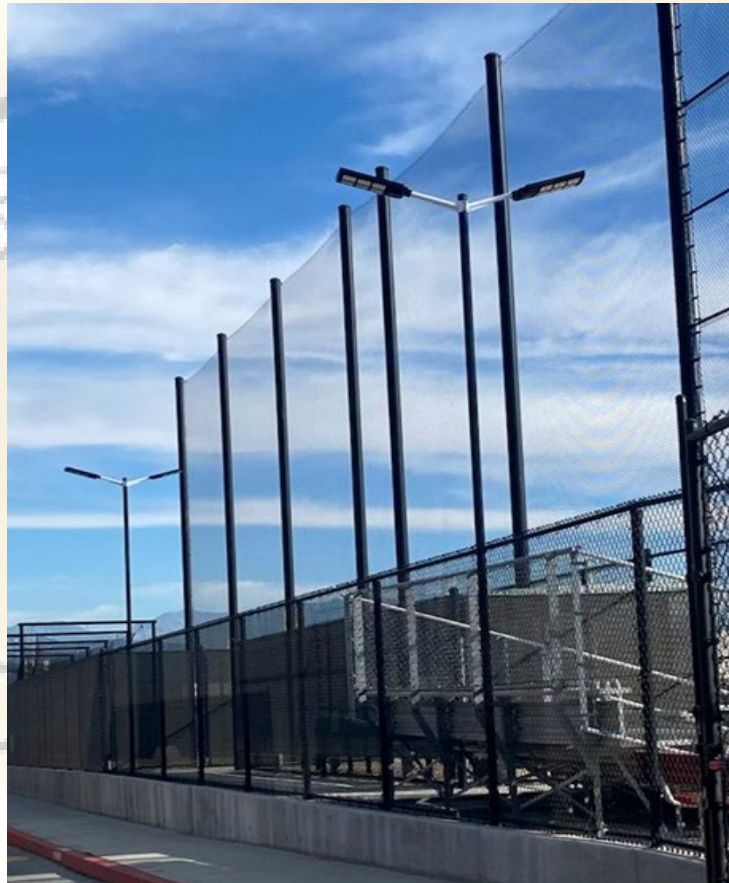

Projects In Progress




2022-2023



Projects In Progress as of October 27, 2022

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending (Currently Working on CEQA)	Pending	Various - Estimate Cost \$18 M	8/2024
Sparks ES, Lassalette, Cedarlane, Baldwin ES, Fairgrove	Blacktop Asphalt & Striping	NA	NA	Pending	Pending	Facilities	12/31/2022
Wedgeworth	K-5 Permanent School	Complete	Complete	Complete	9/2022	COPS	8/2024
District Office (C wing)	HVAC Replacement, Lighting, Flooring and Fire Alarm	Complete	NA	Complete	In Progress	Facilities	3/2023
Sierra Vista (Child Dev)	Flooring Replacement	NA	NA	Complete	In Progress	Head Start	12/15/2022
La Puente HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Project Funds	11/4 /2022
Dibble AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Dibble AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Los Altos HS	Path of Travel – ADA Issues	Complete	Complete	Pending Award	Pending	Facilities	12/15/2022
Cedarlane	Front Exterior Improvements	NA	NA	Pending	Pending	Facilities	12/31/2022

Los Altos High School ADA Improvements

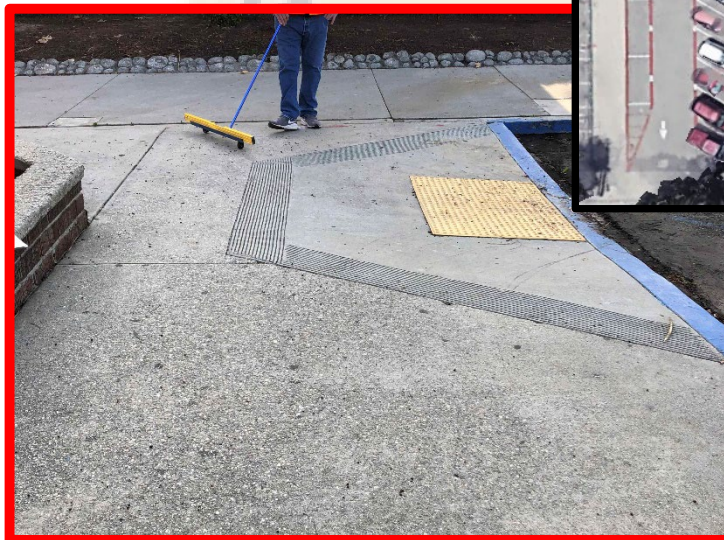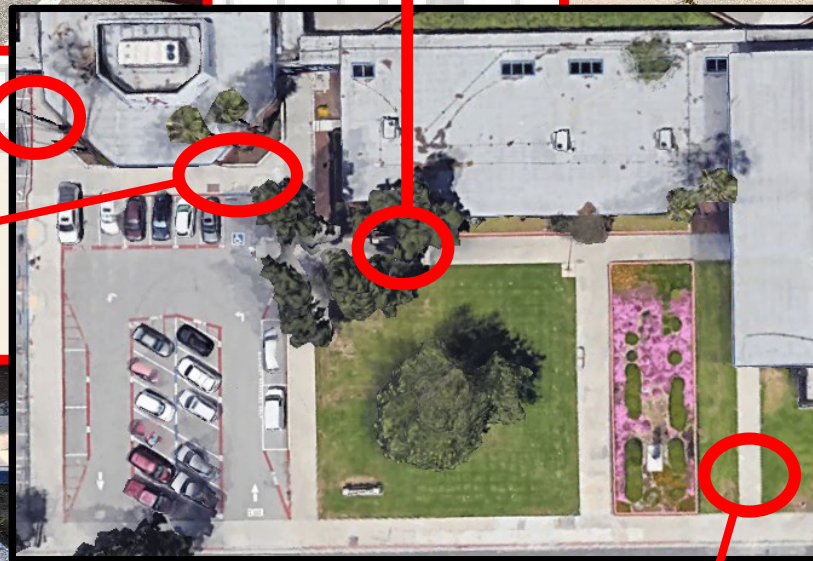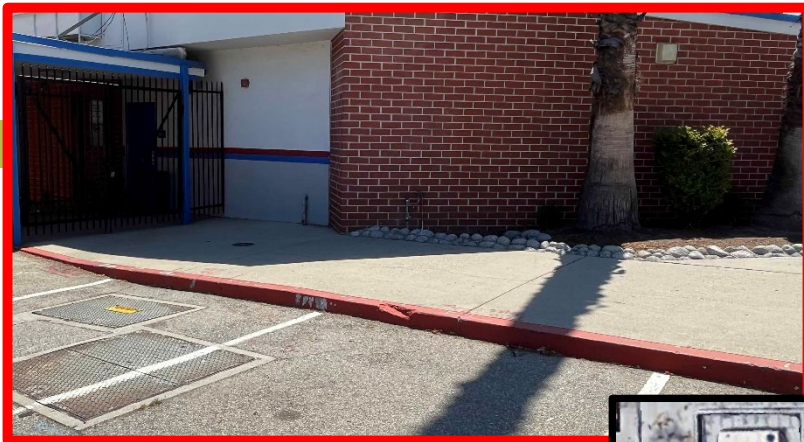



Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Pending	Complete	TBD	TBD
Kwis Elementary	Baseball Fields (Two Youth)	Complete	Pending	Pending	1/2023	3/2024

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Center for the Performing Arts	New Performing Arts Center with approx. 500 seat capacity	In Progress	Pending	Pending		2/2025
Districtwide	HVAC System Replacements	Pending	Pending	Pending		



Next Report – November 17, 2022
