

# HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT

## La Puente Quad

HACIENDA LA PUENTE ADULT EDUCATION  
- Hudson  
- Willow AS  
-Student Service Center

## Los Altos Quad

Palm Canyon

## Wilson Quad

MESA ROBLES SCHOOL  
District Office

## Workman Quad

VALINDA VALIANTS

## School Site Improvement Projects

## Business Services

Regular Board Meeting  
September 22, 2022



# PROJECT COMPLETE LIST 2022-2023



Site	Item Description	Funding Source	Completed Date
Willow	Bottle Filling Stations	Adult ED	7/2022
Sparks ES	Carpet – Classroom 12	Facilities	7/2022
<b>La Puente HS</b>	<b>Dream Center</b>	<b>Facilities</b>	<b>8/2022</b>
Workman HS	Exterior Lighting at Lobo Lane	Facilities	8/2022
<b>District Office</b>	<b>Flooring and Lights – Board Room</b>	<b>Facilities</b>	<b>8/2022</b>
Lassalette	Front Exterior Turf	Facilities	7/2022
Workman HS	Gym Restrooms ADA Upgrades	Facilities	7/2022
<b>La Puente HS</b>	<b>Kitchen</b>	<b>COPS/Facilities</b>	<b>9/2022</b>
Wing Lane	Parking Lot Striping	Facilities	8/2022
<b>La Puente HS</b>	<b>Pool</b>	<b>COPS/Facilities</b>	<b>9/2022</b>

# Projects Completed as of September 22, 2022


**NEW!**

## Workman HS – Gym Restrooms ADA Upgrades (7/2022)



# Projects Completed as of September 22, 2022

## La Puente HS – Pool (8/2022)

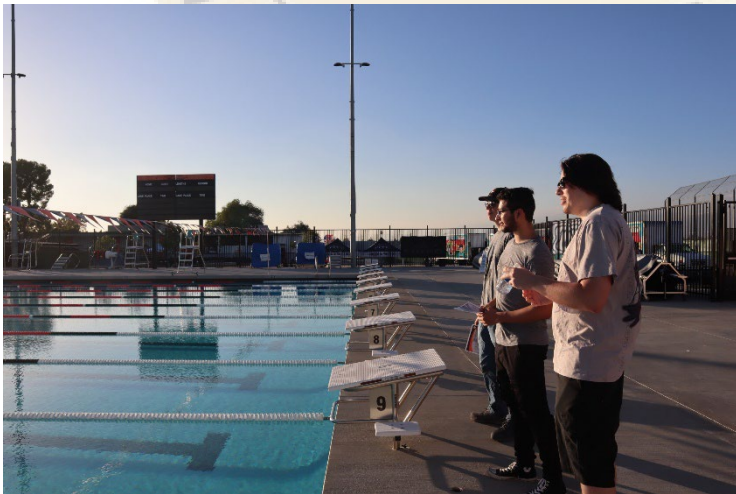

# Projects Completed as of September 22, 2022

**NEW!**

## La Puente HS –Kitchen (8/2022)



# Projects In Progress

2022-2023



# Projects In Progress as of September 22, 2022

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending (Currently Working on CEQA)	Pending	Various - Estimate Cost \$18 M	8/2024
Sparks ES, Lassalette, Cedarlane, Baldwin ES, Fairgrove	Blacktop Asphalt & Striping	NA	NA	Pending	Pending	Facilities	12/31/2022
Wedgeworth	K-5 Permanent School	Complete	Complete	Complete	9/2022	COPS	8/2024
District Office (C wing)	HVAC Replacement, Lighting, Flooring and Fire Alarm	Complete	NA	Complete	In Progress	Facilities	3/2023
Sierra Vista (Child Dev)	Flooring Replacement	NA	NA	Complete	Pending	Program	10/30/2022
La Puente HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Prop 39	10/15/2022
Dibble AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	HVAC Replacement	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Willow AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Dibble AS	Fire Alarm Installation	Complete	NA	Complete	In Progress	Adult Ed	12/2023
Los Altos HS	Path of Travel – ADA Issues	Complete	Complete	In Progress	Pending	Facilities	11/30/2022



# Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Pending	Complete	TBD	TBD

## Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Center for the Performing Arts	New Performing Arts Center with approx. 500 seat capacity	In Progress	Pending	Pending		2/2025
Districtwide	HVAC System Replacements	Pending	Pending	Pending		
Kwis Elementary	Baseball Fields (Two Youth)	Complete	Pending	Pending	1/2023	3/2024





**Next Report – October 27, 2022**
