



HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Business Services


Regular Board Meeting
August 25, 2022



PROJECT COMPLETE LIST 2022-2023



| Site | Item Description | Funding Source | Completed Date |
|------------|--------------------------------|----------------|----------------|
| Willow | Bottle Filling Stations | Adult ED | 7/2022 |
| Sparks ES | Carpet – Classroom 12 | Facilities | 7/2022 |
| Lassalette | Front Exterior Turf | Facilities | 7/2022 |
| Workman HS | Gym Restrooms ADA Upgrades | Facilities | 7/2022 |
| Wing Lane | Parking Lot Striping | Facilities | 8/2022 |
| Workman HS | Exterior Lighting at Lobo Lane | Facilities | 8/2022 |

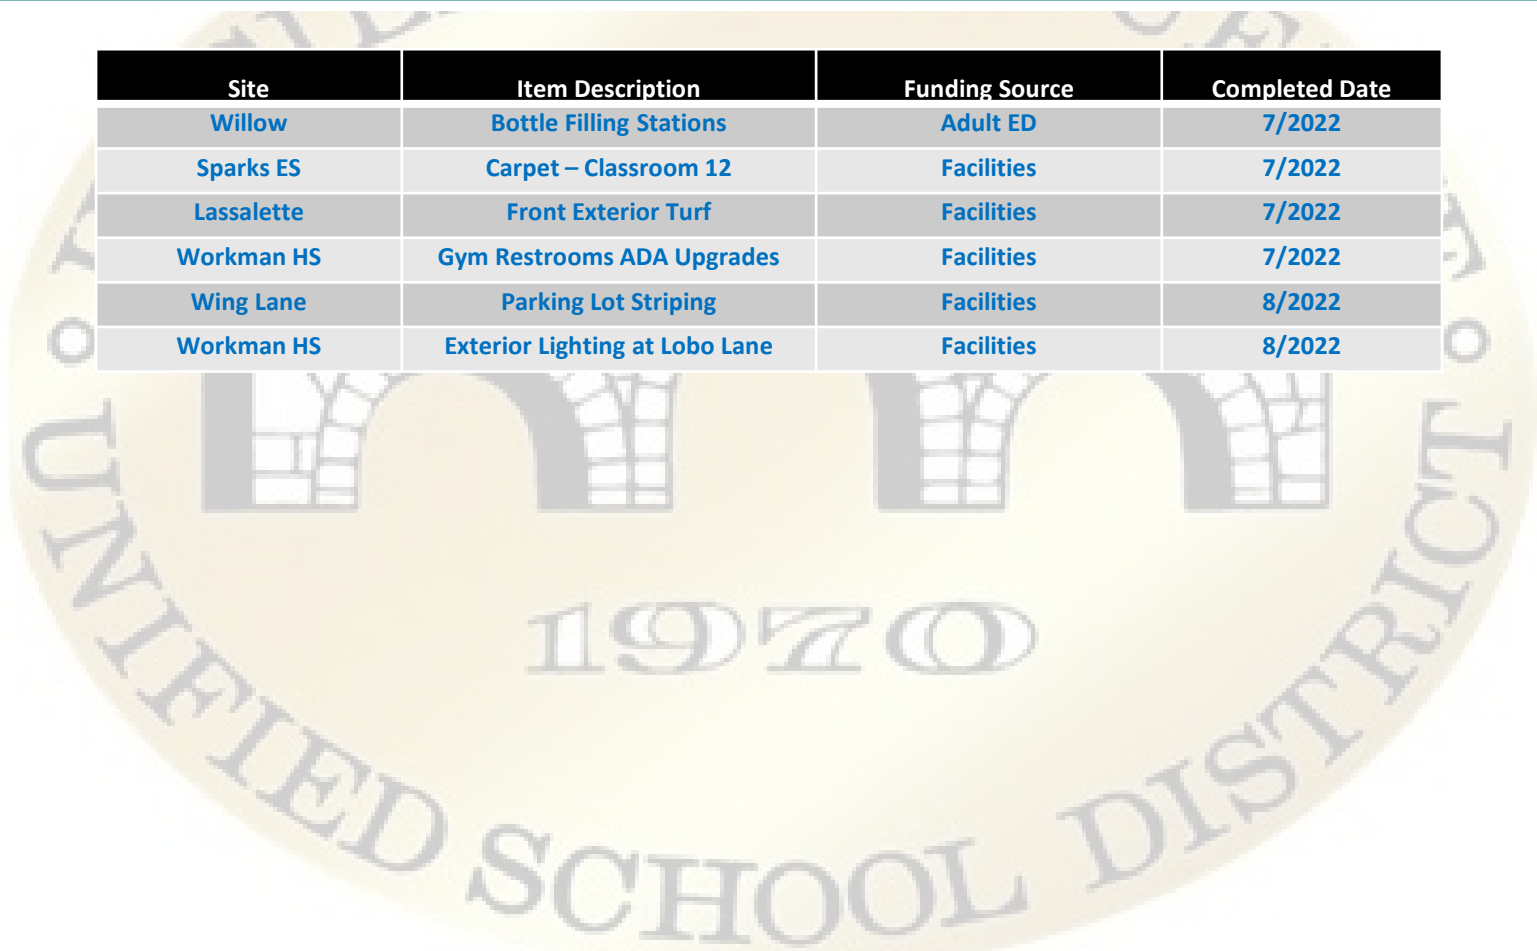

Projects Completed as of August 25, 2022

Temporary HVAC Units Have Been Installed in the Los Altos High School Gym (8/2022)



Projects Completed as of August 25, 2022



Willow – 3 Bottle Filling Stations (7/2022)



Projects Completed as of August 25, 2022

Exterior Lighting at Lobo Lane

(8/2022)

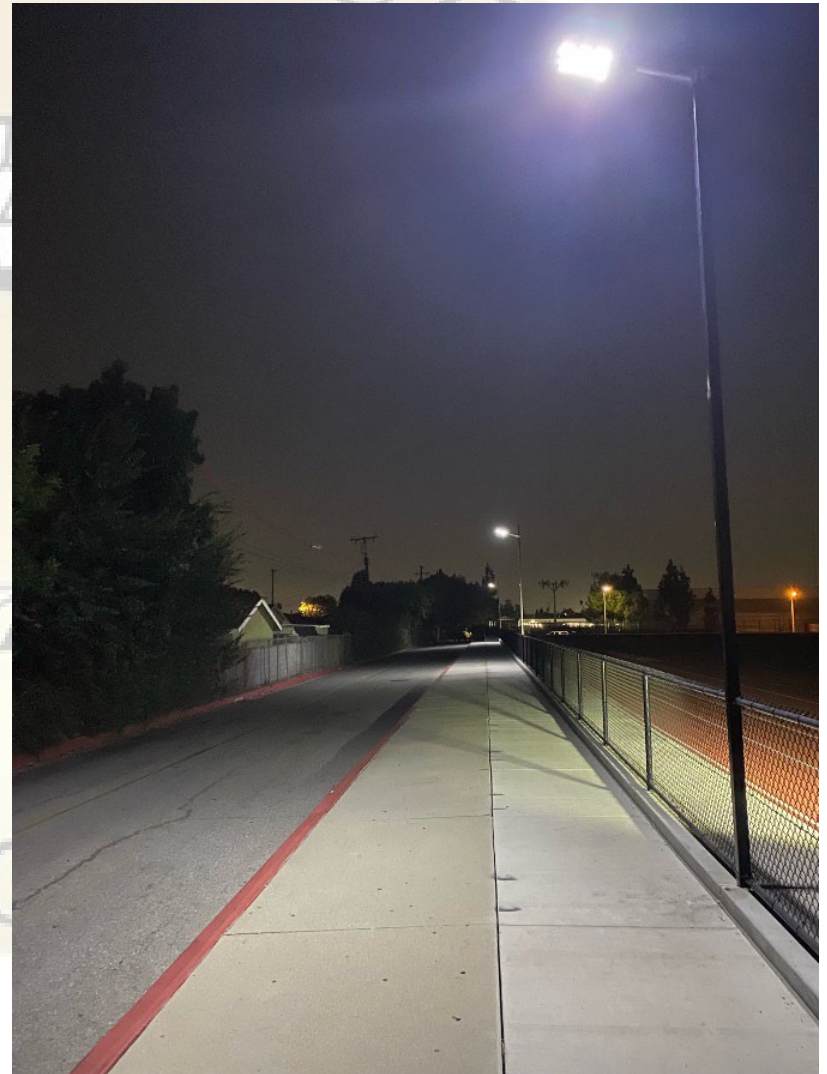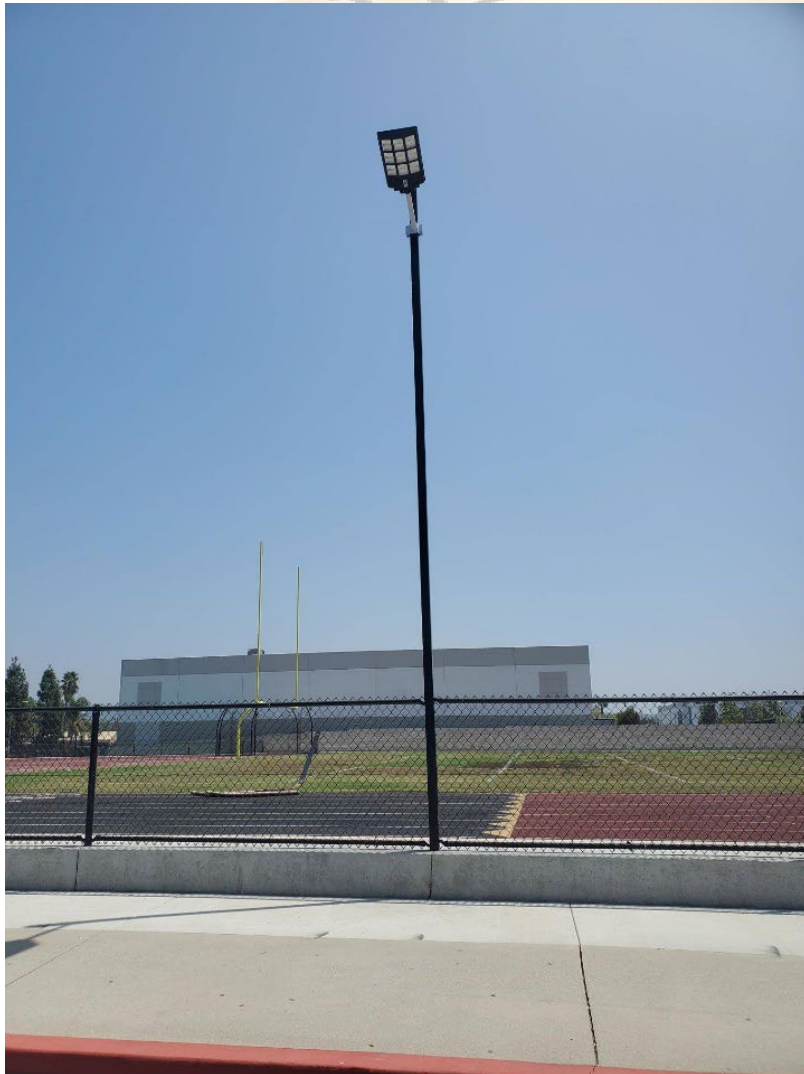

Projects Completed as of August 25, 2022

Lassalette – Front Exterior Turf (7/2022)



Projects Completed as of August 25, 2022

Wing Lane – Parking Lot Striping (8/2022)



Projects In Progress

2022-2023



Projects In Progress as of August 25, 2022

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Completion Date |
|---|--|-----------------|--------------|--|-------------|---------------------------------|------------------------|
| La Puente HS | New Kitchen | Complete | Complete | Complete | In Progress | Facilities & COP | 8/31/2022 |
| La Puente HS | Pool & Locker Room Project | Complete | Complete | Complete | In Progress | Facilities & COP | 8/31/2022 |
| Workman HS | Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete) | Complete | Complete | Pending (Currently Working on CEQA) | Pending | Various - Estimate Cost \$16.5M | 8/2024 |
| Sparks ES, Lassalette, Cedarlane, Baldwin ES, Fairgrove | Blacktop Asphalt & Striping | NA | NA | Pending | Pending | Facilities | 10/31/2022 |

La Puente HS - Updates



Contractors removing construction trailers



Kitchen – Equipment being installed

Projects In Progress as of August 25, 2022



Pool – Water!!!

Projects In Progress as of August 25, 2022

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Completion Date |
|--------------------------|---|-----------------|--------------|-------------|-------------|----------------|------------------------|
| Wedgeworth | K-5 Permanent School | Complete | Complete | Complete | 9/2022 | COPS | 8/2024 |
| District Office (C wing) | HVAC Replacement, Lighting, Flooring and Fire Alarm | Complete | NA | Pending | Pending | Facilities | 3/2023 |
| Sierra Vista (Child Dev) | Flooring Replacement | NA | NA | Complete | Pending | Program | 9/30/2022 |
| La Puente HS | Gym & Locker Room HVAC | Complete | Complete | Complete | In Progress | Prop 39 | 10/15/2022 |
| Dibble AS | HVAC Replacement | Complete | NA | Complete | Pending | Adult Ed | 12/2023 |
| Willow AS | HVAC Replacement | Complete | NA | Complete | Pending | Adult Ed | 12/2023 |
| Willow AS | Fire Alarm Installation | Complete | NA | Complete | Pending | Adult Ed | 12/2023 |
| Dibble AS | Fire Alarm Installation | Complete | NA | Complete | Pending | Adult Ed | 12/2023 |
| Los Altos HS | Path of Travel – ADA Issues | Complete | Pending | Pending | TBD | Facilities | 10/31/2022 |



Projects with Division of State Architect (DSA) Waiting on Approval

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Est. Construct Start | Target Completion Date |
|--------------|--|-----------------|--------------|-------------|----------------------|------------------------|
| Los Altos HS | Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed) | Complete | Pending | Complete | TBD | TBD |

Projects in Design

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Est. Construct Start | Target Completion Date |
|--------------------------------|---|-----------------|--------------|-------------|----------------------|------------------------|
| Center for the Performing Arts | New Performing Arts Center with approx. 500 seat capacity | In Progress | Pending | Pending | | 2/2025 |
| Districtwide | HVAC System Replacements | Pending | Pending | In Review | | |
| Kwis Elementary | Baseball Fields (Two Youth) | In Progress | Pending | Pending | 11/2022 | 3/2024 |

The background features a large, faint watermark of the Unifield School District logo. The logo is circular and contains the text "UNIFIELD SCHOOL DISTRICT" around the perimeter and "1970" at the bottom. In the center is a stylized archway with three smaller arches underneath. A horizontal bar with a green-to-yellow gradient is positioned at the top of the page.

Next Report – September 22, 2022
