


SCHOOL DISTRICT

La Puente Quad




Los Altos Quad

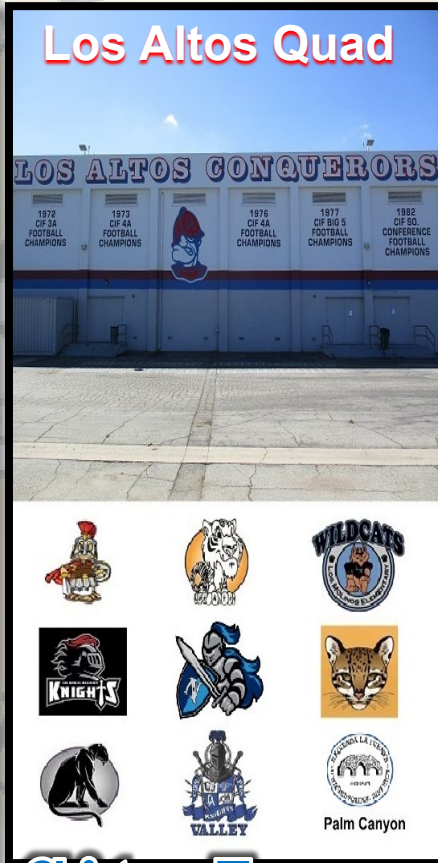

Wilson Quad



Workman Quad

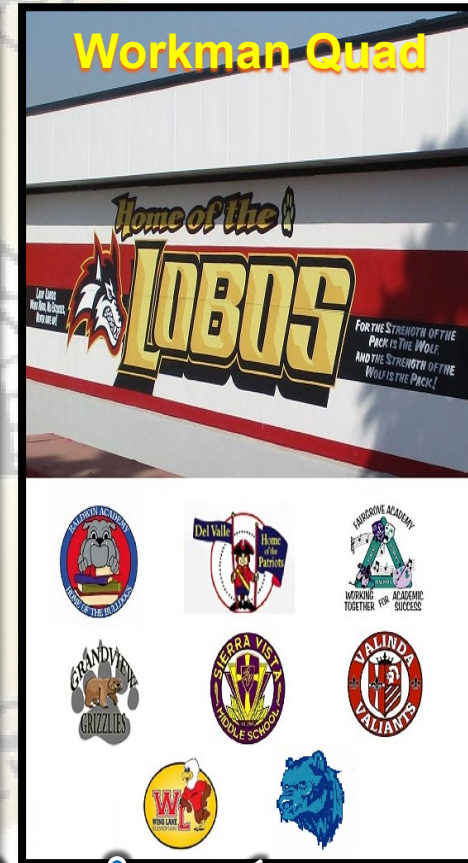

School Site Improvement Projects

Business Services

Board Meeting
July 21, 2022



Regular Board Meeting

July 21, 2022



PROJECT COMPLETE LIST

2021-2022



Site	Item Description	Funding Source	Completed Date
Willow Center	Conference Center Fence	Adult Ed	12/2021
Orange Grove MS	Flooring – Administration Flooring	Facilities	4/2022
Baldwin	Flooring – P12	Facilities	4/2022
Workman HS	Front Entry Concrete	Facilities	12/2021
Wilson HS	Gym & Locker Room HVAC	Prop 39	10/2021
Workman HS	Gym & Locker Room HVAC	Prop 39	4/2022
La Puente HS	Gym Lights Upgrade	Facilities	11/2021
Workman HS	Gym Lights Upgrade	Facilities	11/2021
Workman HS	Media Center Flooring & Paint	Donation	11/2021
Grandview	Office Modular Furniture	Facilities	11/2021
Grandview	Roofing	Facilities	12/2021
Los Altos	Roofing	Facilities	12/2021
Los Altos HS	Solar Panel Arrays	Power Purchase Agreement	11/2021
Wilson HS	Solar Panel Arrays	Power Purchase Agreement	12/2021
District Office	Solar Panel Arrays	Power Purchase Agreement	10/2021
La Puente HS	Solar Panel Arrays	Power Purchase Agreement	1/2022
Willow AS	Solar Panel Arrays	Power Purchase Agreement	1/2022
Workman HS	Solar Panel Arrays	Power Purchase Agreement	11/2021

PROJECT COMPLETE LIST 2021-2022



Site	Item Description	Funding Source	Completed Date
Workman HS	Pool Coping Repairs	Facilities	6/2022
Willow	South Conference Room Flooring	Adult ED	3/2022
Valinda	Trash Bin Enclosure	Facilities	3/2022
Grazide	Tree Barrier	Facilities	11/2021
Bixby	Wedgeworth Interim Housing	Project	12/2021
Cedarlane Academy	PA System Installation	Deferred Maintenance	6/2022
Workman ES	PA System Installation	Deferred Maintenance	6/2022
Wedgeworth	Phase I - Kinder Portable Relocation	Project COP	6/2022

Projects Completed as of July 21, 2022



Baldwin – New Flooring P12 (4/6/2022)



Projects Completed as of July 21, 2022




Workman HS – Pool Coping Repairs (6/24/2022)



Projects Completed as of July 21, 2022



Workman HS Gym & Locker HVAC (4/22/2022)

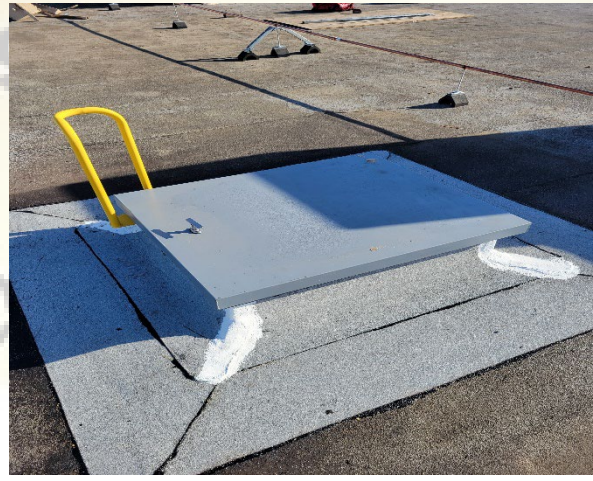

Projects In Progress



Projects In Progress as of July 21, 2022

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
La Puente HS	New Kitchen (including exterior hardscape)	Complete	Complete	Complete	In Progress	Facilities & COP	8/20/2022
La Puente HS	Pool & Locker Room Project	Complete	Complete	Complete	In Progress	Facilities & COP	8/20/2022
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending (Currently Working on CEQA)	Pending	Various - Estimate Cost \$16.5M	8/2024


La Puente HS - Updates

Kitchen – Started Installation of the Storefront Window Panels



Pool – Finished Install of Exterior Tiles

Locker Room – Plastered the Exterior of the Locker Building

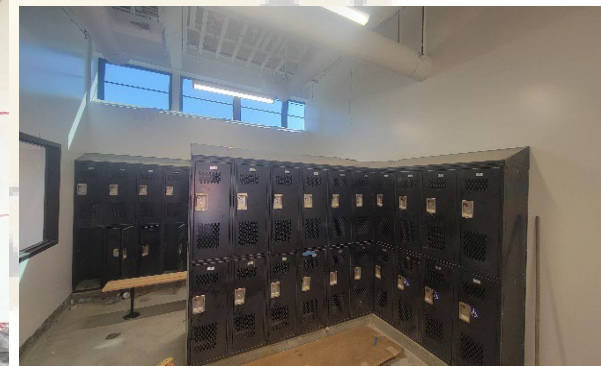

Projects In Progress as of July 21, 2022

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Wedgeworth	K-5 Permanent School	Complete	Complete	Pending Award	9/2022	COPS	8/2024
District Office (C wing)	HVAC Replacement, Lighting, Flooring and Fire Alarm	Complete	NA	Pending	Pending	Facilities	3/2023
Sierra Vista (Child Dev)	Flooring Replacement	NA	NA	Complete	Pending	Program	8/30/2022
Workman HS	Gym Restroom ADA Upgrades	Complete	Complete	Complete	In Progress	Facilities	8/30/2022
Lassalette	Front Exterior Turf	NA	NA	Complete	Pending	Facilities	7/22/2022
La Puente HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Prop 39	10/12/2022
Dibble AS	HVAC Replacement	Complete	NA	Complete	Pending	Adult Ed	12/2023
Willow AS	HVAC Replacement	Complete	NA	Complete	Pending	Adult Ed	12/2023
Willow AS	Fire Alarm Installation	Complete	NA	Pending	Pending	Adult Ed	12/2023
Dibble AS	Fire Alarm Installation	Complete	NA	Pending	Pending	Adult Ed	12/2023



Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC	Complete	Pending	Complete	TBD	TBD

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Center for the Performing Arts	New Performing Arts Center with approx. 500 seat capacity	In Progress	Pending	Pending		2/2025
Districtwide	HVAC System Replacements	Pending	Pending	In Review		
Kwis Elementary	Baseball Fields (Two Youth)	In Progress	Pending	Pending	11/2022	3/2024



Next Report – August 25, 2022
