


SCHOOL DISTRICT

La Puente Quad




Los Altos Quad

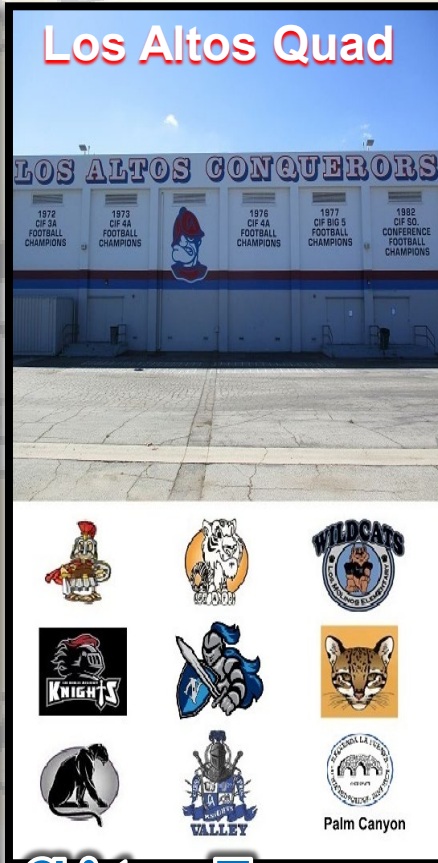

Wilson Quad



Workman Quad

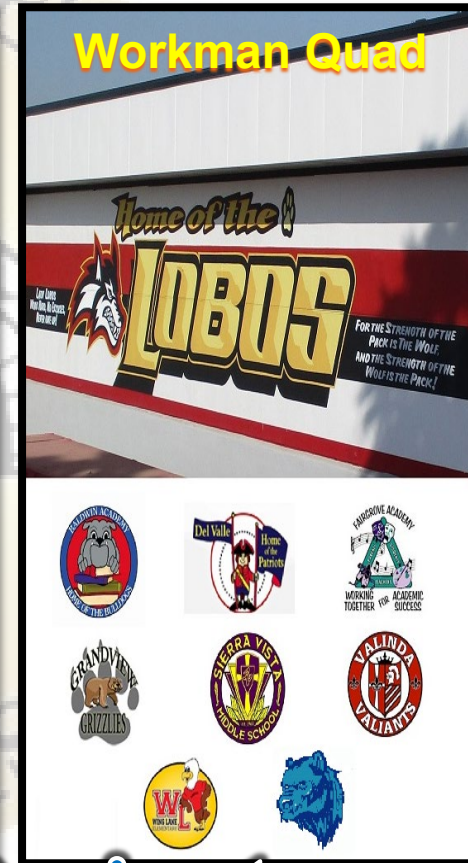

School Site Improvement Projects

Business Services

Regular Board Meeting

March 24, 2022



PROJECT COMPLETE LIST



Site	Item Description	Funding Source	Completed Date
Willow Center	Conference Center Fence	Adult Ed	12/2021
Workman HS	Front Entry Concrete	Facilities	12/2021
Grandview	Roofing	Facilities	12/2021
Los Altos	Roofing	Facilities	12/2021
Willow	South Conference Room Flooring	Adult ED	3/1/2022
Bixby	Wedgeworth Interim Housing	Project	12/2021

Projects Completed as of March 24, 2022

NEW!

Willow South Conference Center Flooring (3/1/2022)



Projects In Progress

2021-2022





Projects In Progress as of March 24, 2022

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
La Puente HS	New Kitchen (including exterior hardscape)	Complete	Complete	Complete	In Progress	Facilities & COP	8/20/2022
La Puente HS	Pool & Locker Room Project	Complete	Complete	Complete	In Progress	Facilities & COP	8/20/2022
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending (Currently Working on CEQA)	Pending	Various - Estimate Cost \$16.5M	12/2023
Workman HS	Gym & Locker Room HVAC	Complete	Complete	Complete	Prop 39	Prop 39	3/30/2022
Dibble AS	HVAC Replacement	Complete	NA	Pending	Pending	Adult Ed	6/2023
Willow AS	HVAC Replacement	Complete	NA	Pending	Pending	Adult Ed	6/2023
Willow AS	Fire Alarm Installation	Complete	NA	Pending	Pending	Adult Ed	6/2023



La Puente HS Kitchen – Aircurtain Installed

La Puente HS Pool – Irrigation Pipe Lay Down

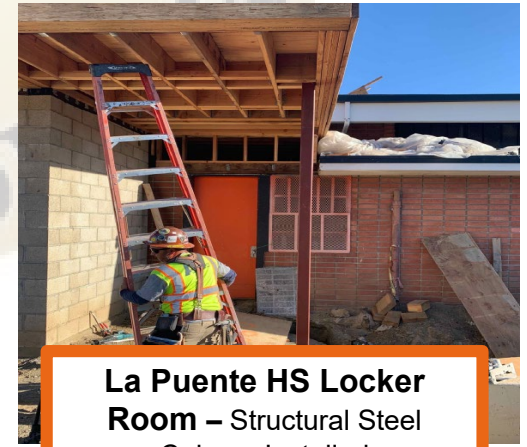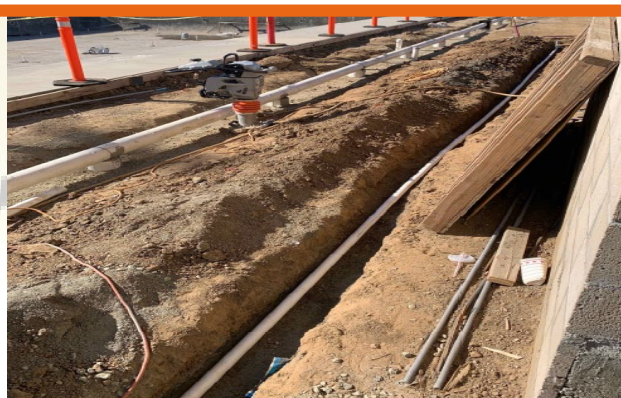

La Puente HS Locker Room – Structural Steel Column Installed

Projects In Progress as of March 24, 2022

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Wedgeworth	Kinder Interim Housing	Complete	Complete	Complete	In Progress	Project COP	4/20/2022
District Office (C wing)	HVAC Replacement, Lighting, Flooring and Fire Alarm	Complete	NA	Pending	Pending	Facilities	1/2023
Sierra Vista (Child Dev)	Flooring Replacement	NA	NA	Complete	Pending	Program	6/30/2022
Workman HS	Gym Restroom ADA Upgrades	Complete	Complete	Complete	Pending	Facilities	6/30/2022

Wedgeworth Kinder Portable Relocation – Grading Underway





Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Wedgeworth	K-5 Permanent School	Complete	In Progress (Revisions for K-5 & Single Story Pending Approval)	In Progress	10/2022	08/2024
La Puente HS	Gym & Locker Room HVAC	Complete	Pending	Complete	TBD	Approx. 3 months
Los Altos HS	Gym & Locker Room HVAC	Complete	Pending	Complete	TBD	TBD

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Performing Arts Center	New Performing Arts Center with approx. 500 seat capacity	In Progress		Pending		
Districtwide	HVAC System Replacements	Pending		Pending		
Kwis Elementary	Baseball Fields	In Progress		Pending	11/2022	8/2023



Next Report – May 5, 2022
