
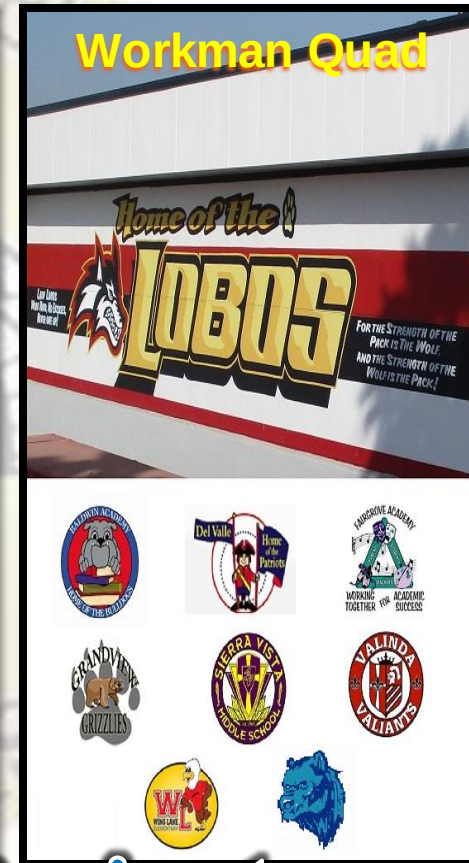


SCHOOL DISTRICT

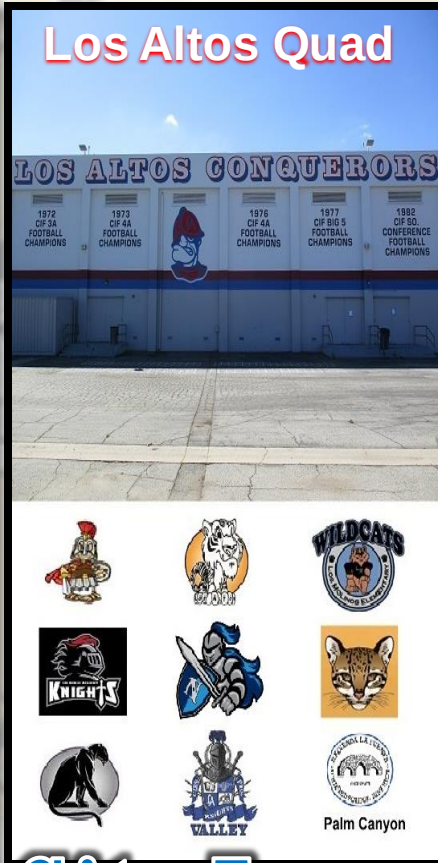

School Site Improvement Projects

Business Services

Regular Board Meeting

February 24, 2022



PROJECT COMPLETE LIST



2

Site	Item Description	Funding Source	Completed Date
Willow Center	Conference Center Fence	Adult Ed	12/2021
Workman HS	Front Entry Concrete	Facilities	12/2021
Wilson HS	Gym & Locker Room HVAC	Prop 39	10/2021
La Puente HS	Gym Lights Upgrade	Facilities	11/2021
Workman HS	Gym Lights Upgrade	Facilities	11/2021
Workman HS	Media Center Flooring & Paint	Donation	11/2021
Willow	MPR Floor Repair	Adult ED	11/2021
Grandview	Office Modular Furniture	Facilities	11/2021
Grandview	Roofing	Facilities	12/2021
Los Altos	Roofing	Facilities	12/2021
Grazide	Tree Barrier	Facilities	11/2021
Bixby	Wedgeworth Interim Housing	Project	12/2021

3

Projects In Progress

2021-2022



Projects In Progress as of February 24, 2022

4

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Willow AS	Conference (South) Room Flooring	Complete	N/A	Complete	In Progress	Adult Ed.	2/28/2022
La Puente HS	New Kitchen (including exterior hardscape)	Complete	Complete	Complete	In Progress	Facilities & COP	4/30/2022
La Puente HS	Pool & Locker Room Project	Complete	Complete	Complete	In Progress	Facilities & COP	5/20/2022
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending	Pending	Various - Estimate Cost \$16.5M	12/2023
Workman HS	Gym & Locker Room HVAC	Complete	Complete	Complete	Prop 39	Prop 39	3/1/2022



La Puente HS Kitchen – Metal Deck is Being Spray Painted



La Puente HS Pool – Structural Pony Wall Completed



Projects with Division of State Architect (DSA) Waiting on Approval

5

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Wedgeworth	K-5 Permanent School & Interim Housing	Complete	In Progress (Revisions for K-5 & Single Story Pending Approval)	Interim Housing: Complete New School: Pending	2/2022	07/2024
La Puente HS	Gym & Locker Room HVAC	Complete	Estimated 1/31/22	Complete	TBD	Approx. 3 months
Los Altos HS	Gym & Locker Room HVAC	Complete	Estimated 2/28/22	Complete	TBD	TBD

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Performing Arts Center	Partnership with LA County Aquatic Center	In Progress		Pending		
Districtwide	HVAC System Replacements	Pending		In Progress		
Kwis Elementary	Baseball Fields	In Progress		Pending	11/2022	8/2023



Next Report – March 24, 2022
