


SCHOOL DISTRICT

La Puente Quad




Los Altos Quad

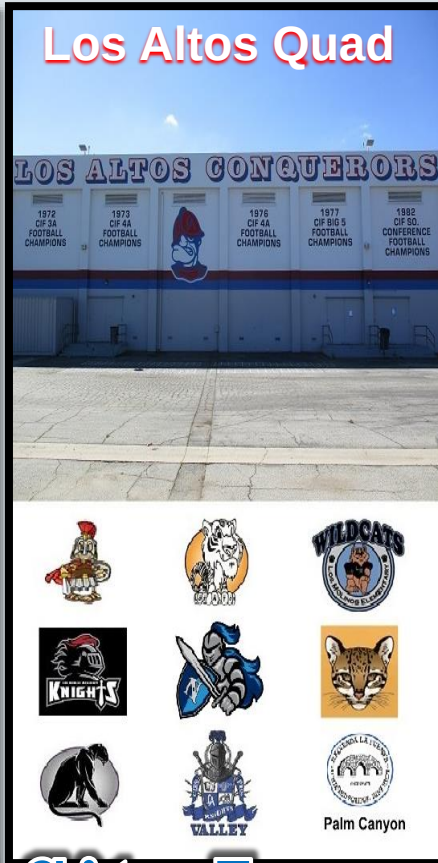

Wilson Quad



Workman Quad

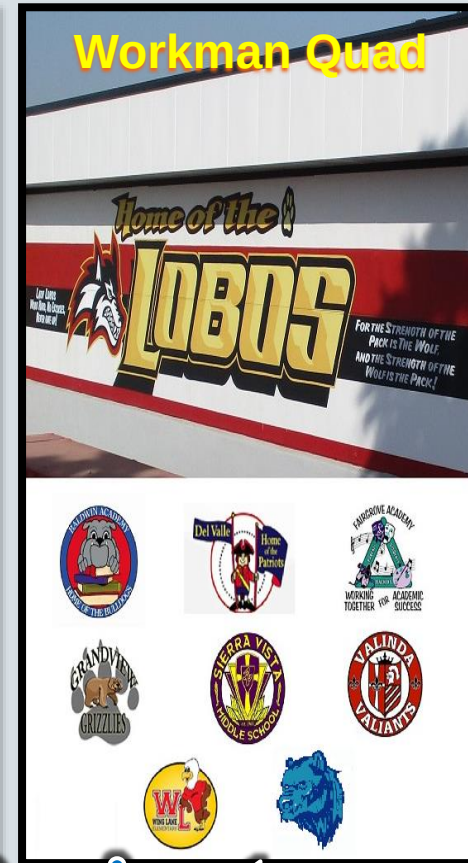

School Site Improvement Projects

Business Services

Regular Board Meeting

November 18, 2021



PROJECT COMPLETE LIST



2

Site	Item Description	Funding Source	Completed Date
Bixby	Ceiling Tiles & Lighting	Facilities/Bond	7/2021
Sunset OH	Ceiling Tiles & Lighting	Facilities/Bond	8/2021
Wilson HS	Gym & Locker Room HVAC	Prop 39	10/2021
Orange Grove MS	Interior Painting (Main Office)	Facilities	8/2021
Valley HS	Interior Painting (Room 5 & 6)	Facilities	8/2021
La Puente HS	Lockers	Facilities	8/2021
Wilson HS	Pool Water Heater Install	Facilities	7/2021
Cedarlane	Roofing	Facilities	7/2021
Nelson	Roofing	Facilities	7/2021
Newton	Roofing	Facilities	8/2021
Sparks MS	Roofing	Facilities	7/2021
Workman ES	Roofing (Cafeteria)	Facilities	8/2021
Los Altos HS	Solar Panel Arrays	Lease Financing	8/2021
La Puente HS	Solar Panel Arrays	Lease Financing	6/2021
Wilson HS	Solar Panel Arrays	Lease Financing	9/2021
Workman HS	Solar Panel Arrays	Lease Financing	8/2021
Willow AS	Solar Panel Arrays	Lease Financing	8/2021
District Office	Solar Panel Arrays	Lease Financing	6/2021

3

Projects In Progress

2021-2022





Projects Completed as of November 18, 2021

La Puente HS – Gym Lights Upgrade

NEW!

4

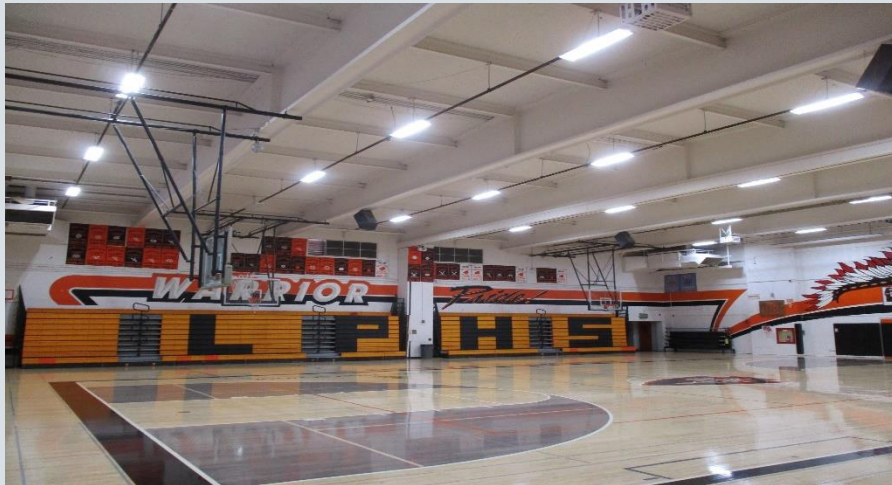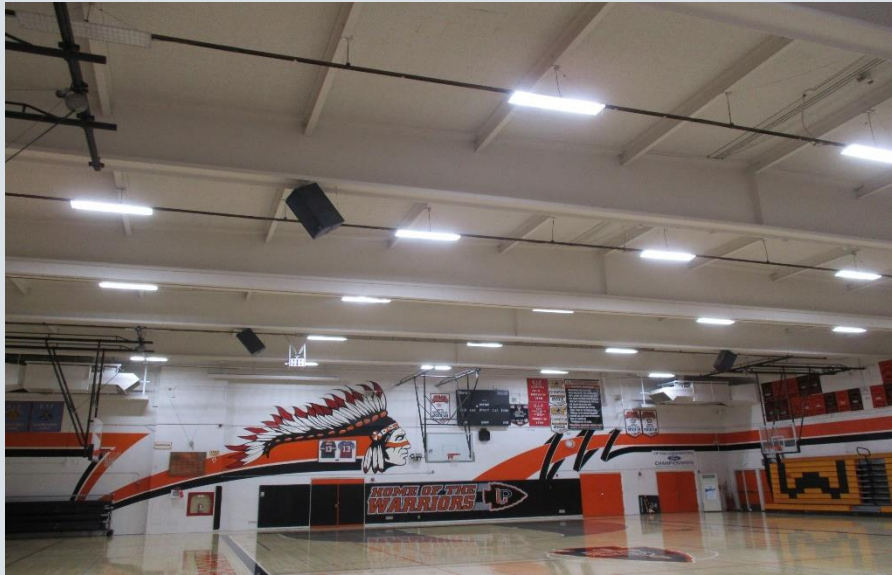


Projects Completed as of November 18, 2021

Workman HS – Gym Lights Upgrade

NEW!

5

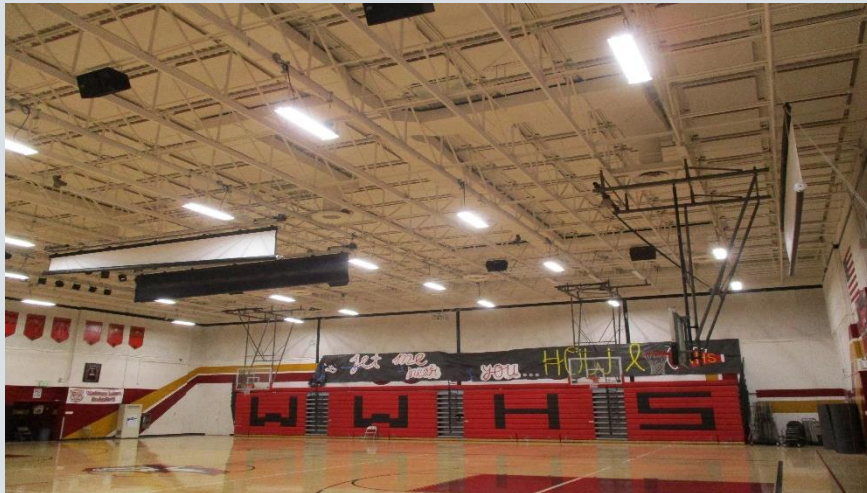

Projects Completed as of November 18, 2021

Willow – MPR Floor Repair

6



Projects In Progress as of November 18, 2021

7

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Willow AS	Conference (South) Room Flooring	Complete	N/A	Pending		Adult Ed.	1/31/2022
La Puente HS	New Kitchen (including exterior hardscape)	Complete	Complete	Complete	In Progress	Facilities	3/31/2022
La Puente HS	Pool & Locker Room Project	Complete	Complete	Complete	In Progress	Facilities	1/31/2022



La Puente HS Pool – Install Electrical Conduits



La Puente HS Kitchen – Installing the Kitchen Hood and countertops



La Puente HS Locker Room – Concrete Stairs installed



Projects In Progress as of November 28, 2021

8

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Grandview	Roofing Restoration	N/A	N/A	Complete	In Progress	Facilities	12/30/2021
Los Altos HS	Roofing Restoration	N/A	N/A	Complete	In Progress	Facilities	12/30/2021



Projects In Progress as of November 18, 2021

9

Site	Item Description	Architect Plans	DSA Approval	Procurement	Funding Source	Est. Construct Start	Target Completion Date
Grazide ES	Perimeter Fence with Bollard Placement	Hold		Hold	Pending	Pending	Pending
Workman HS	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete)	Complete	Complete	Pending	Various - Estimate Cost \$16.5M	Pending	Pending
Workman HS	Gym & Locker Room HVAC	Complete	Complete	Complete	Prop 39	12/31/21	3/1/2022



Projects with Division of State Architect (DSA) Waiting on Approval

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Wedgeworth	K-5 Permanent School & Interim Housing	Complete	In Progress (Revisions for K-5 & Interim Housing Pending Approval)		Q1 2022	07/2024
La Puente HS	Gym & Locker Room HVAC	Complete	Estimated 11/29/21	Complete	02/1/2022	06/30/22

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Est. Construct Start	Target Completion Date
Los Altos HS	Gym & Locker Room HVAC	In Progress	Estimated 1/15/2022	Complete	Pending	
Performing Arts Center	Partnership with LA County Aquatic Center	In Progress				2022/2023

Next Report – December 16, 2021

