

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
January 28, 2021

Business Services



Completed Projects

2020-2021

School Environment

Business Services: Completed Projects

Projects Completed as of January 28, 2021

Fire Alarms




Site	Item Description
Palm ES	Exterior Painting
Sparks ES	Exterior Painting
Sparks MS	Exterior Painting
Wing Lane	Exterior Painting
Workman HS	Exterior Painting
Cedarlane K-8	Fire Alarms
Grandview	Fire Alarms
Los Altos ES	Fire Alarms
Mesa Robles	Fire Alarms
Nelson	Fire Alarms
Newton	Fire Alarms
Sparks MS	Fire Alarms
Valley HS	Fire Alarms
Workman ES	Fire Alarms
Los Molinos	Floor Replacement - Interior Hallways
Wilson HS	Floor Replacement - D9, D12 Carpets
Workman HS	Front Entry Gate
La Puente HS	Front Office Flooring
La Puente HS	Front Office Painting
Los Molinos	Hallway Flooring and Painting

School Environment

Business Services: Completed Projects

Projects Completed as of January 28, 2021

Valinda – Concrete & New Gates

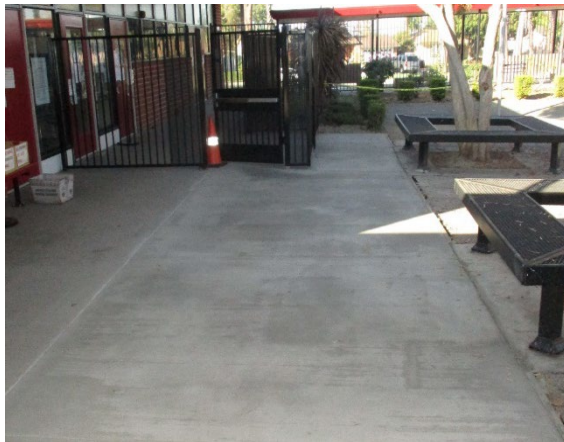

Wing Lane – Concrete for Shade Structure



Site	Item Description
Workman HS	Artificial Track and Field Phase I
District Office	Battery Back Up System
Amar CC	Bottle Filling Stations (Attached to Shade Structure Close Out)
Los Altos HS	Bottle Filling Stations (Attached to Shade Structure Close Out)
Mesa Robles K-8	Bottle Filling Stations (Attached to Shade Structure Close Out)
Sunset	Bottle Filling Stations
Wing Lane	Bottle Filling Stations (Attached to Shade Structure Close Out)
California	Ceiling Tiles
Del Valle	Ceiling Tiles
Los Altos ES	Ceiling Tiles
Nelson	Ceiling Tiles
Sparks ES	Ceiling Tiles
Workman ES	Ceiling Tiles
Valinda	Concrete and New Gates
Wing Lane	Concrete for Shade Structure Close Out
Willow AS	Concrete Replacement – Lunch Area
Willow AS	Conference (North) Room Renovation
District Office	Conference Room Remodel
Cedarlane	Covered Walkway
California	Exterior Painting
Los Molinos	Exterior Painting
Los Robles	Exterior Painting

School Environment

Business Services: Completed Projects

Projects Completed as of January 28, 2021

Lighting (Ceiling)



MPR Lighting



Site	Item Description
Cedarlane K-8	Head Start Shade Structure Installation
Los Altos ES	Interim Housing
Mesa Robles	Interim Housing & Permanent Portables
Lassalette	Kinder Reroof
Willow AS	Kitchen Remodel
Del Valle	Lighting (Ceiling)
Sparks ES	Lighting (Ceiling)
Los Altos ES	Lighting (Ceiling)
Nelson	Lighting (Ceiling)
Workman ES	Lighting (Ceiling)
Baldwin	MPR Lighting
Bixby	MPR Lighting
California	MPR Lighting
Del Valle	MPR Lighting
Grazide	MPR Lighting
Kwis	MPR Lighting
Los Altos ES	MPR Lighting
Los Molinos	MPR Lighting
Los Robles	MPR Lighting
Nelson	MPR Lighting

School Environment

Business Services: Completed Projects

Projects Completed as of January 28, 2021

Preschool Furniture



Site	Item Description
Palm	MPR Lighting
Sparks ES	MPR Lighting
Sunset	MPR Lighting
Temple	MPR Lighting
Wing Lane	MPR Lighting
Amar	New Furniture Replacement
All Preschool	New Furniture Round 1 (Baldwin, California, Lassalette, Sparks ES, Sunset, Temple)
All Preschool	New Furniture Round 2 (Bixby, Cedarlane, Del Valle, Grandview, Valinda, Workman ES)
All Preschool	New Furniture Round 3 (Fairgrove, Kwis, Nelson, Palm, Wing Lane)
Workman ES	Office Entry Doors and Gates
Wilson HS	Photoshop Renovation
Workman HS	Pool Pump Repair
Los Altos HS	Re-Stripping of Tracks (Warranty Work)
Wilson HS	Re-Stripping of Tracks (Warranty Work)
Grandview K-8	Roof Replacement
Los Molinos	Room 6 – 21 st Century Remodel
Sunset	Shade Structure Demolition
Nelson	Synthetic Turf Installation
La Puente HS	Track Re-Surface
Nelson	21 st Century Sample Classroom

Nelson 21st Classroom





Projects In Progress

2020-2021

School Environment

Business Services: Current Projects

Projects In Progress as of January 28, 2021

Bottle Filling Stations



Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Workman HS	Artificial Track and Field Phase II (Submitted to DSA. CEQA Initial Study Complete)	Complete	In Progress			2/1/2021
Baldwin	Bottle Filling Stations	Complete	Complete			3/1/2021
Bixby	Bottle Filling Stations	Complete	Complete			3/1/2021
California	Bottle Filling Stations	Complete	Complete			3/1/2021
Cedarlane K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	4/1/2021
Del Valle	Bottle Filling Stations	Complete	Complete			3/1/2021
Dibble AS	Bottle Filling Stations	Complete	Complete			3/1/2021
District Office	Bottle Filling Stations	Complete	Complete			3/1/2021
Fairgrove K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	2/1/2021
Grandview K-8	Bottle Filling Stations	Complete	Complete			3/1/2021
Grazide	Bottle Filling Stations	Complete	Complete			3/1/2021
Hudson AS	Bottle Filling Stations	Complete	Complete			3/1/2021
Kwis ES	Bottle Filling Stations	Complete	Complete	In Progress		2/1/2021
La Puente HS	Bottle Filling Stations	Complete	Complete	In Progress		2/1/2021
Lassalette K-8	Bottle Filling Stations	Complete	Complete	In Progress		2/1/2021
Los Robles	Bottle Filling Stations	Complete	Complete			3/1/2021
Mesa Robles K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	2/1/2021
Nelson	Bottle Filling Stations	Complete	Complete			3/1/2021
Newton	Bottle Filling Stations	Complete	Complete			3/1/2021

School Environment

Business Services: Current Projects

Projects In Progress as of January 28, 2021

Willow AS MPR
Room



Willow AS (South)
Conference Room



Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Orange Grove	Bottle Filling Stations	In Progress	In Progress			3/1/2021
Palm Canyon	Bottle Filling Stations	In Progress	In Progress			3/1/2021
Palm ES	Bottle Filling Stations	Complete	In Progress			3/1/2021
Sierra Vista	Bottle Filling Stations	In Progress	In Progress			4/1/2021
Sparks ES	Bottle Filling Stations	Complete	Complete	In Progress		2/1/2021
Sparks MS	Bottle Filling Stations	In Progress	In Progress			3/1/2021
Stimson LC	Bottle Filling Stations	Complete	In Progress			4/1/2021
Temple	Bottle Filling Stations	Complete	In Progress			3/1/2021
Valinda	Bottle Filling Stations	In Progress	In Progress			3/1/2021
Valley HS	Bottle Filling Stations	In Progress	In Progress			4/1/2021
Wedgeworth	Bottle Filling Stations	Complete	Complete	In Progress		2/1/2021
Willow AS	Bottle Filling Stations	In Progress	In Progress			4/1/2021
Wilson HS	Bottle Filling Stations	Complete	Complete	In Progress		4/1/2021
Wing Lane	Bottle Filling Stations	Complete	In Progress	In Progress		3/1/2021
Workman ES	Bottle Filling Stations	Complete	Complete	In Progress		2/1/2021
Workman HS	Bottle Filling Stations	In Progress	In Progress			4/1/2021
Willow AS	Conference (South) Room Renovation	Complete	N/A	Complete	In Progress	2/15/2021

School Environment

Business Services: Current Projects

Projects In Progress as of January 28, 2021

California & Wilson HS Fire Alarms



Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Grazide	Exterior Painting	N/A	N/A			2/1/2021
District Office	Fire Alarm	Complete	N/A	In Progress		4/1/2021
Willow AS	Fire Alarm	Complete	Complete	Complete		4/1/2021
California	Fire Alarm	Complete	Complete	Complete	In Progress	4/1/2021
Dibble AS	Fire Alarms	Complete	N/A	Complete		4/1/2021
La Puente HS	Fire Alarms	Complete	Complete	Complete		3/1/2021
Los Altos HS	Fire Alarms	In Progress				4/1/2021
Wilson HS	Fire Alarms	Complete	Complete	Complete	In Progress	4/1/2021
Workman HS	Fire Alarms	Complete	Complete	In Progress		4/1/2021
Lassalette K-8	Front Landscape	In Progress				On Hold
Sparks MS	Front Landscape	In Progress				On Hold
Workman ES	Front Landscape	In Progress				On Hold
La Puente HS	Gym & Locker Room HVAC	In Progress				8/1/2021
Los Altos HS	Gym & Locker Room HVAC	In Progress				8/1/2021
Wilson HS	Gym & Locker Room HVAC	In Progress				8/1/2021
Workman HS	Gym & Locker Room HVAC	In Progress				8/1/2021
Baldwin	Irrigation Replacement	In Progress				On Hold
Bixby	Irrigation Replacement	In Progress				On Hold

School Environment

Business Services: Current Projects

Projects In Progress as of January 28, 2021

La Puente HS New Kitchen



Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Cedarlane K-8	Irrigation Replacement	Complete	N/A	In Progress		On Hold
Del Valle	Irrigation Replacement	Complete	Complete	In Progress		On Hold
Fairgrove K-8	Irrigation Replacement	In Progress				On Hold
Grazide	Irrigation Replacement	In Progress	N/A			On Hold
Sierra Vista	Irrigation Replacement	Complete	Complete	In Progress		On Hold
Los Molinos	Kindergarten Portable Replacement	In Progress				On Hold
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		On Hold
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		On Hold
La Puente HS	New Kitchen	Complete	Complete	In Progress	In Progress	4/30/2021
Del Valle	Office entry doors and gates	Complete	Complete			On Hold
Sparks ES	Office entry doors and gates	Complete	In Progress			On Hold
Temple	Office entry doors and gates	Complete	Complete			On Hold
Valinda	Office entry doors and gates	In Progress				On Hold
Grazide	Perimeter Wall Replacement	In Progress				On Hold
Wedgeworth	Permanent School (CEQA Initial Study ready)	Complete	Complete			8/1/2021
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress		On Hold

School Environment

Business Services: Current Projects

Willow Restrooms



La Puente HS Pool



Projects In Progress as of January 28, 2021

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Cedarlane	Interim Housing	In Progress				2/1/2021
Newton	Interim Housing	Complete	In Progress			2/15/2021
California	New Rubberized Playground with New Swings	N/A	N/A	In Progress		On Hold
District Office	Police Office Replacement & Restrooms	In Progress	N/A			On Hold
Los Altos ES	Portables	In Progress	Complete	In Progress		On Hold
Wedgeworth	Portables	In Progress				On Hold
Willow AS	Restroom Renovation	Complete	N/A	Complete	In Progress	3/30/2021
Amar	Shade Structure - New	Complete	Complete	In Progress		On Hold
District Office	Solar	N/A	N/A	In Progress		
La Puente HS	Solar (Scheduled for 1/21)	N/A		In Progress		
Los Altos HS	Solar (Scheduled for 1/21)	N/A		In Progress		
Willow AS	Solar (Scheduled for 1/21)	N/A	N/A	In Progress		
Wilson HS	Solar (Scheduled for 1/21)	N/A		In Progress		
Workman HS	Solar (Scheduled for 1/21)	N/A		In Progress		
Willow AS	Two-Story Building Renovation	N/A	N/A	In Progress		On Hold
La Puente HS	New Pool	Complete	Complete	In Progress	In Progress	4/30/2021



Next Report – February 25, 2021
