

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
December 12, 2019

Business Services



Completed Projects

2019-2020

School Environment

Business Services: Completed Projects

Projects Completed as of December 12, 2019

Site	Item Description	Construct
Workman HS	Artificial Track and Field Phase I	Complete
District Office	Conference Room Remodel	Complete
Los Molinos	Exterior Painting	Complete
Sparks ES	Exterior Painting	Complete
Sparks MS	Exterior Painting	Complete
Wing Lane	Exterior Painting	Complete
Workman HS	Exterior Painting	Complete
Los Molinos	Floor Replacement - Interior Hallways	Complete
La Puente HS	Front Office Flooring	Complete
La Puente HS	Front Office Painting	Complete
Los Molinos	Hallway Flooring and Painting	Complete
Cedarlane K-8	Head Start Shade Structure Installation	Complete
Los Altos ES	Interim Housing	Complete
All Preschool	New Furniture Round 1 (Baldwin, California, Lassalette, Sparks ES, Sunset, Temple)	Complete
All Preschool	New Furniture Round 2 (Bixby, Cedarlane, Del Valle, Grandview, Valinda, Workman ES)	Complete
All Preschool	New Furniture Round 3 (Fairgrove, Kwis, Nelson, Palm, Wing Lane)	Complete
Workman ES	Office Entry Doors and Gates	Complete
Workman HS	Pool Pump Repair	Complete
Grandview K-8	Roof Replacement	Complete
Los Molinos	Room 6 – 21 st Century Remodel	Complete
Sunset	Shade Structure Demolition	Complete
Nelson	Synthetic Turf Installation	Complete
La Puente HS	Track Re-Surface	Complete



Projects In Progress

2019-2020

School Environment

Business Services: Current Projects

Projects In Progress as of December 12, 2019

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Workman HS	Artificial Track and Field Phase II	Complete	In Progress			10/31/2020	Submitted to DSA. CEQA Initial Study Complete
District Office	Battery Back Up System	N/A	N/A	Complete	In Progress	2/28/2020	
Amar CC	Bottle Filling Stations	Complete	Complete	Complete	In Progress	1/31/2020	
Baldwin	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Bixby	Bottle Filling Stations	Complete	In Progress			12/31/2019	
California	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Cedarlane K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	1/31/2020	
Del Valle	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Dibble AS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
District Office	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Fairgrove K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	1/31/2020	
Grandview K-8	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Grazide	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Hudson AS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Kwis ES	Bottle Filling Stations	Complete	Complete	Complete	In Progress	1/31/2020	
La Puente HS	Bottle Filling Stations	Complete	Complete	Complete	In Progress	1/31/2020	
Lassalette K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	1/31/2020	
Los Altos HS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Los Robles	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Mesa Robles K-8	Bottle Filling Stations	In Progress	In Progress	Complete	In Progress	1/31/2020	
Nelson	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Newton	Bottle Filling Stations	In Progress	In Progress			12/31/2019	

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Current Projects

Projects In Progress as of December 12, 2019

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Orange Grove	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Palm Canyon	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Palm ES	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Sierra Vista	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Sparks ES	Bottle Filling Stations	Complete	Complete	In Progress		1/31/2020	
Sparks MS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Stimson LC	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Sunset	Bottle Filling Stations	Complete	Complete	In Progress		1/31/2020	
Temple	Bottle Filling Stations	Complete	In Progress			12/31/2019	
Valinda	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Valley HS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Wedgeworth	Bottle Filling Stations	Complete	Complete	In Progress		1/31/2020	
Willow AS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Wilson HS	Bottle Filling Stations	Complete	Complete	In Progress		1/31/2020	
Wing Lane	Bottle Filling Stations	Complete	In Progress	In Progress		12/31/2019	
Workman ES	Bottle Filling Stations	Complete	Complete	In Progress		1/31/2020	
Workman HS	Bottle Filling Stations	In Progress	In Progress			12/31/2019	
Willow AS	Concrete Replacement – Lunch Area	Complete	N/A	Complete	In Progress	11/29/2019	
Willow AS	Conference (North) Room Renovation	Complete	N/A	Complete	In Progress	11/30/2019	
Willow AS	Conference (South) Room Renovation	Complete	N/A	Complete	In Progress	6/15/2020	
Cedarlane K-8	Covered Walkway	Complete	Complete	In Progress		1/15/2020	Bids Submitted

School Environment

Business Services: Current Projects

Projects In Progress as of December 12, 2019

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
California	Exterior Painting	N/A	N/A	In Progress	In Progress	1/30/2020	
Grazide	Exterior Painting	N/A	N/A			6/30/2020	
Palm ES	Exterior Painting	N/A	N/A	Complete	In Progress	6/30/2020	
District Office	Fire Alarm	Complete	N/A	In Progress		8/30/2020	
Willow AS	Fire Alarm	Complete	Complete	Complete		7/31/2020	Bid award 9/26/19
Cedarlane K-8	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
Dibble AS	Fire Alarms	Complete	N/A	Complete		7/31/2020	Bid award 9/26/19
Grandview K-8	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
La Puente HS	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
Los Altos ES	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
Los Altos HS	Fire Alarms	In Progress				7/31/2020	
Mesa Robles K-8	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
Nelson	Fire Alarms	Complete	Complete	Complete	In Progress	4/30/2020	Bid award 9/26/19
Newton	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
Sparks MS	Fire Alarms	Complete	Complete	Complete	In Progress	1/31/2020	Bid award 9/26/19
Wilson HS	Fire Alarms	Complete	Complete	Complete	In Progress	7/31/2020	Bid award 9/26/19
Workman ES	Fire Alarms	Complete	Complete	Complete	In Progress	4/30/2020	Bid award 9/26/19
Workman HS	Fire Alarms	Complete	Complete	In Progress		7/31/2020	Bid award 9/26/19
Lassalette K-8	Front Landscape	In Progress				6/30/2020	
Sparks MS	Front Landscape	In Progress				6/30/2020	
Workman ES	Front Landscape	In Progress				6/30/2020	

School Environment

Business Services: Current Projects

Projects In Progress as of December 12, 2019

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Baldwin	Irrigation Replacement	In Progress				7/31/2020	
Bixby	Irrigation Replacement	In Progress				12/31/2020	
Cedarlane K-8	Irrigation Replacement	Complete	N/A	In Progress		7/31/2020	
Del Valle	Irrigation Replacement	Complete	Complete	In Progress		4/10/2020	
Fairgrove K-8	Irrigation Replacement	In Progress				12/31/2020	
Grazide	Irrigation Replacement	In Progress	N/A			7/31/2020	
Sierra Vista	Irrigation Replacement	Complete	Complete	In Progress		4/10/2020	
Los Molinos	Kindergarten Portable Replacement	In Progress				7/15/2020	
Willow AS	Kitchen Remodel	Complete	N/A	Complete	In Progress	12/6/2019	
Baldwin	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Bixby	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
California	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Del Valle	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Grazide	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Kwis ES	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Los Altos ES	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Los Molinos	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Los Robles	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Nelson	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Palm ES	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Sparks ES	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting

School Environment

Business Services: Current Projects

Projects In Progress as of December 12, 2019

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Sunset	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Temple	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
Wing Lane	MPR Lighting	N/A	N/A	In Progress		7/31/2020	Part of Phase 4 lighting
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2020	
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2020	
Amar	New Furniture Replacement	N/A	N/A			12/20/2020	14 of 38 complete
La Puente HS	New Kitchen	Complete	Complete	In Progress		10/31/2020	Re-bid in progress
Del Valle	Office entry doors and gates	Complete	Complete			7/31/2020	Bid to be timed for Summer 2020 Work
Sparks ES	Office entry doors and gates	Complete	In Progress			7/31/2020	Bid to be timed for Summer 2020 Work
Temple	Office entry doors and gates	Complete	Complete			7/31/2020	Bid to be timed for Summer 2020 Work
Valinda	Office entry doors and gates	In Progress				7/31/2020	Bid to be timed for Summer 2020 Work
Grazide	Perimeter Wall Replacement	In Progress				12/31/2020	
Wedgeworth	Permanent School	Complete	In Progress			8/1/2021	Submitted to DSA. CEQA Draft Initial Study ready
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress		12/31/2020	
Wilson HS	Photoshop Renovation	Complete	Complete	Complete	In Progress	12/31/2019	Working with teacher on dark room furniture

School Environment

Business Services: Current Projects

Projects In Progress as of December 12, 2019

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
District Office	Police Office Replacement & Restrooms	In Progress	N/A			3/30/2020	
Los Altos ES	Portables	In Progress					
Wedgeworth	Portables	In Progress					
Willow AS	Restroom Renovation	Complete	N/A	Complete	In Progress	1/15/2020	
Amar	Shade Structure - New	Complete	Complete	In Progress		2/28/2020	
District Office	Solar	N/A	N/A	In Progress			
La Puente HS	Solar	N/A		In Progress			
Los Altos HS	Solar	N/A		In Progress			
Willow AS	Solar	N/A	N/A	In Progress			
Wilson HS	Solar	N/A		In Progress			
Workman HS	Solar	N/A		In Progress			
Willow AS	Two-Story Building Renovation	N/A	N/A	In Progress		2/28/2020	
La Puente HS	New Pool	Complete	Complete	In Progress		10/31/2020	Re-bid in progress

District staff continue to address the issues raised with the LPHS Pool. Demolition contractors have provided three proposals for removing the pool deck and structure. A purchase order is in process and demolition is tentatively scheduled to start over the Thanksgiving break. The pool has been drained **in progress as of 11/23/2019, demolition complete 12/06/2019**

Shade Structure

Cedarlane Head Start



Shade Structure

Sunset



Synthetic Turf

Nelson Elementary




Classroom Furniture

Cedarlane Head Start



Pool Demolition

La Puente High School

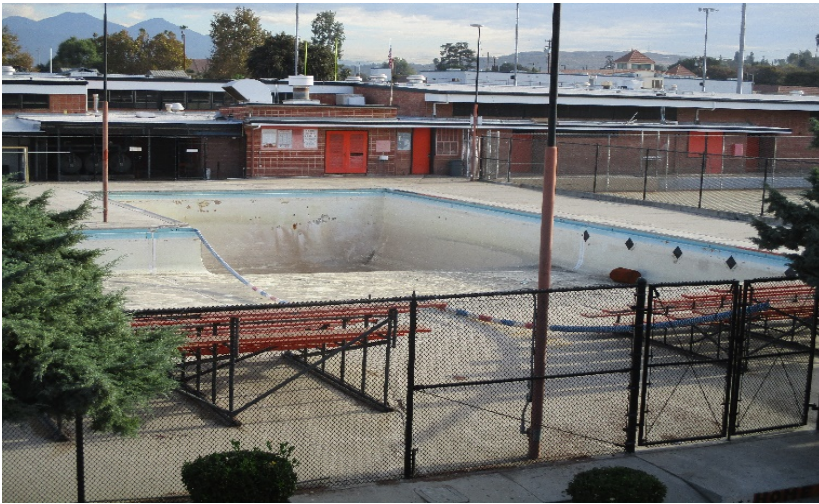



Next Report – January 2020
