

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
January 25, 2018

Business Services



Completed Projects

2017-2018

School Environment

Business Services: Completed Projects

Projects Completed as of January 25, 2018

Site	Item Description	Construct
Baldwin	Concrete Benches	Complete
Cedarlane	Concrete Benches	Complete
Del Valle	Concrete Benches	Complete
Fairgrove	Concrete Benches	Complete
Grandview	Concrete Benches	Complete
Grazide	Concrete Benches	Complete
Lassalette	Concrete Benches	Complete
Los Altos ES	Concrete Benches	Complete
Los Robles	Concrete Benches	Complete
Mesa Robles	Concrete Benches	Complete
Orange Grove	Concrete Benches	Complete
Sierra Vista	Concrete Benches	Complete
Sparks MS	Concrete Benches	Complete
Sunset	Concrete Benches	Complete
Valinda	Concrete Benches	Complete
Wilson HS	Concrete Benches	Complete
Workman HS	Concrete Benches	Complete
Wilson HS	Dance Floor Installation	Complete
Willow Adult Ed	EDD Tenant Improvements	Complete
California	Elementary Playground Surfacing	Complete
Grandview	Elementary Playground Surfacing	Complete
Los Molinos	Elementary Playground Surfacing	Complete
Los Robles	Elementary Playground Surfacing	Complete
Palm ES	Elementary Playground Surfacing	Complete

School Environment

Business Services: Completed Projects

Projects Completed as of January 25, 2018

Site	Item Description	Construct
Temple	Elementary Playground Surfacing	Complete
Workman ES	Elementary Playground Surfacing	Complete
Bixby	Exterior Painting	Complete
Fairgrove	Exterior Painting	Complete
Los Altos HS	Exterior Painting	Complete
Valinda	Exterior Painting	Complete
Facilities	Fire Alarm Replacement	Complete
Bixby	Floor Replacement - Interior Hallways	Complete
Bixby	Floor Replacement - MPR	Complete
Los Molinos	Floor Replacement - MPR	Complete
Palm ES	Floor Replacement - MPR	Complete
Sierra Vista	Floor Replacement - MPR	Complete
Wing Lane	Floor Replacement - MPR	Complete
Los Molinos	Portable Classroom Addition	Complete
Wedgeworth	Portable Classroom Addition	Complete
La Puente HS	Roofing replacement - Administration	Complete
Valinda	Roofing replacement - Covered Walks	Complete
Wing Lane	Roofing replacement - Covered Walks	Complete
Wing Lane	Roofing replacement - MPR	Complete
Grazide	School Entry Signs	Complete
Lassalette	School Entry Signs	Complete
Los Altos HS	School Entry Signs	Complete
Valinda	School Entry Signs	Complete
Workman HS	School Entry Signs	Complete

School Environment

Business Services: Completed Projects

Projects Completed as of January 25, 2018

Site	Item Description	Construct
Stimson LC	Security Fencing	Complete
Cedarlane	Shade Structure	Complete
Los Altos ES	Shade Structure	Complete
Stimson LC	Shade Structure	Complete
Valinda	Shade Structure	Complete
Wedgeworth	Shade Structure	Complete
Workman ES	Shade Structure	Complete
Workman HS	Shade Structure	Complete
Wilson HS	Shade Structure - Concession Stand	Complete
La Puente HS	Synthetic Turf Field Replacement	Complete

Painting

Los Altos High School



Irrigation and Landscaping

Nelson – In progress



Site Benches

Los Altos ES



Shade Structure

Workman ES



Wilson High



Wedgeworth Architect Selection

Staff Meeting
January 23

Community Meeting
January 24

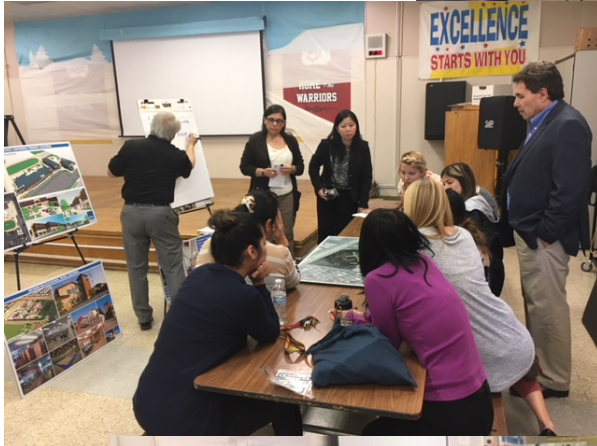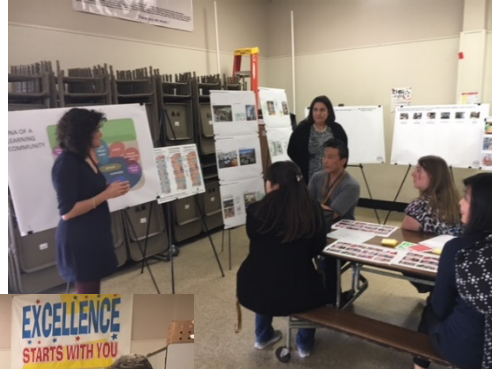



Projects In Progress

2017-2018

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Workman HS	Artificial Track and Field Phase I	In Progress	N/A			10/30/2018	TBP preparing track and softball field bid documents for March 2018 bid
Workman HS	Artificial Track and Field Phase II	In Progress					TBP preparing Stadium design and cost updates based on Dec. 7 Board input
District Office	C Building Walkways & Parking	Complete	N/A			7/31/2018	On hold for completion of portables and electrical work
District Office	Compressed Natural Gas (CNG) Fuel Station	Complete	N/A	Complete	In Progress	3/8/2018	All permits issued. Staging meeting held 1/16/18.
Bixby	Concrete Benches	N/A	N/A	Complete		2/15/2018	
California	Concrete Benches	N/A	N/A	Complete		1/30/2018	
Dibble	Concrete Benches	N/A	N/A	Complete		3/16/2018	
District Office	Concrete Benches	N/A	N/A	In Progress		3/16/2018	
Kwis	Concrete Benches	N/A	N/A	Complete		2/30/2018	
Los Molinos	Concrete Benches	N/A	N/A	Complete		2/15/2018	
Nelson	Concrete Benches	N/A	N/A	Complete		2/15/2018	
Palm ES	Concrete Benches	N/A	N/A	Complete		2/30/2018	
Sparks ES	Concrete Benches	N/A	N/A	Complete		2/15/2018	
Stimson LC	Concrete Benches	N/A	N/A	Complete		2/30/2018	

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Temple	Concrete Benches	N/A	N/A	Complete		1/30/2018	
Valley Alt HS	Concrete Benches	N/A	N/A	Complete		2/30/2018	
Wedgeworth	Concrete Benches	N/A	N/A	Complete		2/30/2018	
Wing Lane	Concrete Benches	N/A	N/A	Complete		2/30/2018	
Workman ES	Concrete Benches	N/A	N/A	Complete		2/30/2018	
Dibble	Fire Alarm Replacement	Complete	N/A	Complete	In Progress	3/1/2018	
District Office	Fire Alarm Replacement	Complete	N/A	In Progress		5/15/2018	Combined with HVAC Bid
Willow - Old	Fire Alarm Replacement	Complete	N/A	Complete	In Progress	3/1/2018	Plans revised for updated code requirements
Willow - New	Fire Alarm Update	Complete	Complete	Complete	In Progress	3/1/2018	Plans revised for updated code requirements
Los Molinos	Floor Replacement - Interior Hallways	N/A	N/A	Complete		6/30/2018	New Asbestos Bid Needed
Fairgrove	Head Start Classroom Replacement	Complete	Complete	Complete	In Progress	2/28/2018	Demolition completed over winter break
Baldwin	Irrigation Replacement	Complete	N/A	In Progress			
Cedarlane	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Del Valle	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Grazide	Irrigation Replacement	In Progress	N/A				
Los Molinos	Irrigation Replacement	Complete	N/A	Complete	In Progress	3/15/2018	
Nelson	Irrigation Replacement	Complete	N/A	Complete	In Progress	2/9/2018	
Sierra Vista	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
La Puente HS	Lower Field Irrigation	Complete	N/A	In Progress			
Baldwin	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Bixby	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
California	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Del Valle	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Grazide	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Kwis	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Los Altos ES	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Los Molinos	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Los Robles	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Nelson	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Palm ES	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Sparks ES	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Sunset	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Temple	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wing Lane	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
Workman ES	MPR Lighting	N/A	N/A	In Progress		6/30/2018	Part of Phase 4 lighting
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2018	
Los Altos HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2018	
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2018	
District Office	NCS & Purchasing Offices	In Progress	N/A	Complete	In Progress	4/30/2018	Bids opened 1/18/2018
La Puente HS	New Kitchen	Complete	In Progress			10/30/2018	DSA Plan Check Corrections Completed
La Puente HS	New Pool and Dressing Area	Complete	In Progress			10/30/2018	DSA Plan Check Corrections Completed
California	Office entry doors and gates	Complete	Complete			6/30/2018	
Del Valle	Office entry doors and gates	Complete	In Progress			6/30/2018	
Grandview	Office entry doors and gates	Complete	Complete			6/30/2018	
Orange Grove	Office entry doors and gates	Complete	Complete			6/30/2018	
Temple	Office entry doors and gates	Complete	In Progress			6/30/2018	
Workman ES	Office entry doors and gates	Complete	Complete			6/30/2018	
District Office	Paving – All Parking areas	N/A	N/A	Complete	In Progress	4/15/2018	75% Complete. Holding remaining work for CNG station
California	Paving – Demolition of Cottage, add parking	N/A	N/A	Complete	In Progress	6/30/2018	
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress		5/15/2018	
Los Altos ES	Portable Classroom Addition	Complete	Complete	Complete		6/30/2018	
Newton	Portable Classroom Replacement	Complete	Complete	Complete	In Progress	4/30/2018	

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Baldwin	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Bixby	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
California	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Cedarlane	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Del Valle	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
Dibble	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
District Office	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
Fairgrove	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Grandview	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Kwis	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
La Puente HS	School Entry Signs	N/A	N/A	Complete	In progress	1/30/2018	
Los Altos ES	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Los Molinos	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Los Robles	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
Mesa Robles	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Nelson	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
Orange Grove	School Entry Signs	N/A	N/A	In Progress		4/7/2018	

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Palm ES	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Sierra Vista	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
Sparks ES	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Sparks MS	School Entry Signs	N/A	N/A	Complete	In Progress	2/15/2018	
Stimson LC	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Sunset	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Temple	School Entry Signs	N/A	N/A	In Progress		4/7/2018	
Valley Alt HS	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Wedgeworth	School Entry Signs	N/A	N/A	In Progress		2/27/2018	
Wilson HS	School Entry Signs	N/A	N/A	Complete	In Progress	1/25/2018	
Wing Lane	School Entry Signs	N/A	N/A	Complete	In Progress	12/31/2017	
Workman ES	School Entry Signs	N/A	N/A	Complete	In Progress	3/1/2018	



New Projects

2017-2018

School Environment

Business Services: Current Projects

New 2017-18 Year Projects In Progress as of January 25, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wedgeworth	Portable Classroom Addition	Complete	In Progress			6/6/2018	Award of bid October 26, 2017 Meeting
Cedarlane	Portable Headstart Classroom Addition	In Progress				7/30/2018	
Grandview	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Mesa Robles	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Newton	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Willow Adult Ed	Roof Replacement	Complete	Complete	Complete	In Progress	1/31/2018	
Workman HS	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Wilson HS	Food Science Room	In Progress				1/1/2019	
Los Altos HS	CTE Engineering Project	In Progress					Approval of grant request on December 7, 2017 agenda

School Environment

Business Services



Next Report – February 2018
