

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site
Improvement Projects

Regular Board Meeting
March 23, 2017

Business Services



Completed: Major Projects

2016-2017

School Environment

Business Services: Completed Projects

Major Projects Completed in 2016-17 as of March 23, 2017

California	Abatement and Flooring Installation – MPR	Complete
Grandview	Abatement and Flooring Installation – MPR	Complete
Los Altos ES	Abatement and Flooring Installation – MPR	Complete
Newton MS	Abatement and Flooring Installation – MPR	Complete
Orange Grove	Abatement and Flooring Installation – MPR	Complete
Sparks ES	Abatement and Flooring Installation – MPR	Complete
Sparks MS	Abatement and Flooring Installation – MPR	Complete
Sunset	Abatement and Flooring Installation – MPR	Complete
Temple	Abatement and Flooring Installation – MPR	Complete
Workman ES	Abatement and Flooring Installation – MPR	Complete
Sierra Vista	Abatement and Flooring Installation – Room 10	Complete
Temple	Abatement and Flooring Installation – Room 10	Complete
Workman ES	Abatement and Flooring Installation – Room 10	Complete
California	Abatement and Flooring Installation – Room 11	Complete
Del Valle	Abatement and Flooring Installation – Room 11	Complete
Temple	Abatement and Flooring Installation – Room 11	Complete
Palm	Abatement and Flooring Installation – Room 13	Complete
Del Valle	Abatement and Flooring Installation – Room 15	Complete
Grandview	Abatement and Flooring Installation – Room 22	Complete
Grandview	Abatement and Flooring Installation – Room 23	Complete
Sierra Vista	Abatement and Flooring Installation – Room 44	Complete
Los Molinos	Abatement and Flooring Installation – Room 5	Complete
Workman ES	Abatement and Flooring Installation – Room 7	Complete
Newton	Abatement and Flooring Installation – Room B5	Complete
Newton	Abatement and Flooring Installation – Room B7	Complete

School Environment

Business Services: Completed Projects

Major Projects Completed in 2016-17 as of March 23, 2017

Baldwin	Abatement and Flooring Installation – Room P5	Complete
Los Altos High	Artificial Track and Field Design	Complete
Los Altos HS	Baseball Infield	Complete
La Puente HS	Ceiling Tile Replacement 12 rooms	Complete
Dibble	Ceiling Tile Replacement Admin & MPR	Complete
Wilson HS	Ceiling Tile Replacement Locker Rooms	Complete
Newton	Ceiling Tile Replacement MPR	Complete
Wilson HS	Digital Sign Replacement	Complete
Los Molinos	Elementary Playground Surfacing	Complete
Kwis	Elementary Playground Surfacing	Complete
Baldwin	Fencing	Complete
Bixby	Fencing	Complete
California	Fencing	Complete
Del Valle	Fencing	Complete
Grazide	Fencing	Complete
Kwis	Fencing	Complete
Los Altos ES	Fencing	Complete
Los Molinos	Fencing	Complete
Los Robles	Fencing	Complete
Nelson	Fencing	Complete
Palm ES	Fencing	Complete
Sparks ES	Fencing	Complete
Stimson Annex	Fencing	Complete
Sunset	Fencing	Complete
Temple	Fencing	Complete

School Environment

Business Services: Completed Projects

Major Projects Completed in 2016-17 as of March 23, 2017

Wedgeworth	Fencing	Complete
Wing Lane	Fencing	Complete
La Puente HS	Front Office Counter and Flooring	Complete
Baldwin	Golden Ribbon Graphics	Complete
Fairgrove	Golden Ribbon Graphics	Complete
Kwis	Golden Ribbon Graphics	Complete
Los Molinos	Golden Ribbon Graphics	Complete
Mesa Robles	Golden Ribbon Graphics	Complete
Spark ES	Golden Ribbon Graphics	Complete
Sunset	Golden Ribbon Graphics	Complete
Temple	Golden Ribbon Graphics	Complete
Valinda	Golden Ribbon Graphics	Complete
Wedgeworth	Golden Ribbon Graphics	Complete
Workman ES	Golden Ribbon Graphics	Complete
District Office	Human Resources Offices	Complete
Orange Grove	Irrigation Replacement	Complete
Workman ES	Kinder Restroom Addition	Complete
Cedarlane	Kitchen Floor Replacement and Painting	Complete
Del Valle	Kitchen Floor Replacement, Tables, and Painting	Complete
Grazide	Kitchen Floor Replacement, Tables, and Painting	Complete
Los Altos ES	Kitchen Floor Replacement, Tables, and Painting	Complete
Los Molinos	Kitchen Floor Replacement, Tables, and Painting	Complete
Mesa Robles	Kitchen Floor Replacement, Tables, and Painting	Complete
Orange Grove	Kitchen Floor Replacement, Tables, and Painting	Complete
Palm ES	Kitchen Floor Replacement, Tables, and Painting	Complete

School Environment

Business Services: Completed Projects

Major Projects Completed in 2016-17 as of March 23, 2017

Sunset	Kitchen Floor Replacement, Tables, and Painting	Complete
Bixby	Model Classroom Upgrades	Complete
California	Model Classroom Upgrades	Complete
Dibble	Model Classroom Upgrades	Complete
Grandview	Model Classroom Upgrades	Complete
La Puente HS	Model Classroom Upgrades	Complete
Los Altos HS	Model Classroom Upgrades	Complete
Newton	Model Classroom Upgrades	Complete
Wilson HS	Model Classroom Upgrades	Complete
Workman HS	Model Classroom Upgrades	Complete
Del Valle	MPR Flooring	Complete
Grazide	MPR Flooring	Complete
Los Robles	MPR Flooring	Complete
Amar	MPR Painting	Complete
Baldwin	MPR Painting	Complete
Del Valle	MPR Painting	Complete
Grandview	MPR Painting	Complete
Grazide	MPR Painting	Complete
Kwis	MPR Painting	Complete
Los Altos ES	MPR Painting	Complete
Mesa Robles	MPR Painting	Complete
Newton MS	MPR Painting	Complete
Sunset	MPR Painting	Complete
Valinda	MPR Painting	Complete
Wing Lane	MPR Painting	Complete

School Environment

Business Services: Completed Projects

Major Projects Completed in 2016-17 as of March 23, 2017

Workman ES	MPR Painting	Complete
Workman HS	Music Room Upgrades	Complete
Cedarlane	Office entry doors and gates	Complete
Fairgrove	Office entry doors and gates	Complete
Los Molinos	Office entry doors and gates	Complete
Nelson	Office entry doors and gates	Complete
Newton	Office entry doors and gates	Complete
Sparks MS	Office entry doors and gates	Complete
Sunset	Office entry doors and gates	Complete
Sierra Vista	Paving and Striping - Front Parking Lot	Complete
Temple	Paving and Striping - Front Parking Lot	Complete
Workman ES	Paving and Striping - Main Playground	Complete
Grandview	Phase III – Energy Retrofits	Complete
Mesa Robles	Phase III – Energy Retrofits	Complete
Newton	Phase III – Energy Retrofits	Complete
Valinda	Phase III – Energy Retrofits	Complete
Los Altos ES	Portable Classroom Addition	Complete
Los Molinos	Portable Classroom Addition	Complete
Los Molinos	Portable Classroom Addition	Complete
Mesa Robles	Portable Classroom Addition	Complete
Wedgeworth	Portable Classroom Addition	Complete
Palm	Roof Replacement – Library/Rooms 7 – 16	Complete
Valinda	Roof Replacement –Multi-purpose	Complete
Los Altos ES	SBAC Testing II – Room C1	Complete
Willow	Science Lab Addition	Complete

School Environment

Business Services: Completed Projects

Major Projects Completed in 2016-17 as of March 23, 2017

Grazide	Seal and Striping - Front Parking and Playgrounds	Complete
Bixby	Shade Structure	Complete
Del Valle	Shade Structure	Complete
Grazide	Shade Structure	Complete
Los Altos HS	Shade Structure	Complete
Los Molinos	Shade Structure	Complete
Mesa Robles	Shade Structure	Complete
Nelson	Shade Structure	Complete
Orange Grove	Shade Structure	Complete
Palm ES	Shade Structure	Complete
Sparks ES	Shade Structure	Complete
Sparks MS	Shade Structure	Complete
Sunset	Shade Structure	Complete
Grandview	Sliding Door Closure	Complete
Sierra Vista	Title I Logo	Complete
Sparks ES	Title I Logo	Complete


New School Signs

Proposed Design for Concrete Monument



New School Benches

Proposed Design

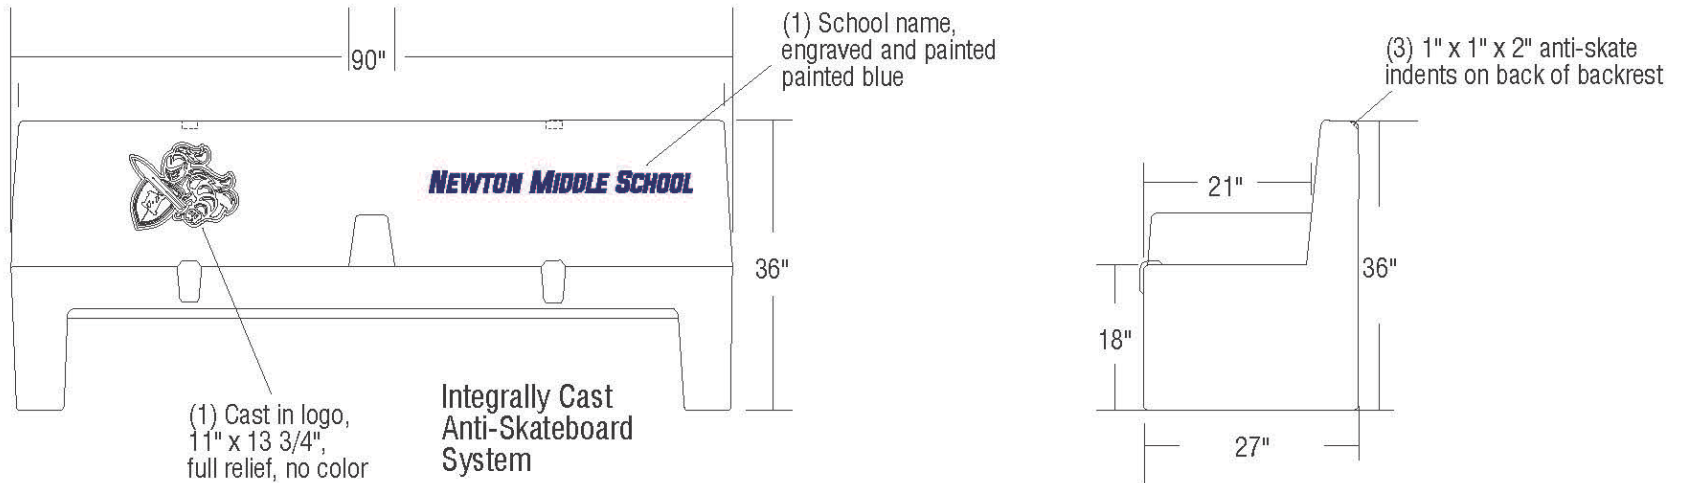



In Progress: Major Projects

2016-2017

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wilson HS	Artificial Track and Field	Complete	Complete	Complete	In Progress	4/30/2017	Additional paving to be completed by District
Workman HS	Artificial Track and Field Design	In Progress					Schematic Design review in process. Presentation to Board at April meeting. Site meetings to begin after Spring Break.
Workman ES	Artificial Turf Replacement	N/A	N/A	Complete	Complete	3/15/2017	
Wilson HS	Athletic Field Irrigation	N/A	N/A	Complete	In Progress	6/30/2017	
District Office	C Building Walkways & Parking	In Progress	N/A				
District Office	Compressed Natural Gas (CNG) Fuel Station	Complete	N/A	Complete	In Progress	6/30/2017	City of Industry Planning Permit approved. LA County Building and Safety permit in Progress
Los Altos HS	Dance Floor Replacement	N/A	N/A	Complete	Complete	3/20/2017	
Cedarlane	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules
Grazide	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules
Los Robles	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Sparks ES	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules
Sunset	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules
Valinda	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules
Wing Lane	Elementary Playground Surfacing	N/A	N/A	Complete	In Progress	5/31/2017	Delayed by impact of rain on project schedules
Bixby	Exterior Painting	N/A	N/A	Complete		6/30/2017	
Fairgrove	Exterior Painting	N/A	N/A	Complete		6/30/2017	
Lassalette	Exterior Painting	N/A	N/A	Complete	In Progress	6/30/2017	
Los Altos HS	Exterior Painting	N/A	N/A	Complete		6/30/2017	
Valinda	Exterior Painting	N/A	N/A	Complete		6/30/2017	
Dibble	Fire Alarm Replacement	Complete	N/A	In Progress		4/30/2017	
District Office	Fire Alarm Replacement	Complete	N/A	In Progress		5/15/2018	Combined with HVAC Bid
Facilities	Fire Alarm Replacement	Complete	N/A	Complete	In Progress	4/30/2017	
Willow	Fire Alarm Replacement	Complete	In Progress			7/15/2017	Submitted to City of La Puente for Approval
La Puente HS	Gymnasium Scoreboards	Complete	N/A	Complete	In Progress	3/30/2017	

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wilson HS	Gymnasium Scoreboards	Complete	N/A	Complete	In Progress	3/30/2017	
Fairgrove	Head Start Classroom Replacement	In Progress				7/20/2017	
Baldwin	Irrigation Replacement	In Progress					
Cedarlane	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Del Valle	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Grazide	Irrigation Replacement	In Progress					
Los Molinos	Irrigation Replacement	In Progress					
Nelson	Irrigation Replacement	Complete	N/A	Complete	In Progress	8/1/2017	Moved due to conflicts with other work
Sierra Vista	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
La Puente HS	Lower Field Irrigation	In Progress					
Workman HS	Main Stairway Replacement	In Progress				7/31/2017	Shifted to tBP Architects
Baldwin	MPR Lighting	N/A	N/A			6/30/2017	
Bixby	MPR Lighting	N/A	N/A			6/30/2017	
California	MPR Lighting	N/A	N/A			6/30/2017	
Del Valle	MPR Lighting	N/A	N/A			6/30/2017	

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Grazide	MPR Lighting	N/A	N/A			6/30/2017	
Kwis	MPR Lighting	N/A	N/A			6/30/2017	
Los Altos ES	MPR Lighting	N/A	N/A			6/30/2017	
Los Molinos	MPR Lighting	N/A	N/A			6/30/2017	
Los Robles	MPR Lighting	N/A	N/A			6/30/2017	
Nelson	MPR Lighting	N/A	N/A			6/30/2017	
Palm ES	MPR Lighting	N/A	N/A			6/30/2017	
Sparks ES	MPR Lighting	N/A	N/A			6/30/2017	
Sunset	MPR Lighting	N/A	N/A			6/30/2017	
Temple	MPR Lighting	N/A	N/A			6/30/2017	
Wing Lane	MPR Lighting	N/A	N/A			6/30/2017	
Workman ES	MPR Lighting	N/A	N/A			6/30/2017	
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2017	
Los Altos HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2017	
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2017	
District Office	NCS & Purchasing Offices	In Progress	N/A	Complete	In Progress	5/30/2017	
La Puente HS	New Kitchen	Complete				8/1/2018	Board Presentation March 23, 2017
La Puente HS	New Pool and Dressing Area	Complete				10/30/2018	Board Presentation March 23, 2017
California	Office entry doors and gates	In Progress				7/15/2017	
Del Valle	Office entry doors and gates	In Progress				7/15/2017	
Grandview	Office entry doors and gates	Complete	Complete			7/15/2017	

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Orange Grove	Office entry doors and gates	In Progress				7/15/2017	
Temple	Office entry doors and gates	In Progress				7/15/2017	
Workman ES	Office entry doors and gates	In Progress				7/15/2017	
District Office	Paving – All Parking areas	N/A	N/A	Complete	In Progress	6/30/2017	60% Complete. Holding remaining work for CNG station
California	Paving – Demolition of Cottage, add parking	N/A	N/A	Complete	In Progress	6/30/2017	
Workman HS	Paving and Striping - Paving Between Gymnasium	N/A	N/A	Complete	In Progress		On hold pending track and field
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress		5/15/2018	Moved to coordinate with relocation of Purchasing and NCS
Los Altos ES	Portable Classroom Addition	In Progress				7/25/2017	
Los Molinos	Portable Classroom Addition	In Progress				7/25/2017	
Wedgeworth	Portable Classroom Addition	In Progress				7/25/2017	
Newton	Portable Classroom Replacement	Complete	Complete	In Progress		4/15/2017	Delayed for DSA and Local Fire Approval
Baldwin	School Entry Signs	In Progress	N/A			7/30/2017	
Bixby	School Entry Signs	In Progress	N/A			7/30/2017	
California	School Entry Signs	In Progress	N/A			7/30/2017	
Cedarlane	School Entry Signs	In Progress	N/A			7/30/2017	
Del Valle	School Entry Signs	In Progress	N/A			7/30/2017	
Dibble	School Entry Signs	In Progress	N/A			7/30/2017	
District Office	School Entry Signs	In Progress	N/A			7/30/2017	

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Fairgrove	School Entry Signs	In Progress	N/A			7/30/2017	
Grandview	School Entry Signs	In Progress	N/A			7/30/2017	
Grazide	School Entry Signs	In Progress	N/A			7/30/2017	
Kwis	School Entry Signs	In Progress	N/A			7/30/2017	
La Puente HS	School Entry Signs	In Progress	N/A			7/30/2017	
Lassalette	School Entry Signs	In Progress	N/A			7/30/2017	
Los Altos ES	School Entry Signs	In Progress	N/A			7/30/2017	
Los Altos HS	School Entry Signs	In Progress	N/A			7/30/2017	
Los Molinos	School Entry Signs	In Progress	N/A			7/30/2017	
Los Robles	School Entry Signs	In Progress	N/A			7/30/2017	
Mesa Robles	School Entry Signs	In Progress	N/A			7/30/2017	
Nelson	School Entry Signs	In Progress	N/A			7/30/2017	
Newton	School Entry Signs	In Progress	N/A			7/30/2017	
Orange Grove	School Entry Signs	In Progress	N/A			7/30/2017	
Palm ES	School Entry Signs	In Progress	N/A			7/30/2017	
Sierra Vista	School Entry Signs	In Progress	N/A			7/30/2017	
Sparks ES	School Entry Signs	In Progress	N/A			7/30/2017	
Sparks MS	School Entry Signs	In Progress	N/A			7/30/2017	
Stimson LC	School Entry Signs	In Progress	N/A			7/30/2017	
Sunset	School Entry Signs	In Progress	N/A			7/30/2017	
Temple	School Entry Signs	In Progress	N/A			7/30/2017	
Valinda	School Entry Signs	In Progress	N/A			7/30/2017	
Valley Alt HS	School Entry Signs	In Progress	N/A			7/30/2017	
Wedgeworth	School Entry Signs	In Progress	N/A			7/30/2017	

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wilson HS	School Entry Signs	In Progress	N/A			7/30/2017	
Wing Lane	School Entry Signs	In Progress	N/A			7/30/2017	
Workman ES	School Entry Signs	In Progress	N/A			7/30/2017	
Workman HS	School Entry Signs	In Progress	N/A			7/30/2017	
Baldwin	Shade Structure	Complete	Complete	Complete	Complete	3/15/2017	
California	Shade Structure	Complete	Complete	Complete	In Progress	4/6/2017	Delayed by rain
Cedarlane	Shade Structure	Complete	Complete	Complete		5/30/2017	On hold for updated survey
District Office	Shade Structure	In Progress				5/30/2017	Delayed by rain
Facilities	Shade Structure	In Progress				5/30/2017	Delayed by rain
Grandview	Shade Structure	Complete	Complete	Complete	Complete	3/31/2017	
Kwis	Shade Structure	Complete	Complete	Complete	Complete	3/31/2017	
Los Altos ES	Shade Structure	Complete	Complete	Complete	In Progress	4/15/2017	Delayed by rain
Sierra Vista	Shade Structure	Complete	Complete	Complete	In Progress	4/15/2017	Delayed by rain
Stimson LC	Shade Structure	Complete	Complete	Complete		6/30/2017	Coordinating install with school schedule
Temple	Shade Structure	Complete	Complete	Complete	Complete	4/15/2017	
Valinda	Shade Structure	Complete	Complete	Complete	In Progress	4/15/2017	Delayed by rain
Valley Alt HS	Shade Structure	Complete	Complete	Complete	In Progress	4/15/2017	Delayed by rain
Wedgeworth	Shade Structure	Complete	Complete	Complete	In Progress	4/15/2017	Delayed by rain
Wing Lane	Shade Structure	Complete	Complete	Complete	In Progress	3/31/2017	Delayed by rain
Workman ES	Shade Structure	Complete	Complete	Complete		6/30/2017	Relocated at request of the school

School Environment

Business Services: Current Projects

Major Projects

2016-17 year as of March 23, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Workman HS	Shade Structure	Complete	Complete	Complete	In Progress	4/15/2017	Unforeseen conditions delayed footings
Los Altos HS	Shade structure - Concession Stand	Complete	Complete	Complete	In Progress	3/31/2017	Delayed by rain
Wilson HS	Shade structure - Concession Stand	Complete	Complete	Complete	In Progress	4/28/2017	Delayed by rain
Amar	Shade Structures - Early Childhood	Complete	Complete	In Progress		3/31/2017	
Valinda	Shade Structures – Early Childhood	Complete	Complete	In Progress		3/31/2017	
Los Altos HS	Sound & Media System	Complete	Complete	On Hold			Reviewing funding
Wilson HS	Sound & Media System	Complete	Complete	On Hold			Reviewing funding
District Office	Textbook and Technology Storage	In Progress	N/A	In Progress		11/21/2017	
Willow	Upgrades for ADA Compliance	Complete	N/A	Complete	Complete	3/17/2017	

Shade Structure

Temple Academy



Shade Structure

Grandview Academy



School Environment

Business Services



Next Report – April 2017
