
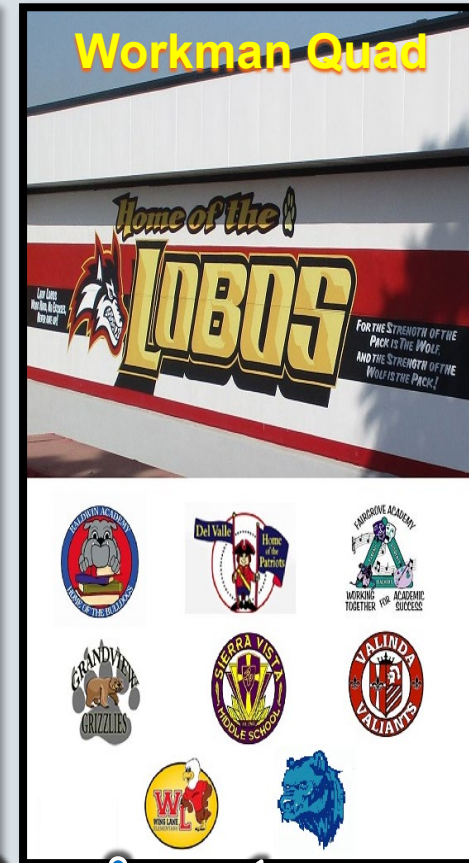


HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Business Services

Regular Board Meeting
September 23, 2021



Projects Completed as of September 23, 2021

Wilson HS –Solar Panel Arrays Installed & Tied In



2



The background of the slide features a close-up, high-angle shot of several rolled-up architectural blueprints. The blueprints are unrolled slightly, revealing detailed technical drawings with various lines, dimensions, and annotations. They are resting on a light-colored, vertically-grained wooden surface. The lighting is soft and even, highlighting the texture of the paper and the wood.

PROJECTS IN PROGRESS

2021/2022

Projects In Progress as of September 23, 2021

4

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Willow AS	Conference (South) Room Flooring	Complete	N/A	Pending		Adult Ed.	12/31/2021
La Puente HS	Gym & Locker Room HVAC	Complete	Complete	Complete		Facilities	12/31/2021
Wilson HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Facilities	12/31/2021



Projects In Progress as of September 23, 2021

5

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
La Puente HS	New Kitchen	Complete	Complete	Complete	In Progress	Facilities	12/31/2021
La Puente HS	Pool Project	Complete	Complete	Complete	In Progress	Facilities	12/31/2021



La Puente HS Kitchen: New Kitchen Hallway, Arrival of Door Frames & Finished Metal Framing, Drywall, Insulation Installed



Projects In Progress as of September 23, 2021

6

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Grandview	Roofing Restoration	N/A	N/A	N/A	In Progress	Facilities	10/30/2021
Los Altos HS	Roofing Restoration	N/A	N/A	N/A	In Progress	Facilities	10/30/2021
Workman ES	Roofing Restoration (Rm:13-17)	N/A	N/A	N/A		Facilities	10/30/2021




Projects In Progress as of September 23, 2021

7

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Grazide ES	Perimeter Chain-link Fence with bollard Placement	Hold	N/A	Hold		Pending Approval	
Workman HS	Artificial Track and Field Phase II (Submitted to DSA. (Next Steps = CEQA))	Complete	Complete	Pending	Estimate Cost \$16.5M	Pending Approval	



Erosion

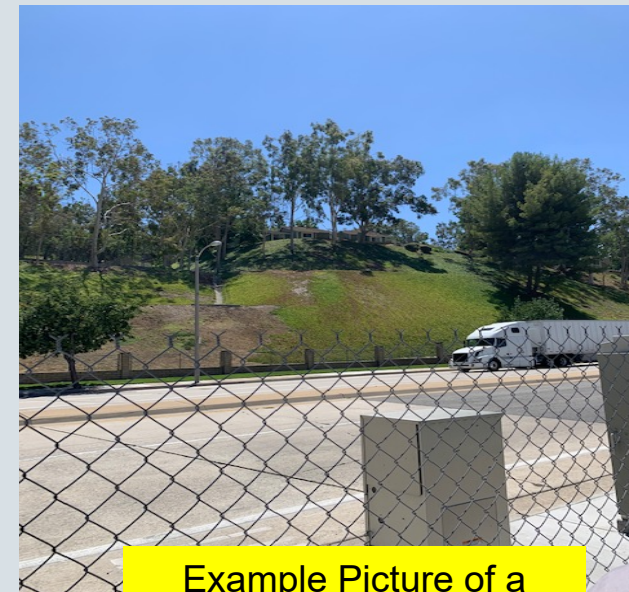

Example Picture of a Slope with Irrigation

**LA County Traffic Division Assisting
with Signal Controls**



Projects with Division of State Architect (DSA) Waiting on Approval

8

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Wedgeworth	Permanent School	Complete	In Progress (Revisions for K-5 Pending Approval)		01/2022	

Projects in Design

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Los Altos HS	Gym & Locker Room HVAC	In Progress				12/1/2021
Workman HS	Gym & Locker Room HVAC	In Progress				12/1/2021
Performing Arts Center	Partnership with LA County Aquatic Center	In Progress				2022/2023

PROJECT COMPLETE LIST



9

SLIDE 1 OF 1

Site	Item Description	Funding Source
Bixby	Ceiling Tiles & Lighting	Facilities
Sunset OH	Ceiling Tiles & Lighting	Facilities
Orange Grove MS	Interior Painting (Main Office)	Facilities
Valley HS	Interior Painting (Room 5 & 6)	Facilities
La Puente HS	Lockers	Facilities
Wilson HS	Pool Water Heater Install	Facilities
Cedarlane	Roofing	Facilities
Nelson	Roofing	Facilities
Newton	Roofing	Facilities
Sparks MS	Roofing	Facilities
Workman ES	Roofing (Cafeteria)	Facilities
Los Altos HS	Solar Panel Arrays	Facilities
Willow AS	Solar Panel Arrays	Facilities
Workman HS	Solar Panel Arrays	Facilities

Next Report – October 28, 2021

