


# School Site Improvement Projects



# Business Services



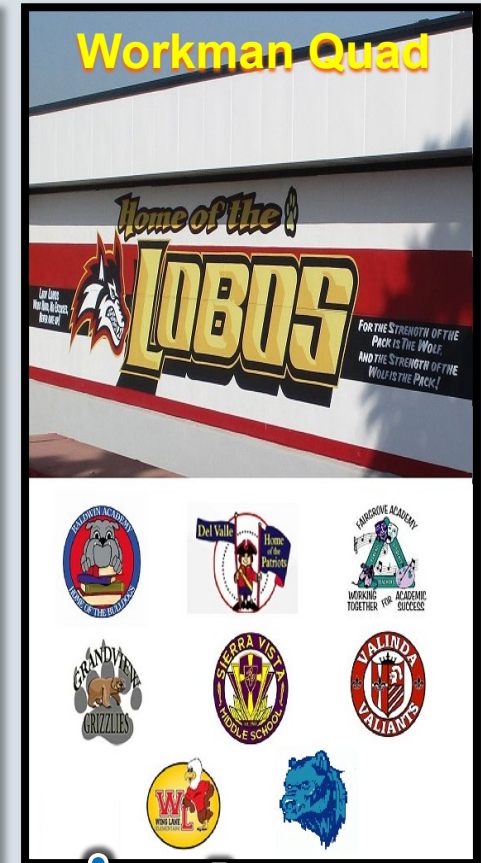

**NEW!**

2

# Completed Projects

2020-2021



**COMPLETED**





# Projects Completed as of July 22, 2021

## Bixby – Ceiling Tiles & Lighting

3



Before



After







# Projects Completed as of July 22, 2021

## Cedarlane – Roofing

4







# Projects Completed as of July 22, 2021

## Nelson – Roofing

5







# Projects Completed as of July 22, 2021

## Sparks MS – Roofing

6







# Projects Completed as of July 22, 2021

## Wilson HS – Installation of Pool Heater

7



8

# Projects In Progress

2021-2022






# Projects In Progress as of July 22, 2021

9

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Cedarlane K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	Measure BB	7/30/2021
Mesa Robles K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	Measure BB	7/30/2021
Willow AS	Conference (South) Room Renovation	Complete	N/A	Complete	In Progress	Adult Ed.	7/30/2021
Wilson HS	Fire Alarms	Complete	Complete	Complete	In Progress	Measure BB	8/1/2021
La Puente HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Facilities	12/31/2021
Wilson HS	Gym & Locker Room HVAC	Complete	Complete	Complete	In Progress	Facilities	12/31/2021
La Puente HS	New Kitchen	Complete	Complete	Complete	In Progress	Facilities	12/21/2021
La Puente HS	Pool Project	Complete	Complete	Complete	In Progress	Facilities	8/9/2021

La Puente HS Pool – Installing rebar  
@ southwest corner

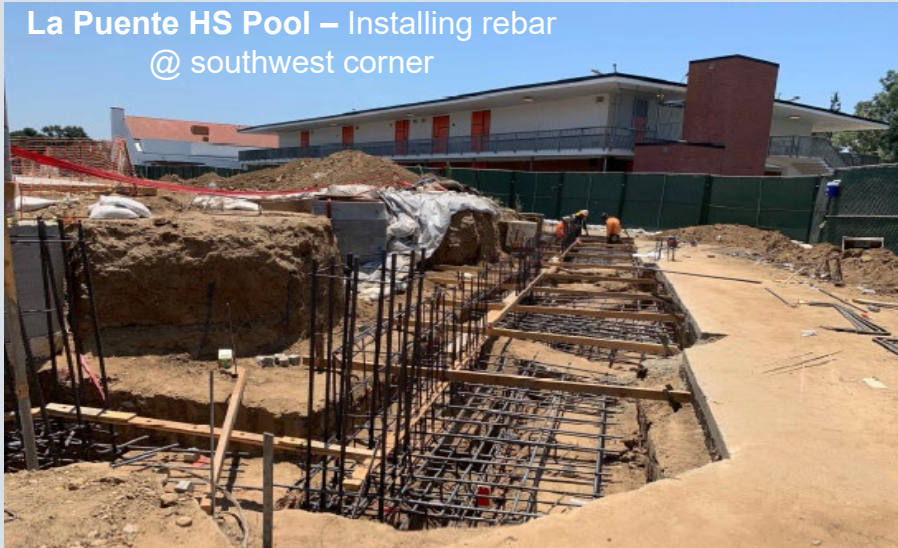

La Puente HS Kitchen: Installing ceiling

# Projects In Progress as of July 22, 2021

10

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
<b>Grandview</b>	Roofing Restoration (Wing10/20/Library/Office/PE)	N/A	N/A	N/A	<b>In Progress</b>	Facilities	<b>7/30/2021</b>
Newton MS	Roofing Restoration (Bldg: D, Band Room)	N/A	N/A	N/A	In Progress	Facilities	<b>7/30/2021</b>
Workman ES	Roofing Restoration (Cafeteria, (Rm:13-17)	N/A	N/A	N/A	In Progress	Facilities	<b>7/30/2021</b>











Changes And Progress Since Last Report - Blue



# Projects In Progress as of July 22, 2021




11

Site		Item Description		Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Los Altos HS		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	7/30/2021
Willow		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	8/15/2021
Wilson HS		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	8/15/2021
Workman HS		Solar Panel Installation		N/A	Complete	N/A	In Progress	NA	7/30/2021



Changes And Progress Since Last Report - Blue

# Projects **READY FOR PROCUREMENT**



12

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Baldwin	Bottle Filling Stations	Complete	Complete			8/1/2021
Bixby	Bottle Filling Stations	Complete	Complete			8/1/2021
California	Bottle Filling Stations	Complete	Complete			8/1/2021
Del Valle	Bottle Filling Stations	Complete	Complete			8/1/2021
Dibble AS	Bottle Filling Stations	Complete	Complete			8/1/2021
District Office	Bottle Filling Stations	Complete	Complete			8/1/2021
Grandview K-8	Bottle Filling Stations	Complete	Complete			8/1/2021
Grazide	Bottle Filling Stations	Complete	Complete			8/1/2021
Hudson AS	Bottle Filling Stations	Complete	Complete			8/1/2021
Kwis ES	Bottle Filling Stations	Complete	Complete			8/1/2021
La Puente HS	Bottle Filling Stations	Complete	Complete			8/1/2021
Lassalette K-8	Bottle Filling Stations	Complete	Complete			8/1/2021
Los Robles	Bottle Filling Stations	Complete	Complete			8/1/2021



Changes And Progress Since Last Report - Blue



# Projects **READY FOR PROCUREMENT & In Progress**

13

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Date
Newton	Bottle Filling Stations	Complete	Complete			Measure BB	8/1/2021
Palm ES	Bottle Filling Stations	Complete	Complete			Measure BB	11/1/2021
Sparks ES	Bottle Filling Stations	Complete	Complete			Measure BB	8/1/2021
Stimson LC	Bottle Filling Stations	Complete	Complete			Measure BB	11/1/2021
Wedgeworth	Bottle Filling Stations	Complete	Complete			Measure BB	8/1/2021
Wilson HS	Bottle Filling Stations	Complete	Complete			Measure BB	8/1/2021
Wing Lane	Bottle Filling Stations	Complete	Complete			Measure BB	8/1/2021
Workman ES	Bottle Filling Stations	Complete	Complete			Measure BB	8/1/2021
Grazide	Exterior Painting	N/A	N/A			Facilities	8/1/2021
Dibble AS	Fire Alarms	Complete	N/A			Adult Ed.	8/1/2021
District Office	Fire Alarms	Complete	N/A			Facilities	8/1/2021
La Puente HS	Fire Alarms	Complete	Complete			Measure BB	8/1/2021
Willow AS	Fire Alarms	Complete	Complete			Adult Ed.	8/15/2021
Workman HS	Fire Alarms	Complete	Complete			Measure BB	8/1/2021
Grazide ES	Perimeter Chain-link Fence with bollard Replacement	In Progress	N/A	<b>In Progress</b>		Facilities	8/30/2021



# Projects with Division of State Architect (DSA) Waiting on Approval

14

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Workman HS	Artificial Track and Field Phase II (Submitted to DSA. <b>(PENDING CEQA)</b> )	Complete	Complete			10/1/2021
Orange Grove	Bottle Filling Stations	Complete	In Progress			10/1/2021
Palm Canyon	Bottle Filling Stations	Complete	Complete			10/1/2021
Sierra Vista	Bottle Filling Stations	Complete	In Progress			10/1/2021
Sparks MS	Bottle Filling Stations	Complete	Complete			10/1/2021
Valinda	Bottle Filling Stations	Complete	Complete	Complete		10/1/2021
Valley HS	Bottle Filling Stations	Complete	In Progress			10/1/2021
Willow AS	Bottle Filling Stations	Complete	In Progress			10/1/2021
Workman HS	Bottle Filling Stations	Complete	Complete	Complete		10/1/2021
Wedgeworth	Permanent School	Complete	In Progress			



# Projects in Design

15

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date
Los Altos HS	Fire Alarms	Complete				8/1/2021
Los Altos HS	Gym & Locker Room HVAC	In Progress				8/1/2021
Workman HS	Gym & Locker Room HVAC	In Progress				8/1/2021



Changes And Progress Since Last Report - Blue

# Workman High School Library

## Interested Donor

16



### Conceptual Design

- Flooring - Vinyl
- Interior Painting





**21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2  
BOND UPDATES**
