
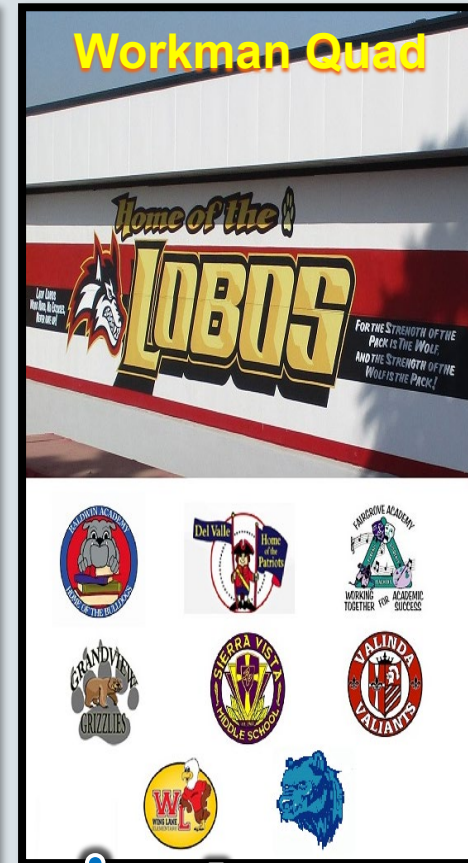


HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT QUADS



School Site Improvement Projects

Business Services

Regular Board Meeting
August 26, 2021



NEW!

2

Completed Projects

2021-2022

COMPLETED



Projects Completed as of August 26, 2021

Sunset OH – Ceiling Tiles & Lighting

3





Projects Completed as of August 26, 2021

La Puente HS – New Lockers

4





Projects Completed as of August 26, 2021

Orange Grove MS – Interior Painting (Main Office)

5





Projects Completed as of August 26, 2021

Valley HS – Interior Painting for New Independent Studies for Elementary Classrooms (Room 5 & 6)


6



Room 5



Room 6

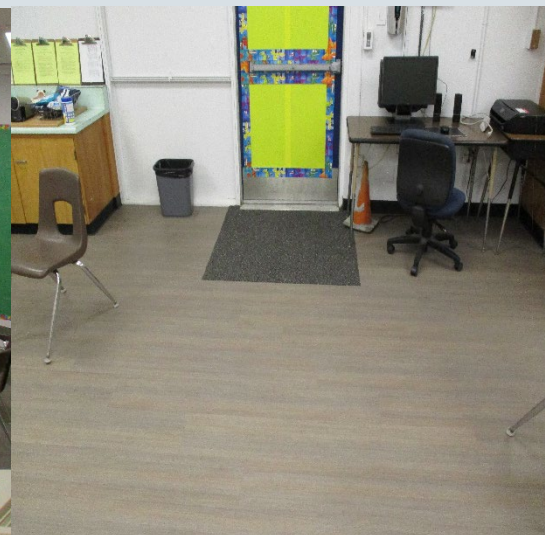



Projects Completed as of August 26, 2021

Newton – Roofing

7





Projects Completed as of August 26, 2021

Workman ES – Roofing (Cafeteria)

8





Projects Completed as of August 26, 2021

Los Altos HS –Solar Panel Arrays Installed

(Tie in pending and target date is TBD)



9



NEW!

Projects Completed as of August 26, 2021

Willow AS – Solar Panel Arrays Installed

(Tie in pending and target date is August 2021)



10





Projects Completed as of August 26, 2021

Workman HS – Solar Panel Arrays Installed

(Tie in pending and target date is TBD)



11



12

Projects In Progress

2021-2022



Projects In Progress as of August 26, 2021



13

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Date |
|-----------|------------------------------------|-----------------|--------------|-------------|-------------|----------------|-------------|
| Willow AS | Conference (South) Room Renovation | Complete | N/A | Complete | In Progress | Adult Ed. | 10/30/2021 |
| Wilson HS | Solar Panel Installation | N/A | Complete | N/A | In Progress | NA | 9/1/2021 |



Projects In Progress as of August 26, 2021

14

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Date |
|--------------|------------------------|-----------------|--------------|-------------|-------------|----------------|-------------|
| La Puente HS | Gym & Locker Room HVAC | Complete | Complete | Complete | In Progress | Facilities | 12/31/2021 |
| Wilson HS | Gym & Locker Room HVAC | Complete | Complete | Complete | In Progress | Facilities | 12/31/2021 |



Projects In Progress as of August 26, 2021

15

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Date |
|--------------|------------------|-----------------|--------------|-------------|-------------|----------------|-------------|
| La Puente HS | New Kitchen | Complete | Complete | Complete | In Progress | Facilities | 12/31/2021 |
| La Puente HS | Pool Project | Complete | Complete | Complete | In Progress | Facilities | 12/31/2021 |



Projects In Progress as of August 26, 2021

16

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Date |
|-----------|--|-----------------|--------------|-------------|-------------|----------------|-------------|
| Grandview | Roofing Restoration (Wing10/20/Library/Office/PE) | N/A | N/A | N/A | In Progress | Facilities | 8/30/2021 |



Changes And Progress Since Last Report - Blue

Projects In Progress as of August 26, 2021

17

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Date |
|--------------|--------------------------------|-----------------|--------------|-------------|-------------|----------------|-------------|
| Los Altos HS | Roofing Restoration | N/A | N/A | N/A | In Progress | Facilities | 9/1/2021 |
| Workman ES | Roofing Restoration (Rm:13-17) | N/A | N/A | N/A | | Facilities | 8/30/2021 |



LOS ALTOS HS - Roofing



Changes And Progress Since Last Report - Blue

Projects READY FOR PROCUREMENT & In Progress

18

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Funding Source | Target Date |
|------------|---|-----------------|--------------|-------------|--|----------------|-------------|
| Grazide ES | Perimeter Chain-link Fence with bollard Replacement | In Progress | N/A | In Progress | Hold (Pending Investigation with County) | Facilities | |



Projects with Division of State Architect (DSA) Waiting on Approval

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Target Date |
|------------|---|-----------------|------------------------|-------------|-----------|-------------|
| Workman HS | Artificial Track and Field Phase II (Submitted to DSA. (PENDING CEQA) | Complete | Complete | | | 12/1/2021 |
| Wedgeworth | Permanent School | Complete | In Progress (Revision) | | 01/2022 | |

Projects in Design

| Site | Item Description | Architect Plans | DSA Approval | Procurement | Construct | Target Date |
|--------------|------------------------|-----------------|--------------|-------------|-----------|-------------|
| Los Altos HS | Gym & Locker Room HVAC | In Progress | | | | 11/1/2021 |
| Workman HS | Gym & Locker Room HVAC | In Progress | | | | 11/1/2021 |

PROJECT COMPLETE LIST



19

SLIDE 1 OF 1

| Site | Item Description |
|-----------|---------------------------|
| Bixby | Ceiling Tiles & Lighting |
| Cedarlane | Roofing |
| Nelson | Roofing |
| Sparks MS | Roofing |
| Wilson HS | Pool Water Heater Install |

Next Report – September 23, 2021

