






## 21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS | PHASES 1 & 2 **BOND UPDATES**

October 22, 2020

# PROJECT STATUS

## MESA ROBLES SCHOOL

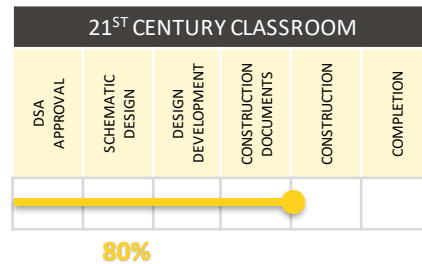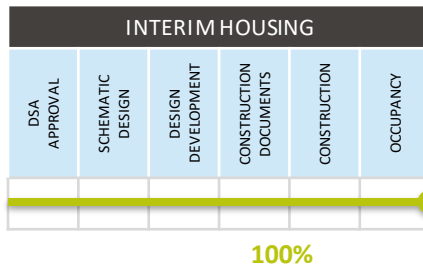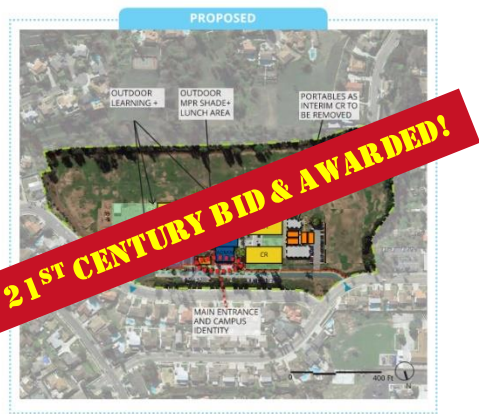

### NOTES:

- Interim Classrooms; ready for move in. Final Punch List 98% Complete
- Data installation complete
- Fire Alarm installation complete
- Final DSA certification underway
- Construction Documents for the 21<sup>st</sup> Century Classroom Improvements Approved by DSA
- Contract awarded October 8, 2020
- Notice to Proceed issued October 19, 2020

# 21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS

## **MESA ROBLES SCHOOL**

PROJECT KICK OFF & GROUND- BREAKING THIS WEEK

IMPROVEMENTS UNDERWAY

DRINKING FOUNTAIN

CLASSROOM TRANSFORMATIONS

# 21<sup>st</sup> CENTURY CLASSROOM IMPROVEMENTS

## MESA ROBLES SCHOOL

### ADA ACCESS IMPROVEMENTS



IMPROVEMENTS UNDERWAY




PATH OF TRAVEL IMPROVEMENTS



# MESA ROBLES SCHOOL



## Middle School Side

## Elementary School Side

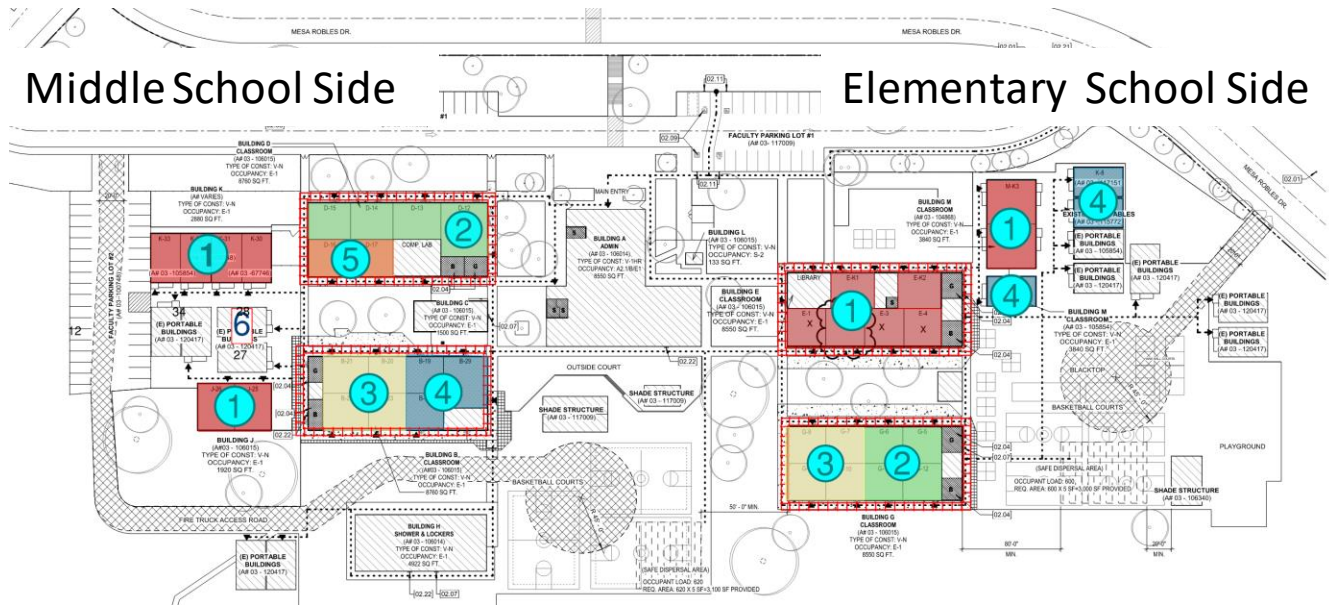

## PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

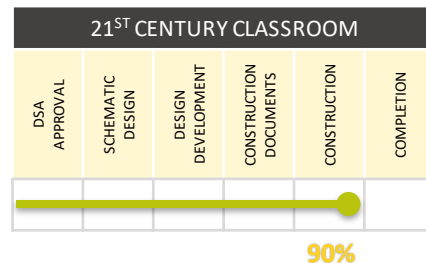

## NOTES:

- Interim Housing Project is 100% complete
- 21<sup>st</sup> Century Walkways Complete
- Access Ramp Roughed-in and Awaiting Concrete Placement
- Phase 1 Punch List Generated: Corrections in Progressing
- Phase 2 & 3 Running in Tandem Nearing Completion Finishes Completed
- Finish Plumbing Electrical and Data Installing

PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

## CLASSROOM INTERIORS PUNCH LIST



PUNCH WALK PHASE 1

PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

## CLASSROOM INTERIORS PUNCH LIST




PUNCHLIST WITH ARCHITECT AND CONTRACTORS SITE CLEAN UP



PROJECT STATUS

# LOS ALTOS ELEMENTARY SCHOOL

CLASSROOM LIGHTING AND FIRE ALARM BY  
UNIT COST PROVIDERS BEGAN LAST WEEK

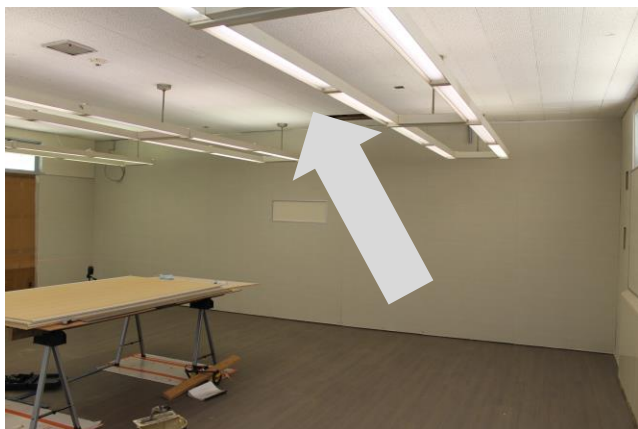

LIGHTING DEMO BEGINNING



LIGHTING DEMO BEGINNING

## PROJECT STATUS

# NELSON ELEMENTARY SCHOOL



21 <sup>ST</sup> CENTURY CLASSROOM						
DSA APPROVAL	SCHEMATIC DESIGN	DESIGN DEVELOPMENT	CONSTRUCTION DOCUMENTS	CONSTRUCTION	COMPLETION	

90%

## NOTES:

- 21<sup>st</sup> Century Classroom Improvements Construction Notice to proceed on 6-8-20
- Phase 1 Punch List Issued By Architect
- Construction Phases 2 and 3 nearing completion
- Site Concrete Completed
- Lighting and Fire Alarm Began Last Week

PROJECT STATUS

# NELSON ELEMENTARY SCHOOL

SITE WORK COMPLETION, FIRE ALARM & LIGHTING REPLACEMENT BEGAN



# WORKMAN ELEMENTARY SCHOOL



NOTES:

- 21<sup>st</sup> Century Classroom Improvements started construction 6-15-2020; Construction Phases 2 & 3 in progress
- Site work paving installation completed
- Electrical rough-in 95% complete; Finish Electrical 85% complete
- Plumbing rough-in complete, Casework fabrication complete installed countertops in fabrication. Finish plumbing pending precursors
- Flooring installation complete permanent buildings, portables demo is 100% complete installation of new 33% complete
- Installation of tackable wall board is completed
- Painting at relo classroom interiors underway

PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL

## CONSTRUCTION PHASES 2 & 3




PAVING AND DRAINAGE DEMOED, AND PREP FOR PAVING AND SURFACE FLOW LINE



PROJECT STATUS

# WORKMAN ELEMENTARY SCHOOL



PHASES 1 THROUGH 3

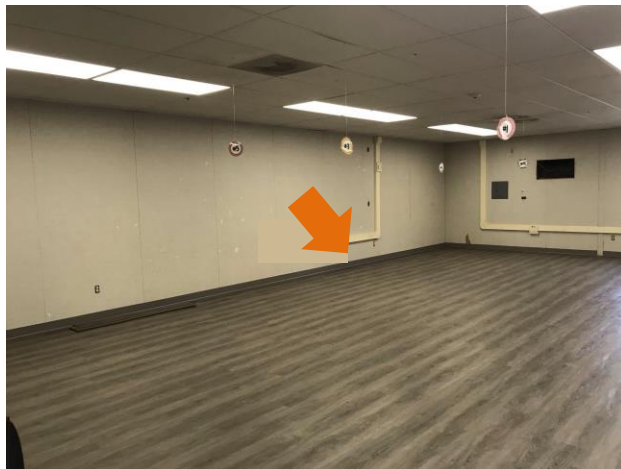

FINISH ELECTRICAL AND DATA INSTALLING

## PROJECT STATUS

# CEDARLANE ACADEMY

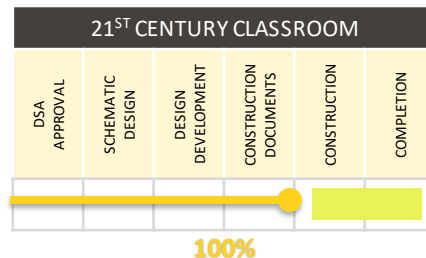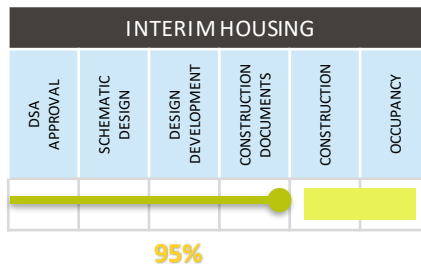


## NOTES:

- Construction Documents for the Interim Housing Project Submitted to DSA for review. DSA approval pending
- 21<sup>st</sup> Century Classroom Improvements Approved by DSA
- Bidding Complete
- Project Awarded
- Notice to Proceed issued October 19, 2020

PROJECT STATUS  
**CEDARLANE ACADEMY**

**START** PHASING PLAN & INTERIM HOUSING

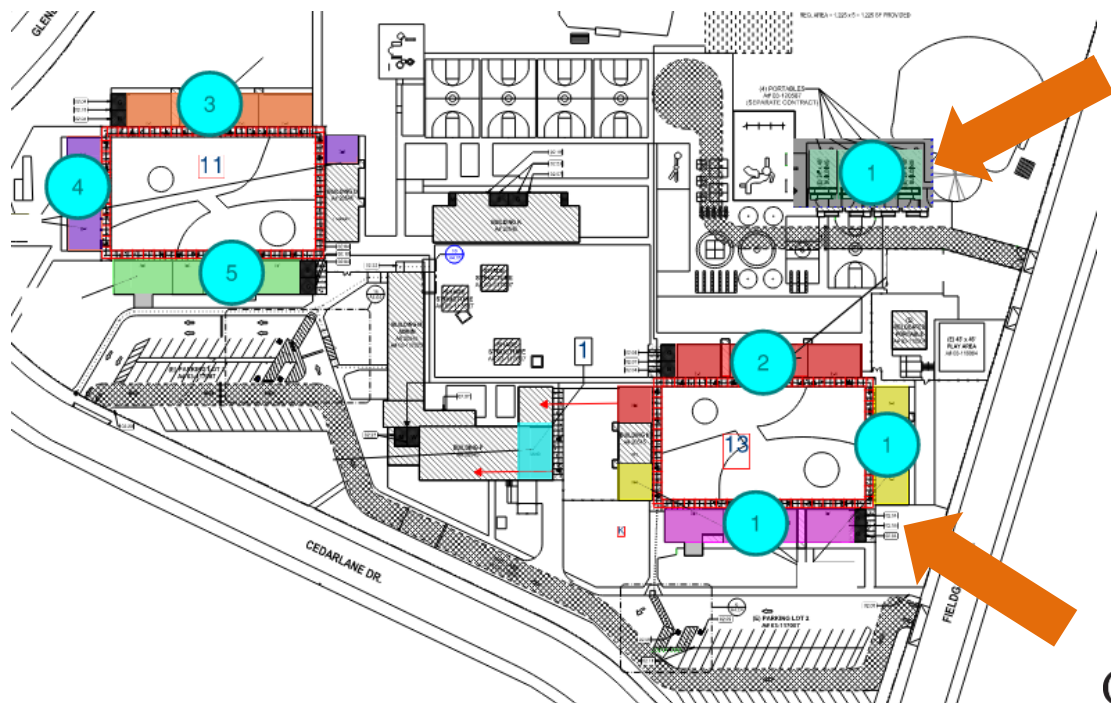

## PROJECT STATUS

# CEDARLANE ACADEMY

## SITE IMPROVEMENTS & PATH OF TRAVEL TO BE ADDRESSED




## 21<sup>ST</sup> CENTURY CLASSROOM IMPROVEMENTS TO BE MADE





## PROJECT STATUS




# GRANDVIEW ACADEMY

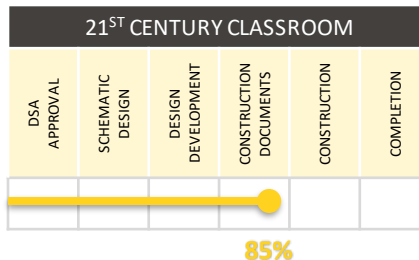

## NOTES:

- 21<sup>st</sup> Century Classroom Project construction documents are 85% complete
- DSA Submittal anticipated after Cumming and District review
- DSA Applications for Grandview are all closed with Certification

## PROJECT STATUS

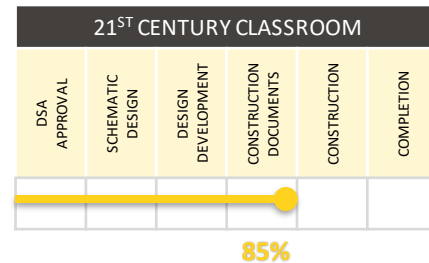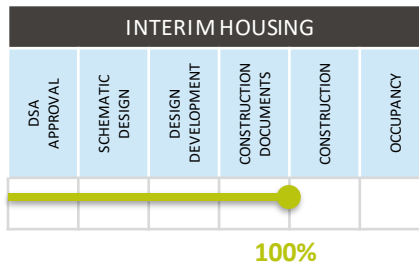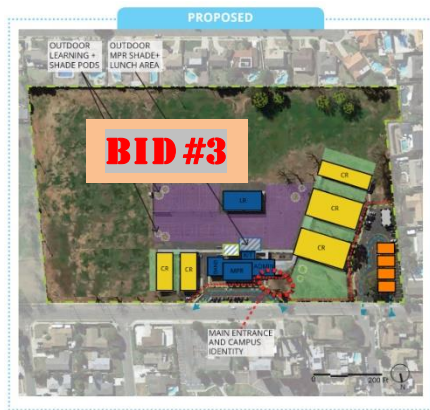


NOTES:

- Interim Housing construction documents are DSA approved
- Temp power installation ready,
- DSA Project Inspector paperwork in process
- **Initial project walk** held October 5
- 21<sup>st</sup> Century DSA Submittal Anticipated in October after Cumming and District review. **Review Completed October 16, 2020**
- DSA approval contingent upon certification of three (3) open DSA applications


## PROJECT STATUS

# SPARKS MIDDLE SCHOOL

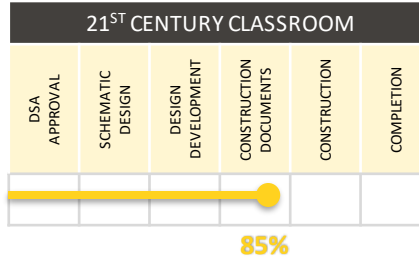

## NOTES:

- Construction Documents for the 21<sup>st</sup> Century Classroom Improvements are 85% complete
- DSA Submittal anticipated November after Cumming and District review
- DSA approval contingent upon certification of three (3) open DSA Applications

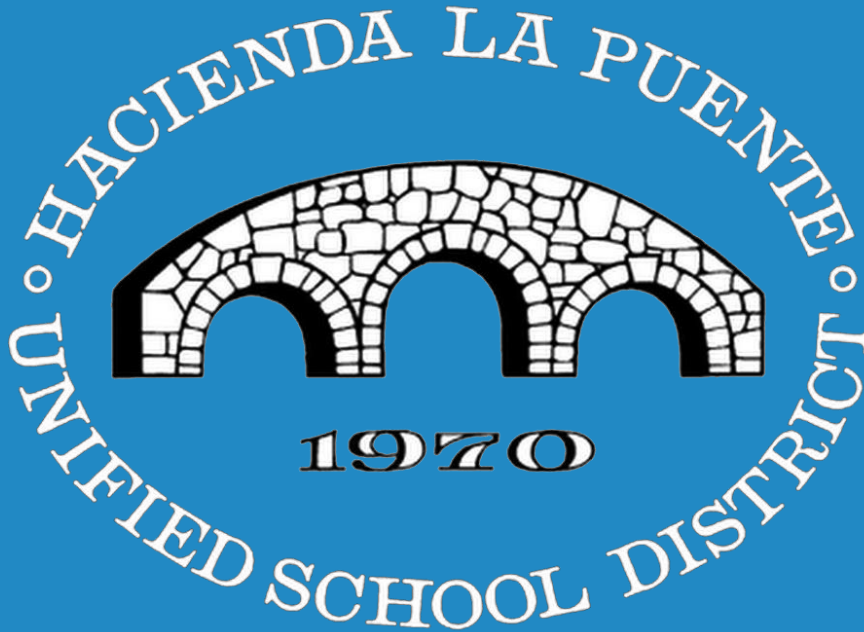

**QUESTIONS & ANSWERS**
