

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site
Improvement Projects

Regular Board Meeting
February 28, 2019

Business Services



Completed Projects

2018-2019

School Environment

Business Services: Completed Projects

Projects Completed as of February 28, 2019

Site	Item Description	Construct
Baldwin	Exterior Painting	Complete
Nelson	Exterior Painting	Complete
Wilson HS	Exterior Painting	Complete
Baldwin ES	Floor Replacement – Headstart	Complete
Sparks ES	Floor Replacement – Headstart	Complete
Workman ES	Floor Replacement – Headstart	Complete
Kwis	Flooring Replacement – Rm 1	Complete
Los Altos HS	Interior Painting: Hacienda/Admin	Complete
Sparks ES	Library Renovation	Complete
Workman HS	Little Theatre Renovation Phase 1	Complete
La Puente HS	Lower Field Irrigation	Complete
Los Altos HS	Music Room Upgrades	Complete
Grandview ES	Office entry doors and gates	Complete
California	Office entry doors and gates	Complete
Orange Grove	Office entry doors and gates	Complete
District Office	Paving – All Parking areas	Complete
Los Altos ES	Portable Classroom Addition	Complete
Wedgeworth	Portable Classroom Addition	Complete

School Environment

Business Services: Completed Projects

Projects Completed as of February 28, 2019

Site	Item Description	Construct
Los Molinos	Roofing replacement – Kinder Wing	Complete
Mesa Robles	Roof Replacement	Complete
Newton	Roof Replacement	Complete
Willow	Roof Replacement	Complete
Orange Grove	School Entry Signs	Complete
Palm Elementary	School Entry Signs	Complete
Wedgeworth	School Entry Signs	Complete
Baldwin	School Entry Signs	Complete
California	School Entry Signs	Complete
Fairgrove	School Entry Signs	Complete
Grandview	School Entry Signs	Complete
Kwis	School Entry Signs	Complete
Nelson	School Entry Signs	Complete
District Office	School Entry Signs	Complete
Bixby	School Entry Signs	Complete
Sierra Vista	School Entry Signs	Complete
Willow	School Entry Signs	Complete
Valley HS	Valley Model Continuation Site Visit Prep	Complete



Projects In Progress

2018-2019

School Environment

Business Services: Current Projects

Projects In Progress as of February 28, 2019

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Workman HS	Artificial Track and Field Phase I	Complete	N/A	Complete	In progress	5/31/2019	Bid awarded 10/11/18. Construction started 10/13/18
Workman HS	Artificial Track and Field Phase II	In Progress					TBP preparing Stadium construction documents based on February 8, 2017 Board direction
District Office	C Building Walkways & Parking	Complete	N/A			8/31/2019	
La Puente HS	Ceiling Tile Repair	N/A	N/A	Complete	In Progress	03/31/2019	Dance room in progress; 95% complete
Dibble	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
District Office	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
Facilities	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
Hudson Adult	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
Palm Canyon	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
Stimson LC	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
Willow Adult Ed	Concrete Benches	N/A	N/A	Complete	In Progress	3/31/2019	
Los Altos HS	CTE Engineering Project	In Progress					Resubmitted to OPSC and CDE
La Puente HS	CTE Project	In Progress					Preparing Submittal CDE
Valley	CTE Project	In Progress					Preparing Submittal CDE
Wilson HS	CTE Project	In Progress					Preparing Submittal CDE
Workman HS	CTE Project	In Progress					Preparing Submittal CDE

School Environment

Business Services: Current Projects

Projects In Progress as of February 28, 2019

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Dibble	Fire Alarm Replacement	Complete	N/A	In Progress		8/31/2019	Fire Alarm Bid in progress
District Office	Fire Alarm Replacement	Complete	N/A	In Progress		8/31/2019	Fire Alarm Bid in progress
Willow - Old	Fire Alarm Replacement	Complete	N/A	Complete	In Progress	8/31/2019	
Willow - New	Fire Alarm Update	Complete	Complete	Complete	In Progress	8/31/2019	
Los Molinos	Floor Replacement - Interior Hallways	N/A	N/A	Complete		6/30/2019	Asbestos Bid Awarded
Wilson HS	Food Science Room	Complete	Complete	Complete	In Progress	03/15/2019	95% Complete
Baldwin	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Cedarlane	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Del Valle	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Grazide	Irrigation Replacement	In Progress	N/A				Reviewing for coordination with possible bond work.
Sierra Vista	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Workman HS	Little Theatre Renovation Phase 2	Complete	N/A	Complete	In Progress	3/31/2019	Complete Except for Flooring

School Environment

Business Services: Current Projects

Projects In Progress as of February 28, 2019

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Baldwin	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Bixby	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
California	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Del Valle	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Grazide	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Kwis	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Los Altos ES	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Los Molinos	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Los Robles	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Nelson	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Palm ES	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Sparks ES	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Sunset	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Temple	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Wing Lane	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Willow	Multipurpose Room Renovation	In Progress	N/A	In Progress	In Progress	3/31/2019	95% complete; Room will be ready for use by end of Feb. 2019
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2019	
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		6/30/2019	
La Puente HS	New Kitchen	Complete	Complete	In Progress		12/31/2019	Bidding to be coordinated with pool

School Environment

Business Services: Current Projects

Projects In Progress as of February 28, 2019

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
La Puente HS	New Pool and Dressing Area	Complete	Complete	In Progress		12/31/2019	DSA Approved August 14, 2018
Del Valle	Office entry doors and gates	Complete	In Progress			7/31/2019	
Temple	Office entry doors and gates	Complete	In Progress			7/31/2019	
Workman ES	Office entry doors and gates	Complete	Complete	Complete	In progress	3/31/2019	
District Office	Office Remodel	N/A	N/A	Complete	In Progress	3/31/2019	Pending PO Estimated start during winter break
California	Paving – Demolition of Cottage, add parking	N/A	N/A	Complete	In Progress	6/30/2019	Cottage has been demo'd; awaiting funding for parking lot
Grazide	Perimeter Wall Replacement	Complete	Complete	In Progress			
Wedgeworth	Permanent School	In Progress				8/1/2021	Schematic Design Presentation to Board 10/25/18
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress		12/31/2019	
Wilson HS	Photoshop Renovation	Complete	Complete	Complete	In Progress	07/31/2019	60% Complete; Flooring and additional renovations to be done over summer

School Environment

Business Services: Current Projects

Projects In Progress as of February 28, 2019

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Cedarlane	Portable Headstart Classroom Addition	Complete	Complete	Complete	In Progress	3/31/2019	90% complete
Grandview	Roof Replacement	Complete	Complete	Complete		5/31/2019	
Workman HS	Roof Replacement	Complete	Complete	Complete	In Progress	5/31/2019	
Del Valle	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Dibble	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Facilities	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Hudson	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Los Robles	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Palm Canyon	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Stimson LC	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Sunset	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Temple	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	
Valley Alt HS	School Entry Signs	N/A	N/A	Complete	In Progress	03/31/2019	


MPR Restroom Renovation

Willow Adult



Site Monuments

Various Sites

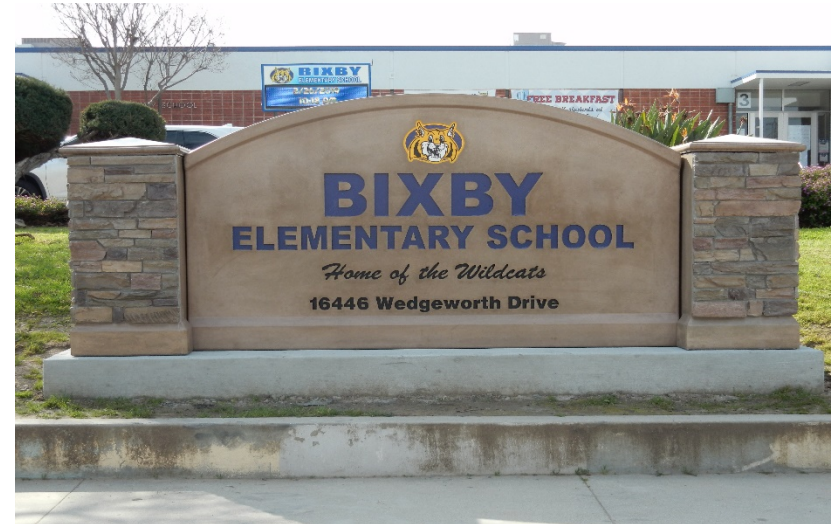

Music Room Upgrades

Los Altos HS

BEFORE

AFTER



Food Science Classroom (95% Complete)

Wilson High School



Decorative Waste Receptacles

Wilson High School





Next Report – March 2019
