

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site
Improvement Projects

Regular Board Meeting
August 23, 2018

Business Services



Completed Projects

2018-2019

School Environment

Business Services: Completed Projects

Projects Completed as of August 23, 2018

Site	Item Description	Construct
District Office	Paving – All Parking areas	Complete
Los Molinos	Roofing replacement – Kinder Wing	Complete
Orange Grove	School Entry Signs	Complete
Palm Elementary	School Entry Signs	Complete
Wedgeworth	School Entry Signs	Complete
Sparks ES	Library Renovation	Complete
Los Altos ES	Portable Classroom Addition	Complete
Baldwin	School Entry Signs	Complete
California	School Entry Signs	Complete
Fairgrove	School Entry Signs	Complete
Grandview	School Entry Signs	Complete
Kwis	School Entry Signs	Complete
Nelson	School Entry Signs	Complete



Projects In Progress

2018-2019

Capital Project Costs

2013-2014

Total	\$ 7,776,886
Bleachers	\$ 497,674
Energy retrofit	\$ 862,981
Fees & Permits	\$ 21,239
Fencing	\$ 340,142
Fire Alarm	\$ 71,908
Misc.	\$ 6,700
Painting	\$ 1,398,438
Paving	\$ 209,355
Playground	\$ 21,757
Pool Construction	\$ 3,876,519
Portable Installation	\$ 14,800
Roofing	\$ 93,496
SBAC Lab	\$ 357,326
Shade Structure	\$ 4,550

2014-2015

Total	\$14,449,184.24
Energy Retrofit	\$ 5,031,598
Dance Floor	\$ 63,092
Fencing	\$ 1,718,003
Fees and Permits	\$ 208,698
Fire Alarm	\$ 126,568
HVAC Replacement	\$ 675,045
Irrigation	\$ 1,209,963
Locker Room	\$ 922,831
MPR Acoustics	\$ 14,980
Painting	\$ 930,315
Paving	\$ 1,405,555
Playground	\$ 116,176
Playground surfacing	\$ 37,306
Portable Installation	\$ 628,943
Roofing	\$ 889,337
Scoreboard	\$ 27,484
Shade Structure	\$ 223,721
Slurry & Stripe	\$ 128,222
Toilet Remodels	\$ 91,347

Capital Project Costs

2015-2016

Total	\$19,165,561
Ceiling Tile Replacement	\$ 676,997
Digital Marquee	\$ 353,967
Energy Retrofit	\$ 4,338,999
Fencing	\$ 539,472
Fire Alarm replacement	\$ 1,368,922
Flooring Replacement	\$ 451,867
Graphics	\$ 54,874
HVAC Replacement	\$ 173,319
Irrigation	\$ 1,211,289
Kitchen Painting and Tables	\$ 1,380,156
Kitchen Remodel	\$ 410,897
Kitchen Replacement	\$ 405,666
Multipurpose Room Upgrades	\$ 447,324

2015-2016

Continued	
Paving	\$ 2,401,768
Portable Installation	\$ 716,084
Restroom Remodels	\$ 61,625
Roofing	\$ 2,310,692
Room Renovations	\$ 160,567
SBAC Lab Phase II	\$ 574,455
School Office Safety Entry	\$ 738,288
Slurry & Stripe	\$ 350,240
Softball Field Install	\$ 38,093

Capital Project Costs

2016-2017

Total	\$26,266,028
Compressed Natural Gas Fueling	\$ 280,252
Fencing	\$ 258,254
Flooring Replacement	\$ 429,248
Graphics	\$ 12,140
HVAC Replacement	\$ 173,319
Kitchen Remodel	\$ 708,477
Multipurpose Room Upgrades	\$ 228,029
Office Entry Remodels	\$ 631,884
Painting	\$ 1,005,431
Playground Surfacing	\$ 828,055
Pool Renovation/Construction	\$ 486,538

2016-2017

Continued	
Portable Installation	\$ 260,217
Restroom Remodels	\$ 294,000
Roofing	\$ 594,663
School Office Safety Entry	\$ 738,288
Science Lab Addition	\$ 2,293,839
Shade Structure	\$ 2,826,039
Track & Field	\$ 13,090,701
21 st Century Classrooms	\$ 655,259
Dance Floor	\$ 43,394
Irrigation Replacement	\$ 428,000

Capital Project Costs

2017-2018

Total	\$12,621,650
ADA Compliance	\$ 8,000
Athletic Facilities	\$ 1,575,137
Benches and Tables	\$ 194,348
CNG Station	\$ 353,283
Energy Retrofit	\$ 615,873
Fencing	\$ 80,795
Fire Alarms	\$ 152,761
Flooring Replacement	\$ 99,161
Kitchen Addition	\$ 96,422
Landscape & Irrigation	\$ 882,271
Monument Signs	\$ 246,132

2017-2018

Continued	
Painting	\$ 365,279
Paving	\$ 452,197
Playground Equipment	\$ 305,749
Portable Addition & Replacement	\$ 3,055,243
Renovations	\$ 262,936
Restroom Addition	\$ 18,044
Retaining Walls	\$ 16,989
Roofing	\$ 2,303,009
School Entry	\$ 132,099
Shade Structure	\$ 1,405,922

Total July 2013 - June 2018

\$80,279,309

School Environment

Business Services: Current Projects

Projects In Progress as of August 23, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Workman HS	Artificial Track and Field Phase I	Complete	N/A	In Progress		5/31/2019	Recommendation to reject all bids and rebid on the July 26 agenda
Workman HS	Artificial Track and Field Phase II	In Progress					TBP preparing Stadium construction documents based on February 8, 2017 Board direction
District Office	C Building Walkways & Parking	Complete	N/A			8/31/2019	
Dibble	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
District Office	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
Facilities	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
Hudson Adult	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
Palm Canyon	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
Stimson LC	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
Willow Adult	Concrete Benches	N/A	N/A	Complete	In Progress	10/30/2018	
Los Altos HS	CTE Engineering Project	In Progress					Resubmitting to OPSC and CDE
La Puente HS	CTE Project	In Progress					Preparing Submittal CDE
Valley	CTE Project	In Progress					Preparing Submittal CDE
Wilson HS	CTE Project	In Progress					Preparing Submittal CDE
Workman HS	CTE Project	In Progress					Preparing Submittal CDE

School Environment

Business Services: Current Projects

Projects In Progress as of August 23, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Baldwin	Exterior Painting	Complete	N/A	Complete	In Progress	9/30/2018	
Nelson	Exterior Painting	Complete	N/A	Complete	In Progress	9/21/2018	
Wilson HS	Exterior Painting	Complete	N/A	Complete	In Progress	10/19/2018	
Dibble	Fire Alarm Replacement	Complete	N/A	In Progress		12/31/2018	Fire Alarm Bid In Progress
District Office	Fire Alarm Replacement	Complete	N/A	In Progress		8/31/2019	Fire Alarm Bid In Progress
Willow - Old	Fire Alarm Replacement	Complete	N/A	Complete	In Progress	11/30/2018	
Willow - New	Fire Alarm Update	Complete	Complete	Complete	In Progress	11/30/2018	
Los Molinos	Floor Replacement - Interior Hallways	N/A	N/A	Complete		12/31/2018	Asbestos Bid In Progress
Kwis	Flooring – Rm 1	Complete	N/A	In Progress		9/30/2018	
Wilson HS	Food Science Room	Complete	Complete	In Progress		1/1/2019	Award of bid on August 23, 2018 Agenda
Baldwin	Irrigation Replacement	Complete	N/A	In Progress			
Cedarlane	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Del Valle	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Grazide	Irrigation Replacement	In Progress	N/A				

School Environment

Business Services: Current Projects

Projects In Progress as of August 23, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Sierra Vista	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Workman HS	Little Theatre Renovation	Complete	N/A	Complete	In Progress	9/30/2018	Complete Except for Flooring
La Puente HS	Lower Field Irrigation	Complete	N/A	Complete	In Progress	12/31/2018	
Baldwin	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Bixby	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
California	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Del Valle	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Grazide	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Kwis	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Los Altos ES	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Los Molinos	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Los Robles	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Nelson	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Palm ES	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Sparks ES	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Sunset	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Temple	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting
Wing Lane	MPR Lighting	N/A	N/A	In Progress		8/30/2019	Part of Phase 4 lighting

School Environment

Business Services: Current Projects

Projects In Progress as of August 23, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Willow	Multipurpose Room Renovation	In Progress				4/1/2019	
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		11/30/2018	
Los Altos HS	Music Room Upgrades	N/A	N/A	Complete	In Progress	11/30/2018	
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		11/30/2018	
La Puente HS	New Kitchen	Complete	Complete			7/15/2019	Bidding to be coordinated with pool
La Puente HS	New Pool and Dressing Area	Complete	Complete	In Progress		7/15/2019	DSA Approved August 14, 2018
California	Office entry doors and gates	Complete	Complete	Complete	In Progress	10/31/2018	
Del Valle	Office entry doors and gates	Complete	In Progress			7/31/2019	
Grandview	Office entry doors and gates	Complete	Complete	Complete	In Progress	9/30/2018	
Orange Grove	Office entry doors and gates	Complete	Complete	Complete	In Progress	12/31/2018	
Temple	Office entry doors and gates	Complete	In Progress			7/31/2019	
Workman ES	Office entry doors and gates	Complete	Complete	Complete	In Progress	11/30/2018	
District Office	Office Remodel	N/A	N/A	Complete	In Progress	11/30/2018	
California	Paving – Demolition of Cottage, add parking	N/A	N/A	Complete	In Progress	12/31/2018	
Grazide	Perimeter Wall Replacement	Complete	Complete	In Progress			
Wedgeworth	Permanent School	In Progress				8/1/2021	
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress			On hold for completion of moves

School Environment

Business Services: Current Projects

Projects In Progress as of August 23, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wilson HS	Photoshop Renovation	Complete	Complete	Complete	In Progress	10/1/2018	Flooring to be replaced after completion of asbestos bid.
Wedgeworth	Portable Classroom Addition	Complete	Complete	Complete	In Progress	8/30/2018	Rooms occupied for start of school
Cedarlane	Portable Headstart Classroom Addition	Complete	Complete	Complete	In Progress	10/30/2018	
Willow	Restroom Repairs and Renovations	In Progress				2/21/2019	
Grandview	Roof Replacement	Complete	Complete	Complete		10/31/2018	
Mesa Robles	Roof Replacement	Complete	Complete	Complete		10/31/2018	
Newton	Roof Replacement	Complete	Complete	Complete	In Progress	8/31/2018	Work started over spring break. Roof is now water tight. Finishes being completed.
Willow Adult	Roof Replacement	Complete	Complete	Complete	In Progress	8/31/2018	B Wing Complete
Workman HS	Roof Replacement	Complete	Complete	Complete	In Progress	9/30/2018	
Bixby	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Del Valle	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Dibble	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
District Office	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Facilities	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Hudson	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Los Robles	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Palm Canyon	School Entry Signs	N/A	N/A	Complete	In Progress	8/30/2018	

School Environment

Business Services: Current Projects

Projects In Progress as of August 23, 2018

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Sierra Vista	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Stimson LC	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Sunset	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Temple	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Valley Alt HS	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	
Willow	School Entry Signs	N/A	N/A	Complete	In Progress	10/30/2018	

Portable Classroom Additions

Los Altos ES




Library Floor Renovation

Sparks ES



Cement Sign Installations

Various Sites

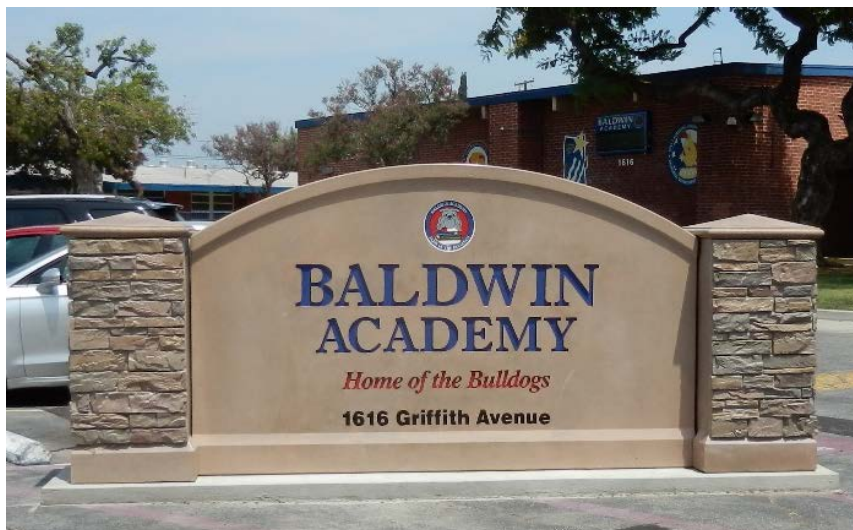



Next Report – September 2018
