

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site
Improvement Projects

Regular Board Meeting
November 16, 2017

Business Services



Completed Projects

2017-2018

School Environment

Business Services: Completed Projects

Projects Completed as of November 16, 2017

Site	Item Description	Construct
Cedarlane	Concrete Benches	Complete
Fairgrove	Concrete Benches	Complete
Grandview	Concrete Benches	Complete
Lassalette	Concrete Benches	Complete
Mesa Robles	Concrete Benches	Complete
Orange Grove	Concrete Benches	Complete
Sierra Vista	Concrete Benches	Complete
Sparks MS	Concrete Benches	Complete
Valinda	Concrete Benches	Complete
Wilson HS	Concrete Benches	Complete
Workman HS	Concrete Benches	Complete
Wilson HS	Dance Floor Installation	Complete
California	Elementary Playground Surfacing	Complete
Grandview	Elementary Playground Surfacing	Complete
Los Molinos	Elementary Playground Surfacing	Complete
Los Robles	Elementary Playground Surfacing	Complete
Palm ES	Elementary Playground Surfacing	Complete
Temple	Elementary Playground Surfacing	Complete
Workman ES	Elementary Playground Surfacing	Complete
Bixby	Exterior Painting	Complete
Fairgrove	Exterior Painting	Complete
Valinda	Exterior Painting	Complete
Facilities	Fire Alarm Replacement	Complete
Bixby	Floor Replacement - Interior Hallways	Complete

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Completed Projects

Projects Completed as of November 16, 2017

Site	Item Description	Construct
Bixby	Floor Replacement - MPR	Complete
Los Molinos	Floor Replacement - MPR	Complete
Sierra Vista	Floor Replacement - MPR	Complete
Wing Lane	Floor Replacement - MPR	Complete
Los Molinos	Portable Classroom Addition	Complete
Wedgeworth	Portable Classroom Addition	Complete
La Puente HS	Roofing replacement - Administration	Complete
Valinda	Roofing replacement - Covered Walks	Complete
Wing Lane	Roofing replacement - Covered Walks	Complete
Wing Lane	Roofing replacement - MPR	Complete
Grazide	School Entry Signs	Complete
Lassalette	School Entry Signs	Complete
Valinda	School Entry Signs	Complete
Cedarlane	Shade Structure	Complete
Los Altos ES	Shade Structure	Complete
Stimson LC	Shade Structure	Complete
Valinda	Shade Structure	Complete
Wedgeworth	Shade Structure	Complete
Workman HS	Shade Structure	Complete
La Puente HS	Synthetic Turf Field Replacement	Complete


Security Gates

Stimson Learning Center



Restroom Renovation

Willow Adult Education

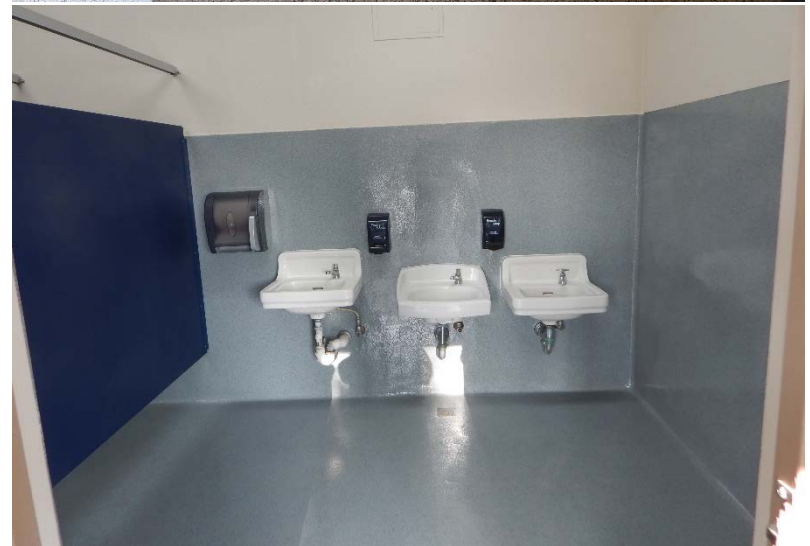



Projects In Progress

2017-2018

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year **In Progress as of November 16, 2017**

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Workman HS	Artificial Track and Field Design	In Progress					Presentation to Board December 7, 2017
District Office	C Building Walkways & Parking	Complete	N/A			7/31/2018	On hold for completion of portables and electrical work
District Office	Compressed Natural Gas (CNG) Fuel Station	Complete	N/A	Complete	In Progress	12/31/2017	LA County Plumbing Permit Pending
Baldwin	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Bixby	Concrete Benches	N/A	N/A	Complete		12/31/2017	
California	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Del Valle	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Dibble	Concrete Benches	N/A	N/A	Complete		12/31/2017	
District Office	Concrete Benches	N/A	N/A	In Progress		12/31/2017	
Grazide	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Kwis	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Los Altos ES	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Los Molinos	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Los Robles	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Nelson	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Palm ES	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Sparks ES	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Stimson LC	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Sunset	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Temple	Concrete Benches	N/A	N/A	Complete		12/31/2017	

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year **In Progress as of November 16, 2017**

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Valley Alt HS	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Wedgeworth	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Wing Lane	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Workman ES	Concrete Benches	N/A	N/A	Complete		12/31/2017	
Los Altos HS	Exterior Painting	N/A	N/A	Complete	In Progress	11/22/2017	Revising graphics
Dibble	Fire Alarm Replacement	Complete	N/A	Complete	In Progress	11/30/2017	
District Office	Fire Alarm Replacement	Complete	N/A	In Progress		5/15/2018	Combined with HVAC Bid
Willow - New	Fire Alarm Replacement	Complete	Complete	In Progress		12/31/2017	Plans revised for updated code requirements
Willow - Old	Fire Alarm Replacement	Complete	N/A	In Progress		12/31/2017	
Los Molinos	Floor Replacement - Interior Hallways	N/A	N/A	Complete	In Progress	1/6/2018	
Palm ES	Floor Replacement - MPR	N/A	N/A	Complete		1/6/2018	
Fairgrove	Head Start Classroom Replacement	Complete	Complete	Complete	In Progress	12/31/2017	
Baldwin	Irrigation Replacement	Complete	N/A	In Progress			
Cedarlane	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Del Valle	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
Grazide	Irrigation Replacement	In Progress	N/A				
Los Molinos	Irrigation Replacement	Complete	N/A	In Progress			

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of November 16, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Nelson	Irrigation Replacement	Complete	N/A	Complete	In Progress	12/31/2017	Purchase order issued September 20, 2017
Sierra Vista	Irrigation Replacement	Complete	N/A	In Progress			Reviewing for coordination with possible bond work.
La Puente HS	Lower Field Irrigation	Complete	N/A	In Progress			Contract re-awarded at August 10, 2017 Meeting
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress		12/31/2017	
Los Altos HS	Music Room Upgrades	N/A	N/A	In Progress		12/31/2017	
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress		12/31/2017	
District Office	NCS & Purchasing Offices	In Progress	N/A	Complete	In Progress	12/31/2017	
La Puente HS	New Kitchen	Complete	In Progress			10/30/2018	DSA Plan Check Corrections received
La Puente HS	New Pool and Dressing Area	Complete	In Progress			10/30/2018	DSA Plan Check Corrections received
California	Office entry doors and gates	Complete	Complete			6/31/18	
Del Valle	Office entry doors and gates	Complete	In Progress			6/31/18	
Grandview	Office entry doors and gates	Complete	Complete			6/31/18	
Orange Grove	Office entry doors and gates	Complete	Complete			6/31/18	
Temple	Office entry doors and gates	Complete	In Progress			6/31/18	
Workman ES	Office entry doors and gates	Complete	Complete			6/31/18	
District Office	Paving – All Parking areas	N/A	N/A	Complete	In Progress	12/31/2017	75% Complete. Holding remaining work for CNG station

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year **In Progress as of November 16, 2017**

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Bixby	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
California	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Cedarlane	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Del Valle	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Dibble	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
District Office	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Fairgrove	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Grandview	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Kwis	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
La Puente HS	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Los Altos ES	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Los Altos HS	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Los Molinos	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Los Robles	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Mesa Robles	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Nelson	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Orange Grove	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Palm ES	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Sierra Vista	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Sparks ES	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Sparks MS	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Stimson LC	School Entry Signs	N/A	N/A	In Progress		12/30/2017	
Sunset	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Temple	School Entry Signs	N/A	N/A	In Progress		12/30/2017	

Changes And Progress Since Last Report - Blue

School Environment

Business Services: Current Projects

Projects Started in 2016-17 Year In Progress as of November 16, 2017

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
California	Paving – Demolition of Cottage, add parking	N/A	N/A	Complete	In Progress	12/31/2017	
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress		5/15/2018	
Los Altos ES	Portable Classroom Addition	Complete	Complete	Complete		12/31/2017	Award of bid October 26, 2017 Meeting
Newton	Portable Classroom Replacement	Complete	Complete	Complete	In Progress	12/31/2017	Award of bid October 26, 2017 Meeting
Baldwin	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Valley Alt HS	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Wedgeworth	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Wilson HS	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Wing Lane	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Workman ES	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Workman HS	School Entry Signs	N/A	N/A	In Progress		11/30/2017	
Workman ES	Shade Structure	Complete	Complete	Complete	In Progress	11/30/2017	Complete except for concrete and fencing
Wilson HS	Shade structure - Concession Stand	Complete	Complete	Complete	In Progress	11/30/2017	

Landscape and Irrigation

Nelson Elementary – In Progress





New Projects

2017-2018

School Environment

Business Services: Current Projects

New 2017-18 Year Projects **In Progress as of November 16, 2017**

Site	Item Description	Architect Plans	DSA Approval	Bidding	Construct	Target Date	Notes
Wedgeworth	Portable Classroom Addition	Complete	In Progress			1/6/2018	Award of bid October 26, 2017 Meeting
Cedarlane	Portable Headstart Classroom Addition	In Progress				7/30/2018	
Willow Adult Ed	EDD Tenant Improvements	Complete	Complete	Complete	In Progress	12/31/2017	
Grandview	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Mesa Robles	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Newton	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Willow Adult Ed	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Workman HS	Roof Replacement	Complete	Complete	In Progress		1/31/2018	
Wilson HS	Culinary Arts Room	In Progress				1/1/2019	
Stimson LC	Security Fencing	N/A	N/A	Complete	Complete	11/9/2017	
Los Altos HS	CTE Engineering Project	In Progress					Approval of grant request on November 16, 2017 agenda

School Environment

Business Services



Next Report – December 2017
