Measures N & O

Citizens' Oversight Committees

5:30 P.M., June 20, 2019

Turlock Unified School DO 102

- 1) Greetings and Call to Order
 - a) Chairperson, Lacy Elliott call the meeting to order
- 2) Roll Call
- 3) Approval of Agenda
 - a) Agenda for the June 20, 2019 meeting
- 4) Review
 - a) Approval of Minutes from the meeting of March 21, 2019
- 5) Staff Report on Projects & Activities
 - a) Prioritization
 - b) Future Planning
- 6) Report of Bond Sale
- 7) Annual Report to the Board
- 8) Annual Work Plan
- 9) Discussion
 - a) Approval of Future Meeting Dates
- 10) Adjourn Meeting

Turlock Unified School District, Measures N and O **Bond Oversight Committee**

Meeting Minutes

21, March, 2019, 5:30 PM, TUSD Pitman High School Library

Meeting #9

Attendees

Committee members in attendance: Lacy Elliott, Bryan Tribble, Patrick Bettencourt, Steve Soderstrom, and Harry Carlson.

Not in attendance: Dave Folly

TUSD Staff: Martell Taylor, Facilities Planner; and Bridget Shelton, Facilities Secretary III

Conducting Meeting: Chairperson, Lacy Elliott

Meeting Commenced 5:35 PM

Approval of Agenda

Current Agenda approved by consensus. No changes were made.

Adoption of Meeting Minutes

No changes were suggested in the Meeting Minutes from January 3, 2019 meeting. The Bond Oversight Committees adopted the minutes by consensus.

Staff Reporting

Meeting began in the Pitman High School Library. The Committee decided to look at the PHS Field Renovations bond project after the close of the meeting.

Martell reported that the PHS Field Renovations are being performed by CT Brayton, and despite rain delays completion is still scheduled for May. He talked about repositioning of the field, new softball and soccer fields, and also the synthetic track and field. Martell also told the Committee the District is considering adding bleachers eventually but will not be using bond funds to do so. Harry Carlson wanted to make sure that the District is only doing what was approved on Schedule A of the bond measure. Martell assured the Committee that the District is only doing the projects that were approved during the election process. Patrick Bettencourt asked if the District had any ownership of the park fields adjacent to Pitman. The answer was no, those fields are owned and governed by the City of Turlock. He also reported about the security work, fencing, and moving of the office at Pitman, along with a new Career Technical Education kitchen. These project are estimated to be \$3 million, and were approved by the Board of Trustees that Tuesday. Although CTE will be receiving a grant for part of the funding of their project. The PHS Fire Alarm system is also being replaced during the summer. This is causing Pitman campus to be closed June and July. The Fire Alarm cost is near \$500 thousand. The Committee wondered where Pitman's summer office staff were going to be located during the campus closure. Martell said he didn't know but would report back next meeting.

Martell then reported about THS. He told the Committee the STEM Building plans are ready for submittal, and explained there is a 6 month "bin" time. Which means that it will generally take 6 months to get plan approval from the Division of State Architects (DSA), and be able to start construction. The L Building roofing and HVAC project went to the Board, and is being partially paid for with Maintenance funding. Security fencing has

been placed on hold at THS until summer of 2020. Patrick Bettencourt asked why we couldn't do it sooner. Martell explained that there are some issues with doing the fencing while the STEM Building is being constructed. There has also been some question as to how to best close the opening between Julien and THS and also Colorado. Bryan Tribble asked if the District is planning to close Berkeley, Martell responded, they are planning to narrow the openings of Berkeley to Canal with "bubble outs". These "bubble outs" create a more narrow street opening, enabling security gates to be added. The City may deed the section of Berkeley Ave that runs through the middle of Turlock High School to the District, but this is undetermined at this point. The Canal Street Parking project will be funded with Redevelopment funds and will provide much needed parking to replace parking spots that are going to be affected by the new construction.

Martell then began reporting on Measure N. He began with the Dutcher Modernization project that had went to bid at the 3/19/19 Board Meeting, and is going for approval on 4/2/19. The projects include parking lot improvements, campus security, and aging portable replacements, totaling an estimated \$5 million. The committee discussed the proposed changes for the parking lot entry and different options presented to the Board which included pulling traffic off Hawkeye and allowing a left or right hand turn. Dutcher projects are set to start as soon as school is out and continue through December.

The Committee wanted to know when TJHS would be getting their fencing. Lacy commented that there was a homeless person in the cafeteria the week before and the parents were not notified until later that day. Martell said that is also a site where major modernization and construction will be taking place and the District is still trying to get a fencing plan that will work during construction. In addition to modernization TJHS will also be getting a new HVAC system, either a hydronic/central plant system or individual units for each classroom.

Martell reported on Brown Phase II and fencing. This includes a new modular office building. Brown projects are \$650,000 and will start in May and complete in October.

Cunningham is getting additional parking, office reconfiguration, and security fencing. These projects will be completed this summer.

Julien's fencing is on hold due to major construction going on. One of the upgrades Julien will be getting is a new modular office.

Wakefield and Osborn's fencing is also on hold due to the amount of projects going on in the District. The Committee stated they would like to see safety and security as a higher priority. Martell assured them that safety and security is a very high priority to the District, and that they are doing everything they can to make sure that all sites receive cameras and fencing as soon as possible.

Bond Sales were briefly discussed. They are set for April/May 2019. The Committee was given the schedule created by Government Financial Strategies, Inc. The second series on Bond sales for Measure N is for 1/3. For Measure O the Bond Sale is for the remaining 2/3 due to fewer projects that have a higher dollar amount.

Martell mentioned a few projects that are not being funded by the bonds, such as CTE, and the TUSD Farm. He told them the Swine Facility is complete.

Expenditure and Expense Reports

The Expenditure Reports were reviewed. No one from the committee had any questions or comments.

Annual Audits for Period Ending June 30, 2018

The Committee was presented with the annual audits. Martell pointed out that the District was in compliance with accepted accounting procedures.

Other Business

The Committee decided to have the June meeting at Dutcher Middle School. Next meeting will be June 20th, at 5:30pm. The Committee will receive a Yearly Work Plan to review and approve, and they will work on a draft of the Annual Report to the Board. Martell asked if anyone from the Committee would like to present the report at the Board meeting in August, no one volunteered.

The meeting was adjourned and Martell and some of the Committee went to look at the PHS Field Renovations.

Meeting	Adi	ou	rn	ed

6:34 pm

Secretary III. Bridget Shelton

Date of approval





MARVIN A. DUTCHER MIDDLE SCHOOL

URLOCK UNIFIED SCHOOL DISTRICT






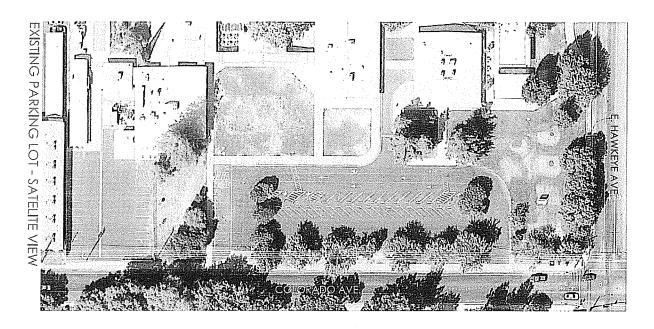

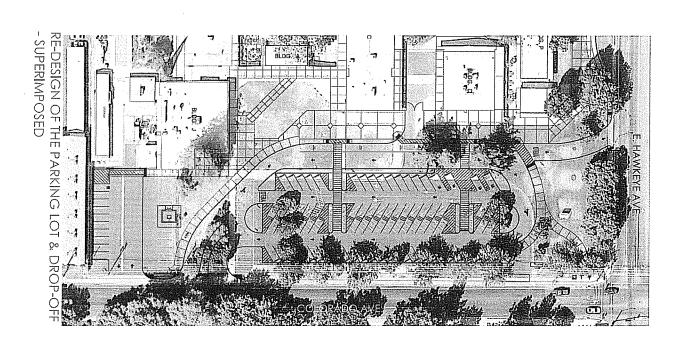




RE-DESIGN OF THE PARKING LOT & DROP-OFF

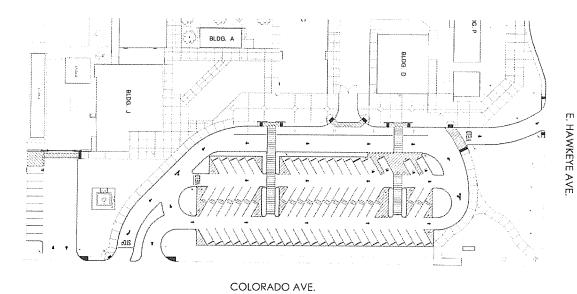


ALTERNATE DESIGN OF THE DROP-OFF AREA

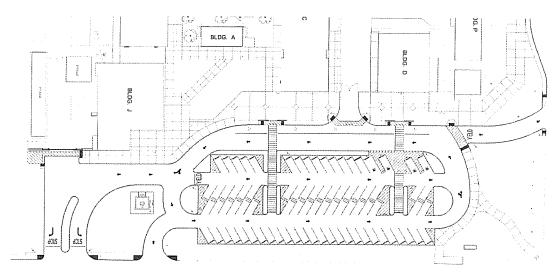

COLORADO AVE.

E. HAWKEYE AVE.



TERESCHOOL DISTRICT


VARVINA. DUTCHER VIDDLE SCHOOL



DMS MODERNIZATION BOND N
MODULAR CLASSROOM INFORMATION



EXISTING ARIAL VIEW

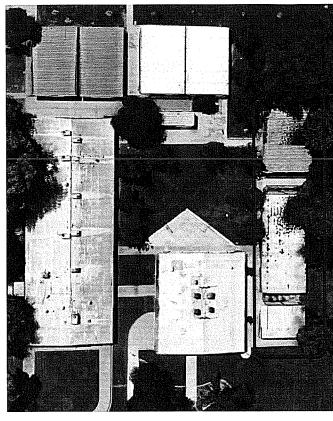

(E) D.F.

BLDG. D ADMIN. BLDG. DSA #40946

BLDG. S DSA #47336

₽

ס

P

ס

BLDG. N DSA # n2-10847 7

PROPOSED ARCHITECTURAL VIEW

BLDG. M DSA # 45536


BLDG. C DSA #14146 & #60578



MARVIN A. DUTCHER MIDDLE SCHOOL TURLOCK UNIFIED SCHOOL DISTRICT






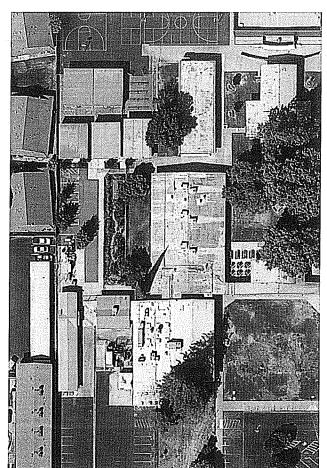

EXISTING AERIAL VIEW




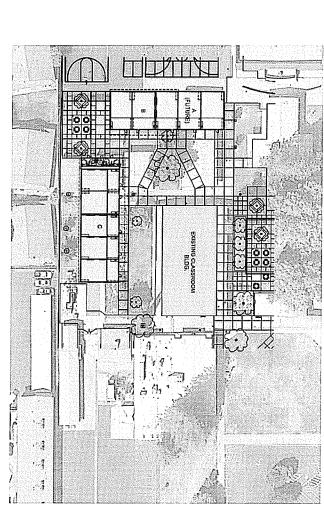





MODULAR CLASSROOMS H & L MARVIN A. DUTCHER MIDDLE SCHOOL TURLOCK UNIFIED SCHOOL DISTRICT

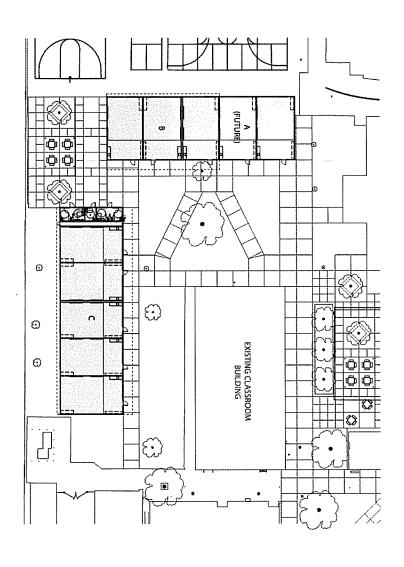


RELOCATABLE CLASSROOMS - SITE PLAN

RELOCATABLE CLASSROOMS & RESTROOMS - FLOOR PLAN 2



MODULAR CLASSROOMS H & L MARVIN A. DUTCHER MIDDLE SCHOOL TURLOCK UNIFIED SCHOOL DISTRICT

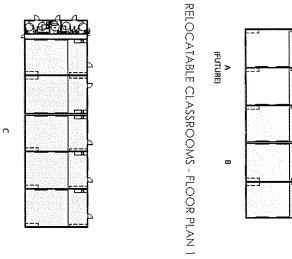



Costs Currently Encumbered:

5% Contingency Soft Cost Acme Construction \$4,513,000.00

Projected Costs:

H & L Modular Replacement

H & L Restroom Facility

P & S Site Work

H & L Site Work

P Modular Replacement

Grand Total

960,000.00

968,665.87 225,650.00


190,000.00

500,000.00 262,000.00

100,000.00

\$7,719,315.00

DMS Project Budget as shown on December 5, 2018 Board Work Shop \$7,500,000.00



- Bond Measure N								
21-0000-0-хххх-0000-хххх-100-Мххх-ю	r					Total		
1st Sale of Bonds:	\$12,500,000		2nd Sale of Bonds	\$13,600,000.00		\$26,100,000.0		1
Proceeds Received	\$12,390,000	.00	Proceeds Received	\$13,497,000.00		\$25,887,000.0		
						\$213,000.0	O Cost of Issuan	ce ·
Org:						The second secon		
NOOD U	nallocated Costs							
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO #	Board
							181308&	
Signs of Success	4,692.95	0.00	0.00	0.00	4,692.95	Measure N signs	195113	N/A
							1836708	
						그 문에 바다가 하시네. 이렇게 하다고	185381&	
							185607&	. A
							1856618	
Government Financial Strategies	7,159.79	0.00	0.00	0.00	7,159.79	CDIAC Annual Debt Report/Consulting	193046&	N/A
							193834&	
함께 있는 회장이 되는 생물들은		100				아이 하다 시작하다 한 때 모모 있다.	194116&	
							194712& 195854&	1 m
							1958546	
							174795&	4
VTD & Co., LLP	4,400.00	0.00	0.00	0,00	4,400.00	Annual Audit Measure N	193866	N/A
VID & CO., LLI	4,400.00		0.00		1,100.00	7777,0077,0072,7770,0072,77	180197&	.,,.,
							183901&	
Lozano Smith	1,475.99	0.00	0,00	0.00	1,475.99	Measure N - General Counsel	185441&	N/A
							191076	
	A - 2 - 2 - 2 - 2 - 2 - 2 - 2 - 2 - 2 -	\$0.00	\$0.00	\$0.00	¢+7 720 72	-	1910/6	
Total:	\$17,728.73	\$0.00	50,00	\$0.00	\$17,728.73			
_								
Org:								
	ncing Projects (one contra			Phase 1 - Complete				
Menghetti Construction	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description		Board
-BR	151,084.00	60,858.90	90,225.10	Final	Final	Brown Elementary	174351	3/7/20
-EA	484,926.63	229,229.30	255,697.33	Final	Final	Earl Elementary	174351	3/7/20
-MD	194,592.12	120,479.95	74,112.17	Final	Final	Medeiros Elementary	174351	3/7/20
-WL	453,635.25	272,332.70	181,302.55	Final	Final	Walnut Elementary	174351	3/7/20
-co	0.00	32,109.05	-32,109.05	Final	Final	_5% Owner Contingency	174351	3/7/20:
	1,284,238.00	715,009.90	569,228.10	Final	Final			
United Inspection								Board
-BR	1,220.00	400.00	820.00	Final	Final	Brown Elementary	174128	N/A
-EA	1,220.00	400.00	820,00	Final	Final	Earl Elementary	174128	N/A
-MD	1,220.00	400.00	820.00	Final	Final	Medeiros Elementary	174128	N/A
-WL	1,220.00	400.00	820.00	Final	Finat	Walnut Elementary	174128	N/A
Kleinfelder			•				PO# B	Board
-BR	0,00	0.00	0.00	Final	Final	Brown Elementary	174934	5/2/20:
-EA	553.30	0.00	553.30	Final	Final	Earl Elementary	174934	5/2/20:
-MD	0.00	0.00	0.00	Final	Final	Medelros Elementary	174934	5/2/20
-WL	553.30	0.00	553,30	Final	Final	Walnut Elementary	174934	5/2/20
AAI Ceramic Tile						·	PO# B	loard
-EA	3,050.00	0.00	3,050.00	Final	Final	Earl lobby - floor tile	180542	N/A
Glass Boss, Inc.	2,050.00	0.02	_,					loard
-EA	14,932.48	0.00	14,932,48	Final	Final	Earl security entry door	180543	N/A
-un	14,002.40	0.00	27,000.70	i inut	1 11101	zari zazarity citaly dodi	*202.43	.,,.,
skw .	2,000,00	0.00	2,000.00	. Final	Final	Fencing Design	182319	N/A
	2,000.00 13,00	13.00	0.00	Final	Final	Printing @ Brown	175356	N/A
-BR								
-EA	14.00	14.00	0.00	Final	Final	Printing @ Earl	175356	N/A
-MD	13.00	13.00	0.00	Final	Final	Printing @ Medeiros	175356	N/A
-EA	5,723.22	5,723.22	0.00	Final	Final	Earl security layout	175388	N/A
signs of Success	2,078.75	0.00	2,078.75	Final	Final	Measure N signs	181308	N/A
							N000 FY17-	
Planning Other Allocation	12,780.79	0.00	12,780.79	Final	Final	Previously Unallocated Costs	18	N/A
Total:	\$1,330,829.84	\$722,373.12	\$608,456.72	\$0	\$0			
encing Project Totals by Site								
BR	\$155,309.4					Brown Elementary		
EA	\$516,680.04	4				Earl Elementary		
MD	\$198,468.2	1				Medeiros Elementary		
	\$460,372.12	,				Walnut Elementary		
-WL	3400,372.17					wallut clementary		

57.00

0.00

0.00

0,00

CEQA Notice of Exempt Filing

183358

N/A

6/12/2019, 10:39 AM

Stanislaus Co. Clerk/Recorder

Total:

57.00

\$868,531.17

1st Sale of Bonds: Proceeds Received	\$12,500,000	.00	2nd Sale of Bonds			rar a	00 000 00	
	\$12,390,000	nn	Proceeds Received	\$13,600,000.00 \$13,497,000.00			00,000.00	
	, 12,330,000		7 TOCEEUS MECEIVEU	\$13,497,000.00	•		87,000.00 13,000.00 Cost of Issue	ence
Org: N007: I	Brown Phase II - Fencing &	Modernization						
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO#	Board
Northstar Engineering	12,610.00	0.00	12,610.00	0.00	0.00	Topographic Survey	18224	
Northstar Engineering	660.00	0.00	0.00	0.00	660,00	Topo Survey - Utilities	19124	
Northstar Engineering	11,750.00	0.00	0.00	4,420.00	7,330.00	Civil Engineering	19208	9/4/20
Division of State Arch	9,225.00	0.00	0.00	0.00	9,225.00	DSA Fee	193760) N/A
							1852118	
Kleinfelder	37,476.45	0.00	0.00	27,770.00	9,706.45	Address Total	1914738	5/21/20
Members	37,470.43	0.00	0.00	27,770,00	3,706.43	Materials Testing	195886 1850158	•
United Inspection	11,280.00	0.00	0.00	9,840.00	1,440.00	Inspection Services	19530	
DC Inspections Inc.	3,000.00	0.00	0.00	3,000.00	0.00	Modular In-Plant Inspection	195464	
Leach Group Inc.	1,350.00	0.00	0.00	1,350.00	0.00	Modular In-Plant Inspection	195089	8/7/20:
All Commercial Fence	185,693.65	0.00	45,687.00	0.00	140,006.65	Construction Main	185552	
Planning Other Allocation	1,736.11	0.00	1,736.11	0.00	0.00	Previously Unallocated Costs	N000 FY17	N/A
McClatchy Newspaper Inc.	719.04	0.00	0,00	0.00	719.04	Advertisement-Notice to Bidde	18	5
JTS Modular	15,000.00	0.00	0.00	0.00	15,000.00	Building Design	rs 194789 192786	
JTS Modular	347,250.00	0.00	0.00	296,662.50	50,587.50	Modular Office Bullding	194900	
Taylor Backhoe Services Inc.	412,908.49	0.00	0.00	412,908.49	0.00	Sitework for JTS Modular Bidg	195675	
						~	182739&	
							185397&	
							185557&	
SKW & Associates-B% Fee	85,335.95	0.00	22,367.73	23,509.48	39,458.74	Architectural & Engineering	194036&	11/7/201
							194201&	
							195192& 195737	
Total;	\$1,135,994.69	\$0.00	\$82,400.84	\$779,460.47	\$274,133.38		155757	
Org:								
	owell Elementary Fencing	& Modernization						
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO #	Board
Northstar Engineering	14,320.00	0.00	14,320.00	0.00	0.00	Topographic Survey	182351	
Kleinfelder	12,000.00	0.00	0.00	11,770.00	230.00	Testing	185211	5/1/201
United Inspection	4,320.00	0.00	0.00	0.00	4,320.00	Inspection Services	185015	N/A
All Commercial Fence Glass Boss, Inc.	253,080.00 13,143.24	0.00 0.00	113,956.00 0.00	0.00	139,124.00	Construction Main	185552	6/5/201
G1833 2033, ITC.					13,143.24	Front Office Store Front	185556 NOOO FY17-	N/A
	3,298.48	0,00	3,298.48	0.00	0,00	Previously Unallocated Costs	18	N/A
Planning Other Allocation							*******	
Planning Other Allocation SKW & Associates-8% Fee	29,129.59	0.00	24,906.41	0.00	4,223.18	Architectural & Engineering	182739& 185397&	11/7/201
SXW & Associates-8% Fee Total: Org:	\$329,291.31	\$0.00	\$156,480.89	0.00 \$11,770.00	4,223.18 \$161,040.42	Architectural & Engineering		11/7/201
SXW & Associates-8% Fee Total: Org: N009 Me Vendor	\$329,291.31 edeiros Security Camera Sy Cost	\$0.00 stem Paid 16-17	\$156,480.89 Phase 1 - Complete Paid 17-18	\$11,770.00 Encumbered 18-19	\$161,040.42 Paid 18-19	Description	185397& 185557	Board
SXW & Associates-8% Fee Total: Org: N009 Me Vendor Planning Other Allocation	\$329,291.31 edeiros Security Camera Sy Cost 109.15	\$0.00 stem Paid 16-17 0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15	\$11,770.00 Encumbered 18-19 0.00	\$161,040.42 Paid 18-19 0.00	Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18	Board N/A
SXW & Associates-8% Fee Total: Org: N009 Me Vendor	\$329,291.31 edeiros Security Camera Sy Cost	\$0.00 stem Paid 16-17	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00	\$11,770.00 Encumbered 18-19	\$161,040.42 Paid 18-19 0.00 15,161.14	Description	185397& 185557 PO # N000	Board N/A
SXW & Associates-8% Fee Total: Org: N009 Me Vendor Planning Other Allocation Johnson Controls Security Solutions Total:	\$329,291.31 edeiros Security Camera Sy: Cost 109.15 20,079.14	\$0.00 stem Paid 16-17 0.00 0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15	\$11,770.00 Encumbered 18-19 0.00 0.00	\$161,040.42 Paid 18-19 0.00	Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18	Board N/A
SXW & Associates-6% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org:	\$329,291.31 edeiros Security Camera Sy: Cost 109.15 20,079.14 \$20,188.29	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00	\$161,040.42 Paid 18-19 0.00 15,161.14	Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18	Board N/A
SKW & Associates-6% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Poid 17-18 109.15 4,918.00 \$5,027.15	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00	\$161,040.42 Paid 18-19 0.00 15,161.14 \$15,161.14	Description Previously Unallocated Costs Security Camera System	185397& 185557 PO# NO00 FY17-18 184597	Board N/A 3/20/2018
SKW & Associates-6% Fee Total: Org: N009 Nee Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 Source System Paid 16-17	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19	\$161,040.42 Paid 18-19 0.00 15,161.14	Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18 184597	Board N/A
SKW & Associates-6% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Poid 17-18 109.15 4,918.00 \$5,027.15	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00	\$161,040.42 Paid 18-19 0.00 15,161.14 \$15,161.14	Description Previously Unallocated Costs Security Camera System	185397& 185557 PO # N000 FY17-18 184597 PO # N000 FY17-	Board N/A 3/20/2018
SKW & Associates-6% Fee Total: Org: N009 Nee Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19	Paid 13-19 0.00 15,161.14 \$15,161.14	Description Previously Unallocated Costs Security Camera System Description	185397& 185557 PO # N000 FY17-18 184597	Board N/A 3/20/2018 Board N/A
SKW & Associates-5% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00	Paid 13-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO# N000 FY17-18 184597 PO# N000 FY17- 18	Board N/A 3/20/2018 Board N/A
SKW & Associates-6% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total:	\$329,291.31 edeiros Security Camera Syr. Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96	\$0.00 stem Paid 16-17 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO# N000 FY17-18 184597 PO# N000 FY17- 18	Board N/A 3/20/2018 Board N/A
SKW & Associates-8% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Earl	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO# N000 FY17-18 184597 PO# N000 FY17- 18	Board N/A 3/20/2018 Board N/A
SXW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr. Cost 109.15 20,079.14 \$70,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96	\$0.00 stem Paid 16-17 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18 184597 PO # N000 FY17-18 185170	Board N/A 3/20/2018 Board N/A
SKW & Associates-8% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Earl	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 528,982.96	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System	185397& 185557 PO # N000 FY17-18 184597 PO # N000 FY17- 18 185170 PO # I N000 FY17-	Board N/A 3/20/2018 Board N/A 4/24/2018
SKW & Associates-8% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Vendor Planning Other Allocation	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 mningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18 184597 PO # 185170 PO # 1 N000 FY17-18 N000 FY17-18	Board N/A 3/20/2018 Board N/A 4/24/2018
SKW & Associates-6% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Corg: N011 Earl Vendor	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 mningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description	185397& 185557 PO # N000 FY17-18 184597 PO # N000 FY17- 18 185170 PO # I N000 FY17-	Board N/A 3/20/2018 Board N/A 4/24/2018
SKW & Associates-8% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Learning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Planning Other Allocation All Commercial Fence Total:	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 24,575.00	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00 \$0.00 0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18 184597 PO # 185170 PO # 1 N000 FY17-18 N000 FY17-18	Board N/A 3/20/2018 Board N/A 4/24/2018
SXW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 24,575.00	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18 184597 PO # 185170 PO # 1 N000 FY17-18 N000 FY17-18	Board N/A 3/20/2018 Board N/A 4/24/2018
SXW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr. Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 Il Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs	185397& 185557 PO # N000 FY17-18 184597 PO # N000 FY17- 18 185170 PO # I N000 FY17- 18 185552	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018
SXW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 nningham Elementary Fencil 683.09	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 Paid 16-17 0.00 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 \$0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main	185397& 185557 PO # N000 FY17-18 184597 PO # N000 FY17- 18 185170 PO # I N000 FY17- 18 185552	Board N/A 3/20/2018 Board N/A 4/24/2018 30ard N/A 6/5/2018
SKW & Associates-B% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0,00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 ningham Elementary Fencic Cost 683.09 10,000.00	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 Paid 16-17 0.00 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 50.00 Encumbered 18-19 0.00 0.00 50.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 683.09 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing	185397& 185557 PO # N000 FY17-18 184597 PO # 18 185170 PO # 1 N000 FY17- 18 185552 PO # 194788 195570	Board N/A 3/20/2018 Board N/A 4/24/2018 N/A 6/5/2018
SKW & Associates-8% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Security Solutions Total: Org: N011 Commercial Fence Total: Org: N010 Cur Vendor Planning Other Allocation All Commercial Fence Total: Org: N012 Vendor MCClatchy Newspaper Inc. Kelinfelder Taylor Backhoe Services Inc.	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 mingham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00	Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Flase II - Complete Encumbered 18-19 0.00 0.00 Encumbered 18-19 0.00 0.00 \$0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 528,982.95 Paid 18-19 0.00 61,525.00 \$61,525.00 Paid 18-19 683.09 0.00 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing	185397& 185557 PO # N000 FY17-18 184597 PO # 185170 PO # 1 1 185552 PO # 194788 195570 PO # 194788	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018
SKW & Associates-B% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0,00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 ningham Elementary Fencic Cost 683.09 10,000.00	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 Paid 16-17 0.00 0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 50.00 Encumbered 18-19 0.00 0.00 50.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 683.09 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing	PO# NO00 FY17-18 184597 PO# N000 FY17-18 184597 PO# 18 185170 PO# 18 185552 PO# 195688	Board N/A 3/20/2018 Board N/A 4/24/2018 N/A 6/5/2018
SKW & Associates-6% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Security Solutions Total: Org: N011 Commercial Fence Total: Org: N010 Cur Vendor Planning Other Allocation All Commercial Fence Total: Org: N012 Cun Vendor MCClatchy Newspaper Inc. Kelinfelder Taylor Backhoe Services Inc.	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 mingham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00	Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Flase II - Complete Encumbered 18-19 0.00 0.00 Encumbered 18-19 0.00 0.00 \$0.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 528,982.95 Paid 18-19 0.00 61,525.00 \$61,525.00 Paid 18-19 683.09 0.00 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing	185397& 185557 PO # N000 FY17-18 184597 PO # 185170 PO # 1 1 185552 PO # 194788 195570 PO # 194788	Board N/A 3/20/2018 Board N/A 4/24/2018 30ard N/A 6/5/2018
SKW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr. Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fence Cost 279.26 74,575.00 \$74,854.26 nningham Elementary Fence Cost 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 10,000.00 480,165.00 2,496.00 \$8,918.00	Paid 18-19 0.00 15,161.14 \$15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 Paid 18-19 0.00 61,525.00 \$61,525.00 Paid 18-19 683.09 0.00 0.00 0.00 \$40,063.59	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services	PO # NO00 FY17-18 184597 PO # NO00 FY17-18 184597 PO # 185570 PO # 18 185552 PO # 194788 195674 195688 191520&	Board N/A 3/20/2018 Board N/A 4/24/2018 N/A 6/5/2018 Board N/A 6/5/2018
SKW & Associates-B% Fee Total: Org: N009 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Cur Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Earl Vendor Planning Other Allocation All Commercial Fence Total: Org: N012 Cun WCCIatchy Newspaper Inc. Gleinfelder Taylor Backhoe Services Inc. Johlted Inspections	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 24,575.00 \$74,854.26 ningham Elementary Fencic Cost 683.09 10,000.00 480,165.00 2,496.00	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00 \$0.00 Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 2.00 2.496.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 63.09 0.00 0.00 0.00	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services	PO # NO00 FY17-18 184597 PO # NO00 FY17-18 185570 PO # 19778 185552 PO # 19678 195564 195668 191520& 195310&	Board N/A 3/20/2018 Board N/A 4/24/2018 N/A 6/5/2018 Board N/A 6/5/2018
SKW & Associates-B% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr. Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 Il Elementary Phase II - Fence Cost 279.26 74,575.00 \$74,854.26 nningham Elementary Fence Cost 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 10,000.00 480,165.00 2,496.00 \$8,918.00	Paid 18-19 0.00 15,161.14 \$15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 Paid 18-19 0.00 61,525.00 \$61,525.00 Paid 18-19 683.09 0.00 0.00 0.00 \$40,063.59	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services	PO # NO00 FY17-18 184597 PO # NO00 FY17-18 185570 PO # 19778 185552 PO # 19678 195564 195668 191520& 195310&	Board N/A 3/20/2018 Board N/A 4/24/2018 N/A 6/5/2018 Board N/A 6/5/2018
SKW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 ningham Elementary Fencic 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$542,325.68	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 \$0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 \$50.00 Encumbered 18-19 0.00 \$50.00 \$50.00	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 63.09 0.00 0.00 0.00 \$40,063.59	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services Architectural & Engineering	PO # NO00 FY17-18 184597 PO # NO00 FY17-18 185170 PO # 185170 PO # 194788 185552 PO # 194788 195688 191520& 195310& 195786&	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 Board N/A 6/5/2018 Board 8/7/2018 Board 8/7/2018 Board 8/7/2018
SKW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 mningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 \$28,982.96 I Elementary Phase II - Fence Cost 279.26 74,575.00 \$74,854.26 mingham Elementary Fencin Cost 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$542,325.68	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 \$0.00 \$0.00 \$0.00 Paid 17-18	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 From the complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 10,000.00 480,165.00 2,496.00 \$8,918.00 Encumbered 18-19	Paid 18-19 0.00 15,161.14 \$15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 \$61,525.00 Paid 18-19 683.09 0.00 0.00 0.00 \$40,063.59 \$40,746.68	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services	PO # NO00 FY17-18 184597 PO # NO00 FY17-18 184597 PO # 185570 PO # 18 185552 PO # 194788 195570 195674 195688 191520& 195786&	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 Board N/A 6/5/2018
SKW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syc Cost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 ningham Elementary Fencic 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$542,325.68	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 \$0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 Phase II - Complete Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 10,000.00 480,165,00 2,496,00 \$8,918,00 \$501,579,00	Paid 18-19 0.00 15,161.14 \$15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 683.09 0.00 0.00 0.00 \$40,063.59 \$40,746.68	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services Architectural & Engineering	185397& 185557 PO # N000 FY17-18 184597 PO # 18 185170 PO # 18 185170 PO # 194788 195570 195674 195688 191520& 195786& PO # B	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 B/7/2018 N/A 4/16/2019 N/A 8/7/2018
SKW & Associates-B% Fee Total: Org: N009	\$329,291.31 edelros Security Camera Sycost 109.15 20,079.14 \$20,188.29 nningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 I Elementary Phase II - Fence Cost 279.26 74,575.00 \$74,854.26 nningham Elementary Fencia Cost 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$542,325.68	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 0.00 0.00 0.00 0.00 0.00 \$0.00 \$0.00 Paid 17-18 0.00 0.00 0.00 0.00 0.00 0.00 \$0.00 Paid 17-18 0	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 0.00 \$0.00 From the complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 10,000.00 480,165.00 2,496.00 \$8,918.00 Encumbered 18-19	Paid 18-19 0.00 15,161.14 \$15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 \$61,525.00 Paid 18-19 683.09 0.00 0.00 0.00 \$40,063.59 \$40,746.68	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services Architectural & Engineering	PO # NO00 FY17-18 184597 PO # NO00 FY17-18 185170 PO # 185170 PO # 194788 185552 PO # 194788 195688 191520& 195310& 195786&	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 Board N/A 6/5/2018 Board 8/7/2018 Board 8/7/2018 Board 8/7/2018
Total: Org: N009 Me Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N010 Vendor Planning Other Allocation Johnson Controls Security Solutions Total: Org: N011 Johnson Controls Security Solutions Total: Org: N011 Farl Vendor Planning Other Allocation All Commercial Fence Total: Org: N012 Vendor Total: Org: N012 Cum Vendor Inclied inspections KW & Associates-8 % Fee Total: Org: N013 Julie Vendor Org: N014 Vendor Total: Org: N015 Org: N016 Vendor Total: Org: N017 Vendor Total: Org: N018 Vendor Total: Org: N019 Vendor Total: Org: N018 Vendor Total: Org: N019 Vendor Total: Org: N010 Vendor Total: Org: N010	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 mningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 \$28,982.96 Il Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 mingham Elementary Fencil 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$5542,325.68 m Elementary Fencing Cost 0 \$49,986.63	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 \$0.00 \$0.00 Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 \$0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 \$50.00 Encumbered 18-19 0.00 \$50.1579.00 Encumbered 18-19 0 \$35,536,53	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 63.09 0.00 0.00 0.00 0.00 \$40,063.59 \$40,746.68	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services Architectural & Engineering	185397& 185557 PO # N000 FY17-18 184597 PO # 18 185170 PO # 18 185170 PO # 194788 195570 195674 195688 191520& 195786& PO # B	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 B/7/2018 N/A 4/16/2019 N/A 8/7/2018
SKW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Syr Cost 109.15 20,079.14 \$20,188.29 mningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 \$28,982.96 Il Elementary Phase II - Fenc Cost 279.26 74,575.00 \$74,854.26 mingham Elementary Fencil 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$5542,325.68 m Elementary Fencing Cost 0 \$49,986.63	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 50.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 \$0.00 \$0.00 Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 \$0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 \$50.00 Encumbered 18-19 0.00 \$50.1579.00 Encumbered 18-19 0 \$35,536,53	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 63.09 0.00 0.00 0.00 0.00 \$40,063.59 \$40,746.68	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services Architectural & Engineering Description Advertisement-Notice to Bidders Architectural & Engineering	185397& 185557 PO # N000 FY17-18 184597 PO # 18 185170 PO # 18 185170 PO # 194788 195570 195674 195688 191520& 195786& PO # B	Board N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 B/7/2018 N/A 4/16/2019 N/A 8/7/2018
SKW & Associates-8% Fee Total: Org: N009	\$329,291.31 edeiros Security Camera Sycost 109.15 20,079.14 \$20,188.29 mningham Security Camera Cost 0.00 \$28,982.96 \$28,982.96 1 Elementary Phase II - Fencicat 279.26 74,575.00 \$74,854.26 mingham Elementary Fencicat 683.09 10,000.00 480,165.00 2,496.00 \$48,981.59 \$542,325.68 m Elementary Fencing Cost 0 \$49,296.63 \$49,296.63	\$0.00 stem Paid 16-17 0.00 0.00 \$0.00 \$0.00 System Paid 16-17 0.00 50.00 \$0.00	\$156,480.89 Phase 1 - Complete Paid 17-18 109.15 4,918.00 \$5,027.15 Paid 17-18 0.00 \$0.00 \$0.00 Paid 17-18 279.26 13,050.00 \$13,329.26 Paid 17-18 0.00 0.00 0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$11,770.00 Encumbered 18-19 0.00 0.00 \$0.00 \$0.00 Phase 1 - Complete Encumbered 18-19 0.00 \$0.00 \$0.00 \$0.00 Complete Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 \$0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 \$0.00 \$0.00 Encumbered 18-19 0.00 \$50.00 Encumbered 18-19 0.00 \$50.1579.00 Encumbered 18-19 0 \$35,536,53	Paid 18-19 0.00 15,161.14 \$15,161.14 Paid 18-19 0.00 28,982.96 \$28,982.96 Paid 18-19 0.00 61,525.00 Paid 18-19 63.09 0.00 0.00 0.00 0.00 \$40,063.59 \$40,746.68	Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Security Camera System Description Previously Unallocated Costs Construction Main Description Advertisement-Notice to Bidders Testing Security Fencing Inspection Services Architectural & Engineering Description Advertisement-Notice to Bidders Architectural & Engineering	185397& 185557 PO# N000 FY17-18 184597 PO# N000 FY17- 18 185170 PO# 194788 195570 195674 195688 191520& 195786& PO# B 191520	N/A 3/20/2018 Board N/A 4/24/2018 Board N/A 6/5/2018 Board 8/7/2018 N/A 4/16/2019 N/A 8/7/2018

Bond Measure N 21-0000-0-xxxx-0000-xxxx-100-Nxxx-xx 1st Sale of Bonds: Proceeds Received	\$12,500,000.00 \$12,390,000.00		d Sale of Bonds oceeds Received	\$13,600,000.00 \$13,497,000.00		Total \$26,100,000 \$25,887,000 \$213,000	
Org:	field Security Comera Syste						
	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO# Board
Vendor Johnson Controls Security Solutions	\$39,363.00	\$0.00	\$0.00	\$0.00	\$39,363,00	Security Camera System	192060 9/4/2018
Total:	\$39,363.00	\$0.00	50.00	\$0.00	\$39,363.00		
Org:		30.00		Phase 1 - Completion 6/30/2019			
**************************************	it Security Camera System		Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO# Board
Vendor	Cost	Paid 16-17	\$0.00	\$14,365.43	\$41,670.17	Security Camera System	193686 12/12/2018
AMS,NET	\$56,035,60	\$0.00	\$0.00	\$14,365.43	\$41,670.17	Security Camera System	193686 12/12/2018
Total:	\$56,035.60	\$0.00	\$0.00	\$14,363.43	541,670.17		
Org: NO17 Earl St	ecurity Camera System						
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO# Board
AMS.NET	\$52,667.91	\$0.00	\$0.00	\$52,667.91	\$0.00	Security Camera System	194363 2/5/2019
Total:	\$52,667.91	\$0.00	\$0.00	\$52,667.91	\$0.00		
Org: NO18 Crowd Vendor AMS.NET Total:	ell Security Camera System Cost \$44,707.84 \$44,707.84	Paid 16-17 \$0.00 \$0.00	Paid 17-18 \$0.00 \$0.00	Encumbered 18-19 \$44,707.84 \$44,707.84	Paid 18-19 \$0.00 \$0.00	Description Security Camera System	PO# Board 194365 2/5/2019
Org: NO19 TJHS S	Security Camera System			Start June 2019			P
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO# Board
AM5.NET	\$100,946.44	\$0.00	\$0.00	\$100,946.44	\$0.00	Security Camera System	194365 2/5/2019
Total:	\$100,946.44	\$0.00	\$0.00	\$100,946.44	\$0.00		

\$12,829,463.57 \$727,108.12 \$1,317,528.43 \$6,494,994.89 \$2,283,851.64 \$13,057,536.43

Total Balance N Includes \$672,500 of unencumbered estimated Architectural fees (percent fee) from N004 -Osborn.

Total Balance N includes \$780,506.32 of unencumbered estimated Architectural fees (percent fee) from N005-TJHS.

Total Balance N includes \$552,974.17 of unencumbered estimated Architectural fees (percent fee) from N006-Wakefield Phase 2. Total Balance N: Balance Remaining N:

TURLOCK UNIFIED SCHOOL DISTRICT GENERAL OBLIGATION BOND - MEASURE N Bond Issue to Date Expenditure by Funding Summary Report As of June 10, 2019

Columbia Columbia			Building	Capital Eacilities	Capital Eacilities	Special Reserve	General	Total	
Unallocated Costs* 17,728.73 0.00 0.00 0.00 0.00 17,728.73 Wakefield Kinder Relocation** [Complete] 0.00 1,888,549.90 0.00 0.00 0.00 1.00 1,888,549.90 Wakefield Phase II - Modernization 17,557.00 0.00 0.00 0.00 0.00 0.00 17,557.00 Wakefield Security Camera System 39,363.00 0.00 0.00 0.00 0.00 0.00 39,363.00 Brown Phase I - Fencing [Complete] 155,309.47 0.00 0.00 0.00 0.00 0.00 0.00 155,309.47 Earl Phase I - Fencing [Complete] 156,880.04 0.00 0.00 0.00 0.00 0.00 0.00 18,4688.11 Walnut Elementary Fencing [Complete] 18,468.11 0.00 0.00 0.00 0.00 0.00 18,4682.11 Walnut Elementary Fencing [Complete] 40,372.12 0.00 0.00 0.00 0.00 0.00 18,308.29.84 Brown Phase II - Fencing & Mod. 356,534.22 0.00 0.00 0.00 0.00 0.00 356,534.22 Crowell Elementary Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 0.00 377,521.31 Crowell Security Camera System 0.00 0.00 0.00 0.00 0.00 0.00 377,521.31 Crowell Security Camera System 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	į	경로함이 나도 사람이라 하는데요? 나도	-					TOLAI	
Wakefield Phase II - Modernization 17,557.00 0.00 0.00 0.00 17,557.00 Wakefield Security Camera System 39,363.00 0.00 0.00 0.00 39,363.00 Brown Phase I - Fencing [Complete] 153,680.04 0.00 0.00 0.00 0.00 515,680.04 Medicino Stementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 198,468.21 Walnut Elementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 0.00 198,468.21 Walnut Elementary Fencing [Complete] 198,468.21 0.00 317,521.31 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.		Unallocated Costs*						17,728.73	
Wakefield Security Camera System 39,363.00 0.00 0.00 0.00 0.00 39,363.00 Brown Phase I - Fencing [Complete] 155,309.47 0.00 0.00 0.00 0.00 0.00 155,309.47 Earl Phase I - Fencing [Complete] 1516,680.04 0.00 0.00 0.00 0.00 0.00 0.00 156,680.04 Medieros Elementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 0.00 0.00 198,468.21 Walnut Elementary Ed. Ctr. Fencing [Complete] 460,372.12 0.00		Wakefield Kinder Relocation** [Complete]	0.00	1,888,549.90	0.00	0.00	0.00	1,888,549.90	
Brown Phase I - Fencing [Complete] 155,309.47 0.00 0.00 0.00 0.00 155,309.47 Earl Phase I - Fencing [Complete] 516,680.04 0.00 0.00 0.00 0.00 0.00 0.00 516,680.04 Medeiros Elementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 0.00 198,468.21 Earl Phase I - Fencing [Complete] 46,972.12 0.00 0.00 0.00 0.00 0.00 46,9372.12 Fencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 0.00 1,330,829.84 0.00 0.00 0.00 0.00 0.00 1,330,829.84 0.00 0.00 0.00 0.00 0.00 0.00 1,330,829.84 0.00 0.00 0.00 0.00 0.00 0.00 1,330,829.84 0.00 0.00 0.00 0.00 0.00 0.00 1,330,829.84 0.00 0.00 0.00 0.00 0.00 0.00 0.00 317,521.31 0.00 0.0		Wakefield Phase II - Modernization	17,557.00	0.00	0.00	0.00	0.00	17,557.00	
Earl Phase I - Fencing (Complete) 516,680.04 0.00 0.00 0.00 0.00 0.00 198,680.04 Medeiros Elementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 0.00 198,668.21 Pencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 0.00 198,668.21 Pencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 0.00 1,330,829.84 Pencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 0.00 1,330,829.84 Pencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 0.00 1,330,829.84 Pencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 0.00 1,330,829.84 Pencing Rown Phase II - Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 0.00 0.00 317,521.31 Pencing Elementary Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 0.00 0.00 0.00		Wakefield Security Camera System	39,363.00	0.00	0.00	0.00	0.00	39,363.00	
Earl Phase I - Fencing [Complete] 516,680.04 0.00 0.00 0.00 0.00 198,468.21 Welderos Elementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 0.00 198,468.21 Walnut Elementary Fencing [Complete] 460,372.12 0.00 0.00 0.00 0.00 400,372.12 Fencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 1,330,829.84 Brown Phase II - Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 317,521.31 Crowell Elementary Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 0.00 317,521.31 Crowell Security Camera System 0.00		Brown Phase I - Fencing [Complete]	155,309.47	0.00	0.00	0.00	0.00	155,309.47	
Mediarios Elementary Fencing [Complete] 198,468.21 0.00 0.00 0.00 0.00 0.00 460,372.12 Walnut Elementary Fencing [Complete] 460,372.12 0.00 0.00 0.00 0.00 0.00 460,372.12 Fencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 1,332,829.84 Brown Phase II - Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 0.00 317,521.31 Crowell Elementary Fencing & Mod. 317,521.31 0.00			516,680.04	0.00	0.00	0.00	0.00	516,680.04	
Walnut Elementary Ed. Ctr. Fencing [Complete] Fencing Projects 460,372.12 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 356,534.22 0.00 0.00 0.00 0.00 0.00 356,534.22 0.00		- · · · · · · · · · · · · · · · · · · ·	198,468.21	0.00	0.00	0.00	0.00	198,468.21	
Fencing Projects 1,330,829.84 0.00 0.00 0.00 0.00 1,330,829.84 Brown Phase II - Fencing & Mod. 356,534.22 0.00 0.00 0.00 0.00 317,521.31 Crowell Elementary Fencing & Mod. 317,521.31 0.00			460,372.12	0.00	0.00	0.00	0.00	460,372.12	
Crowell Elementary Fencing & Mod. 317,521.31 0.00 0.00 0.00 0.00 317,521.31 Crowell Security Camera System 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 74,854.26 0.00 0.00 0.00 0.00 0.00 74,854.26 0.00			1,330,829.84	0.00	0.00	0.00	0.00	1,330,829.84	
Crowell Security Camera System 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 74,854.26 0.00 0.00 0.00 0.00 0.00 74,854.26 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 20,188.29 Cunningham Elementary Fencing 40,746.68 0.00 0.00 0.00 0.00 0.00 0.00 40,746.68 Cunningham Security Camera System[Complete] 28,982.96 0.00 0.00 0.00 0.00 0.00 0.00 28,982.96 Julien Elementary Fencing 13,660.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 13,660.00 0.00 0.00 0.00 0.00 0.00 </td <td></td> <td>Brown Phase II - Fencing & Mod.</td> <td>356,534.22</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>356,534.22</td> <td></td>		Brown Phase II - Fencing & Mod.	356,534.22	0.00	0.00	0.00	0.00	356,534.22	
Earl Elementary Phase II - Fencing [Complete] 74,854.26 0.00 0.00 0.00 0.00 74,854.26 Earl Security Camera System 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 20,188.29 0.00 0.00 0.00 0.00 20,188.29 0.00 0.00 0.00 0.00 40,746.68 0.00 0.00 0.00 0.00 0.00 40,746.68 0.00 714.00 0.00 0.00 0.00 0.00 714.00 0.00 0.00 0.00 0.00 715,573.42 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 <td></td> <td>Crowell Elementary Fencing & Mod.</td> <td>317,521.31</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>317,521.31</td> <td></td>		Crowell Elementary Fencing & Mod.	317,521.31	0.00	0.00	0.00	0.00	317,521.31	
Earl Security Camera System 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 20,188.29 Cunningham Elementary Fencing 40,746.68 0.00 0.00 0.00 0.00 40,746.68 Cunningham Security Camera System[Complete] 28,982.96 0.00 0.00 0.00 0.00 0.00 0.00 28,982.96 Julien Elementary Fencing 13,660.00 0.00 0.00 0.00 0.00 0.00 0.00 13,660.00 0.00 0.00 0.00 0.00 13,660.00 0.00 0.00 0.00 0.00 714.00 0.00 0.00 0.00 0.00 714.00 0.00 0.00 0.00 0.00 1,961,720.17 0.00 0.00 0.00 0.00 1,961,720.17 0.00 666,655.86 0.00 0.00 715,573.42 0.00 0.00 0.00 0.00 0.00 17,500.00 0.00 0.00 0.00 0.00 0.00 <td< td=""><td></td><td>Crowell Security Camera System</td><td>0.00</td><td>0.00</td><td>0.00</td><td>0.00</td><td>0.00</td><td>0.00</td><td></td></td<>		Crowell Security Camera System	0.00	0.00	0.00	0.00	0.00	0.00	
Medeiros Security Camera System [Complete] 20,188.29 0.00 0.00 0.00 20,188.29 Cunningham Elementary Fencing 40,746.68 0.00 0.00 0.00 0.00 40,746.68 Cunningham Security Camera System[Complete] 28,982.96 0.00 0.00 0.00 0.00 28,982.96 Julien Elementary Fencing 13,660.00 0.00 0.00 0.00 0.00 0.00 13,660.00 eCademy Charter at Crane Fencing 714.00 0.00 0.00 0.00 0.00 0.00 714.00 Dutcher Middle School 1,961,720.17 0.00 0.00 0.00 0.00 1,961,720.17 Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 0.00 0.00 0.00 0.00 0.00 0.00 Walnut Security Camera System 41,670.17 0.00 0.00 0.00 0.00 0.00 41,670.17		Earl Elementary Phase II - Fencing [Complete]	74,854.26	0.00	0.00	0.00	0.00	74,854.26	
Cunningham Elementary Fencing 40,746.68 0.00 0.00 0.00 40,746.68 Cunningham Security Camera System[Complete] 28,982.96 0.00 0.00 0.00 0.00 0.00 28,982.96 Julien Elementary Fencing 13,660.00 0.00 0.00 0.00 0.00 0.00 13,660.00 eCademy Charter at Crane Fencing 714.00 0.00 0.00 0.00 0.00 714.00 Dutcher Middle School 1,961,720.17 0.00 0.00 0.00 0.00 1,961,720.17 Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 0		Earl Security Camera System	0.00	0.00	0.00	0.00	0.00	0.00	
Cunningham Security Camera System[Complete] 28,982.96 0.00 0.00 0.00 0.00 28,982.96 Julien Elementary Fencing 13,660.00 0.00 0.00 0.00 0.00 0.00 13,660.00 eCademy Charter at Crane Fencing 714.00 0.00 0.00 0.00 0.00 714.00 Dutcher Middle School 1,961,720.17 0.00 0.00 0.00 0.00 1,961,720.17 Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 41,670.17 0.00 0.00 0.00 0.00 0.00 41,670.17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0		Medeiros Security Camera System [Complete]	20,188.29	0.00	0.00	0.00	0.00	20,188.29	
Julien Elementary Fencing 13,660.00 0.00 0.00 0.00 0.00 13,660.00 eCademy Charter at Crane Fencing 714.00 0.00 0.00 0.00 0.00 714.00 Dutcher Middle School 1,961,720.17 0.00 0.00 0.00 0.00 1,961,720.17 Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 0.00 0.00 0.00 0.00 0.00 17,500.00 Turlock Junior High School Security Camera Sys. 0.00 0.00 0.00 0.00 0.00 0.00 0.00 41,670.17 Walnut Security Camera System 41,670.17 0.00 0.		Cunningham Elementary Fencing	40,746.68	0.00	0.00	0.00	0.00	40,746.68	
eCademy Charter at Crane Fencing 714.00 0.00 0.00 0.00 0.00 714.00 Dutcher Middle School 1,961,720.17 0.00 0.00 0.00 0.00 0.00 1,961,720.17 Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 0.00 0.00 0.00 0.00 17,500.00 Turlock Junior High School Security Camera Sys. 0.00 0.00 0.00 0.00 0.00 0.00 0.00 Walnut Security Camera System 41,670.17 0.00 0.00 0.00 0.00 0.00 41,670.17		Cunningham Security Camera System[Complete]	28,982.96	0.00	0.00	0.00	0.00	28,982.96	
Dutcher Middle School 1,961,720.17 0.00 0.00 0.00 0.00 1,961,720.17 Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 0.00 0.00 0.00 0.00 0.00 17,500.00 Turlock Junior High School Security Camera Sys. 0.00 0.00 0.00 0.00 0.00 0.00 0.00 41,670.17 Walnut Security Camera System 41,670.17 0.00 0.00 0.00 0.00 0.00 41,670.17		Julien Elementary Fencing	13,660.00	0.00	. 0.00	0.00	0.00	13,660.00	
Osborn Two-Way Immersion Acad.*** 48,917.56 0.00 666,655.86 0.00 0.00 715,573.42 Turlock Junior High School Mod. 17,500.00 0.00 0.00 0.00 0.00 0.00 17,500.00 Turlock Junior High School Security Camera Sys. 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 41,670.17 Walnut Security Camera System 41,670.17 0.00 0.00 0.00 0.00 0.00 41,670.17		eCademy Charter at Crane Fencing	714.00	0.00	0.00	0.00	0.00	714.00	
Turlock Junior High School Mod. 17,500.00 0.00 0.00 0.00 0.00 17,500.00 Turlock Junior High School Security Camera Sys. 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 41,670.17 0.00 0.00 0.00 0.00 41,670.17 0.00 0.00 0.00 0.00 41,670.17 0.00 0.00 0.00 0.00 0.00 0.00 41,670.17 0.00	ļ	Dutcher Middle School	1,961,720.17	0.00	0.00	0.00	0.00	1,961,720.17	
Turlock Junior High School Security Camera Sys. 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.00 41,670.17 0.00 0.00 0.00 0.00 41,670.17	(Osborn Two-Way Immersion Acad.***	48,917.56	0.00	666,655.86	0.00	0.00	715,573.42	
Walnut Security Camera System 41,670.17 0.00 0.00 0.00 0.00 41,670.17		Turlock Junior High School Mod.	17,500.00	0.00	0.00	0.00	0.00	17,500.00	
	-	Furlock Junior High School Security Camera Sys.	0.00	0.00	0.00	0.00	0.00	0.00	
Total Expenditures by Funding 4,328,488.19 1,888,549.90 666,655.86 0.00 0.00 6,883,693.95	١	Nalnut Security Camera System	41,670.17	0.00	0.00	0.00	0.00	41,670.17	
	٦	Total Expenditures by Funding	4,328,488.19	1,888,549.90	666,655.86	0.00	0.00	6,883,693.95	

Notes: (1) Unspent bond proceeds from measure N earned \$123,939 in interest, as of 6/30/2018. (2) Unspent proceeds from measures N & O, combined, earned an additional \$302,783.11 in interest, from 7/1/2018 to 3/31/2019. (3) On May 8, 2019 TUSD sold general obligation bonds with a par value of \$13,600,000, to be used to modernize elementary schools per TUSD Board Resolution No. 30/2015-16. The sale proceeds of \$13,497,000 were received by TUSD on 5/22/2019.

6/12/2019, 10:56 AM 1 of 16

^{*}Current unallocated costs from fiscal year 2018-19 will be allocated to projects based on total project expenditures at year end per total measure N expenditures at year end.

^{**}Funding change 6/30/2018. Funded from Developer Fees Collected.

^{***} RDA funding used to purchase two adjoining properties to Osborn Elementary School, one at 217 N. Soderquist Rd and the other at 233 N. Soderquist Rd., Turlock CA 95380 during the 2018-19 fiscal year.

	OL DISTRICT, STANISLAUS COUNTY	<u> </u>	
Current Unallocated Costs			Report Number: 9
			Period Ending: 6/10/20
PLANNING		eraeri (H.)	North Control
ARCHITECT/ENGINEERII	NG FEES		
n enganisan memperapakan pada salah sa Salah salah sa			
	Summary of Architect/Engineering Fees	0.00	
DEPARTMENT OF GENE	RAL SERVICES FEES		
CALIEODNIA DEDADTME	Summary of Department of General Services Fees INT OF EDUCATION FEES	0.00	
CALIFORNIA DEPARTIME	INT OF EDUCATION FEES		
	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING			
	Summary of Preliminary Testing	0.00	
OTHER PLANNING COST			
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
10/3/2018 36065693			General Counsel
12/12/2018 36079070			General Counsel
1/11/2019 36083537 1/11/2019 36083537			General Counsel General Counsel
2/1/2019 36087357			General Counsel
3/6/2019 36093074			General Counsel
4/3/2019 36098588			General Counsel
5/15/2019 36106929			General Counsel
	Signs of Success, Inc.		TUSD Signs
	Vavrinek Trine Day & Co., LLP.		Bond Audit Reports
	Summary of Other Planning Cost	17,728.73	•
	TOTAL PLANNING	17,728.73	
		.,,,,,,	
CONSTRUCTION			
MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION	COSTS		
	Summary of Other Construction Costs	0.00	
INSPECTION			
	Summary of Inspection	0.00	
LABOR COMPLIANCE	• •		
EADON COMPENANCE			
	Summary of Labor Compliance	0.00	
CONSTRUCTION TESTS	Cummary of Eabor Compilation	0.00	,
	Summary of Construction Tests	0.00	
FURNITURE & EQUIPME	NT		
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
TOTAL CURRENT UNALLO	OCATED COSTS	17,728.73	
TOTAL GURKENT UNALLO	OCATED COSTS	11,120.13	:

6/12/2019, 10:56 AM

Wakefield Elementary - Pha	se II Modernization		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERI 11/14/2018 36073998	NG FEES FF & J Architects, INC.	17,500.00	Topographic Survey
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees ERAL SERVICES FEES	17,500.00	
CALIFORNIA DEPARTMI	Summary of Department of General Services Fees ENT OF EDUCATION FEES	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER BY ANNUAL COOR	Summary of Preliminary Testing	0.00	
OTHER PLANNING COS 1/17/2018 36018579	Stanislaus Co. Clerk/Recorder	57.00	CEQA-Exempt Filing Notice
	Summary of Other Planning Cost TOTAL PLANNING	57.00 17,557.00	
CONSTRUCTION MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
TOTAL WAKEFIELD PHASE	II MODERNIZATION	17,557.00	

6/12/2019, 10:56 AM 3 of 16

Wakefield Elementary School	- Security Camera System		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERIN	G FEES		
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	0.00	
CALIFORNIA DEPARTMEN	Summary of Department of General Services Fees NT OF EDUCATION FEES	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	•
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost TOTAL PLANNING	0.00	•
CONSTRUCTION MAIN CONSTRUCTION			
11/9/2018 36073373 11/20/2018 36075431 3/20/2019 36096148	Johnson Controls Security Solutions Johnson Controls Security Solutions Johnson Controls Security Solutions	25,672.48 4,381.52	Security Cameras Security Cameras Security Cameras
OTHER CONSTRUCTION (Summary of Main Construction	39,363.00	
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	-
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	-
	Summary of Furniture & Equipment	0.00	-
	TOTAL CONSTRUCTION	39,363.00	-
TOTAL WAKEFIELD SECUR	ITY CAMERA SYSTEM	39,363.00	- · · · · · · · · · · · · · · · · · · ·

6/12/2019, 10:56 AM 4 of 16

	OL DISTRICT, STANISLAUS COUNTY Phase II Fencing & Modernization		Report Number: 9
			Period Ending: 6/10/2019
PLANNING	MC EEES		
ARCHITECT/ENGINEERI 1/5/2018 36016475		500.00	Architecture/Engineering
1/30/2018 36021052			Architecture/Engineering
3/2/2018 36026799			Architecture/Engineering
3/28/2018 36032049		and the second second	Architecture/Engineering
5/30/2018 36044315			Architecture/Engineering
6/1/2018 36044955		3,000.00	Architecture/Engineering
6/20/2018 36048445			Architecture/Engineering
6/20/2018 36048445			Architecture/Engineering
6/20/2018 36048445 11/29/2018 36076711	SKW & Associates SKW & Associates		Architecture/Engineering Architecture/Engineering
1/4/2019 36082214	SKW & Associates		Architecture/Engineering
1/4/2019 36082214	SKW & Associates		Architecture/Engineering
2/8/2019 36088585	SKW & Associates		Architecture/Engineering
2/8/2019 36088585	SKW & Associates		Architecture/Engineering
3/8/2019 36093665	SKW & Associates	4,870.00	Architecture/Engineering
4/12/2019 36100960	SKW & Associates		Architecture/Engineering
4/12/2019 36100960	SKW & Associates		Architecture/Engineering
4/12/2019 36100960 4/12/2019 36100960	SKW & Associates SKW & Associates		Architecture/Engineering
5/30/2019 36110122	SKW & Associates		Architecture/Engineering Architecture/Engineering
	5 JTS Modular Inc.		Architecture/Engineering
	Summary of Architect/Engineering Fees	76,826,47	
DEPARTMENT OF GENE		70,020.47	
1/2/2019 36081792	Division of State Architect	9,225,00	Plan Review Fees
	Summary of Department of General Services Fee		
CALIFORNIA DEPARTME		-,	
	Summary of California Department of Education F	ees 0,00	
DDEL IMINADY TECTING	Outminity of California Department of Education 1	0,00	
PRELIMINARY TESTING			
	Summary of Preliminary Testing	0.00	
OTHER PLANNING COST			
6/30/2018	Previoulsy Unallocated Costs	1,736.11	Debt Report, Legal, Consulting
	Summary of Other Planning Cost	1,736.11	
	TOTAL PLANNING	87,787.58	
ONSTRUCTION			
MAIN CONSTRUCTION			100
6/30/2018 EP180933	All Commercial Fence	45 687 00 F	encing Contractor
10/3/2018 36065615	All Commercial Fence		encing Contractor
5/8/2019 36105325	JTS Modular Inc.		Andular Building
3.5.2515 3513352	Summary of Main Construction	236,281.15	
•	Summary of Mean Construction	200,201.10	
OTHER CONSTRUCTION	COSTS		
1/5/2018 36016419	Northstar Engineering Grp.	11,349.00 T	opographic Survey
1/30/2018 36021028	Northstar Engineering Grp.		opographic Survey
9/21/2018 36063698	Northstar Engineering Grp.		Itility Topo Survey
12/12/2018 36079076 1/4/2019 36082197	Northstar Engineering Grp.		ivil Engineering
3/8/2019 36093654	Northstar Engineering Grp. Northstar Engineering Grp.		ivil Engineering ivil Engineering
4/26/2019 36103391	McClatchy Newspaper Inc.		lotice to Bidders
472072013 00100031	, , ,		
	Summary of Other Construction Costs	21,319.04	
NSPECTION			
	United Inspection Inc.		onstruction Inspection
	United Inspection Inc. United Inspection Inc.		onstruction Inspection onstruction Inspection
11/29/2010 300/33/3	•		onstruction inspection
	Summary of Inspection	1,440.00	
ABOR COMPLIANCE			
	Summary of Labor Compliance	0.00	
ONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
8/8/2018 36055832	Kleinfelder	230.00 C	onstruction Testing
10/5/2018 36066310	Kleinfelder		onstruction Testing
11/9/2018 36073375	Kleinfelder	5,409.25 C	onstruction Testing
1 11912010 30073373			

9,706.45

0.00 268,746.64

5 of 16

356,534.22

TOTAL BROWN PHASE II FENCING & MODERNIZATION

FURNITURE & EQUIPMENT

6/12/2019, 10:56 AM

Summary of Construction Tests

Summary of Furniture & Equipment

TOTAL CONSTRUCTION

Crowell Elementary School - Fe	DISTRICT, STANISLAUS COUNTY encing and Modernization		Report Number: 9
			Period Ending: 6/10/2019
PLANNING			
ARCHITECT/ENGINEERING	G FEES		
3/28/2018 36032049	SKW & Associates	13,330.00	Architecture/Engineering
5/30/2018 36044315	SKW & Associates	213.88	Architecture/Engineering
	SKW & Associates	1,058.55	Architecture/Engineering
6/1/2018 36044955	SKW & Associates	5,000.00	Architecture/Engineering
	SKW & Associates	4.442.00	Architecture/Engineering
6/20/2018 36048445	SKW & Associates		Architecture/Engineering
6/20/2018 36048445	SKW & Associates		Architecture/Engineering
10/24/2018 36070007	SKW & Associates		Architecture/Engineering
			Architecture/Engineering
11/29/2018 36076711	SKW & Associates		
1/4/2019 36082214	SKW & Associates		Architecture/Engineering
1/4/2019 36082214	SKW & Associates	1417.75	Architecture/Engineering
	Summary of Architect/Engineering Fees	29,129.59	
DEPARTMENT OF GENERA	AL SERVICES FEES		
	Summary of Department of General Services Fees	0.00	•
CALIFORNIA DEPARTMEN	T OF EDUCATION FEES		
	Summary of California Department of Education Fees	0.00	•
PRELIMINARY TESTING			
	Summary of Preliminary Testing	0.00	•
OTHER PLANNING COST	Positive Novella anta d Conta	2 000 40	Dalah Danasi I anal Oceanillina
6/30/2018	Previoulsy Unallocated Costs		Debt Report, Legal, Consulting
	Summary of Other Planning Cost	3,298.48	
	TOTAL PLANNING	32,428.07	
CONCEDUCTION			
CONSTRUCTION			
MAIN CONSTRUCTION			
6/30/2018 EP180934	All Commercial Fence		Fencing Contractor
10/3/2018 36065615	All Commercial Fence		Fencing Contractor
8/15/2018 36057013	Pauls Glass Company	13143.24	Storefront
	Summary of Main Construction	266,223.24	-
OTHER CONSTRUCTION C	COSTS		
1/5/2018 36016419	Northstar Engineering Group	6,444.00	Topographic Survey
1/30/2018 36021028	Northstar Engineering Group	7,876.00	Topographic Survey
2, 22, 222			
	Summary of Other Construction Costs	14,320.00	
INSPECTION			
8/15/2018 36057027	United Inspection Inc.	2,160.00	Construction Inspection
10/10/2018 36067139	United Inspection Inc.	1,296.00	Construction Inspection
	United Inspection Inc.	864.00	Construction Inspection
1020,2010 000.0.20	•	***************************************	- '
LABOR COMPLIANCE	Summary of Inspection	4,320.00	
Eribott com Entrol			
	Summary of Labor Compliance	0.00	-
CONSTRUCTION TESTS	Canada of East, Complained	0.00	
8/8/2018 36055832	Kleinfelder	230.00	Construction Testing
	Summary of Construction Tests	230.00	
FURNITURE & EQUIPMENT		250.00	
	Summary of Furniture & Equipment	0.00	-
	TOTAL CONSTRUCTION	285,093.24	-
TOTAL COOMELL ELEMENT	FADV EENCING & MODERNIZATION	317,521.31	-
IOTAL CROWELL ELEMENT	FARY FENCING & MODERNIZATION	317,521.31	=

6/12/2019, 10:56 AM 6 of 16

Earl Elementary School - Ph	ase II Fencing		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERII	NG FEES		
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees RAL SERVICES FEES	0.00	
CALIFORNIA DEPARTME	Summary of Department of General Services Fees NT OF EDUCATION FEES	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
6/30/2018	Previoulsy Unallocated Costs	279.26	Debt Report, Legal, Consulting
	Summary of Other Planning Cost	279.26	
	TOTAL PLANNING	279.26	
CONSTRUCTION MAIN CONSTRUCTION 6/30/2018 EP180935 10/3/2018 36065615	All Commercial Fence All Commercial Fence	61,525.00	Fencing Contractor Fencing Contractor
	Summary of Main Construction	74,575.00	
OTHER CONSTRUCTION	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	
•			
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	74,575.00	
TOTAL EARL ELEMENTARY	PHASE II FENCING	74,854.26	

6/12/2019, 10:56 AM. 7 of 16

Medeiros Elementary School -	DISTRICT, STANISLAUS COUNTY Security Camera System		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERING	3 FEES		
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	0.00	
CALIFORNIA DEPARTMEN	Summary of Department of General Services Fees	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
6/30/2018	Previoulsy Unallocated Costs	109.15	Debt Report, Legal, Consulting
	Summary of Other Planning Cost	109.15	
	TOTAL PLANNING	109.15	•
CONSTRUCTION MAIN CONSTRUCTION 6/30/2018 EP180639 11/14/2018 36074004	Tyco Fire & Security Johnson Controls Security Solutions Summary of Main Construction		Security Cameras Security Cameras
OTHER CONSTRUCTION O	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	-
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	<u>-</u> -
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	-
	Summary of Furniture & Equipment	0.00	,
	TOTAL CONSTRUCTION	20,079.14	<u>-</u>
TOTAL MEDEIROS SECURI	TY CAMERA SYSTEM	20,188.29	

	OL DISTRICT, STANISLAUS COUNTY		
Cunningham Elementary Sc	hool - Fencing		Report Number: 9 Period Ending: 6/10/2019
PLANNING			
	NO FEEC		
ARCHITECT/ENGINEERI		5 E00 00	A
10/24/2018 36070007 3/8/2019 36093665			Architecture/Engineering
			Architecture/Engineering
4/12/2019 36100960 4/12/2019 36100960			Architecture/Engineering
4/12/2019 36100960			Architecture/Engineering Architecture/Engineering
4/19/2019 36102250			Architecture/Engineering
5/30/2019 36110135			Architecture/Engineering
5/30/2019 36110135			Architecture/Engineering
3/30/2013 301/10/103		40.063.59	
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees RAL SERVICES FEES	40,003.39	
	Summary of Department of General Services Fees	0.00	-
GALIFORNIA DEPARTME	NT OF EDUCATION FEES Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING	Summary of Camorna Department of Education Fees	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	40,063.59	
CONSTRUCTION MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION		000.00	N. C. C. W. L.
4/26/2019 36103391	McClatchy Newspaper, Inc.	683.09	Notice to Bidders
	Summary of Other Construction Costs	683.09	
INSPECTION		300.33	
	Summary of Inspection	0.00	
LABOR COMPLIANCE			
			•
CONCEDUCTION TESTS	Summary of Labor Compliance	0.00	
CONSTRUCTION TESTS			
	Summary of Construction Tests	0.00	
FURNITURE & EQUIPMEN	Т		
	Summary of Furniture & Equipment	0.00	·
	TOTAL CONSTRUCTION	683.09	
TOTAL CUNNINGHAM ELEM	ENTARY FENCING	40,746.68	

6/12/2019, 10:56 AM 9 of 16

Cunningham Elementary Scho	ol - Security Camera System		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERING	3 FEES		
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	0.00	
CALIFORNIA DEPARTMEN	Summary of Department of General Services Fees IT OF EDUCATION FEES	0.00	•
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	•
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost	0.00	-
CONSTRUCTION	TOTAL PLANNING	0.00	
MAIN CONSTRUCTION 11/20/2018 36075431 12/12/2018 36079067	Johnson Controls Security Solutions Johnson Controls Security Solutions	22,106.96	Security Cameras Security Cameras
OTHER CONSTRUCTION (Summary of Main Construction COSTS	28,982.96	
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	<u>-</u>
LABOR COMPLIANCE			
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	5
	Summary of Furniture & Equipment	0.00	,
	TOTAL CONSTRUCTION	28,982.96	
TOTAL CUNNINGHAM SEC	JRITY CAMERA SYSTEM	28,982.96	<u> </u>

DETAILED LISTING OF PROJECT EXPENDITURES - BOND MEASURE N TURLOCK UNIFIED SCHOOL DISTRICT, STANISLAUS COUNTY Julien Elementary School - Fencing

Julien Elementary School - I	encing		Report Number: 9 Period Ending: 6/10/2019
PLANNING	어린 시작된 이 경기가 돌아왔다며 했다.		
ARCHITECT/ENGINEERI			
11/29/2018 36076711 5/30/2019 36110135			Architecture/Engineering
5/30/2019 30110135		13,660.00	Architecture/Engineering
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees RAL SERVICES FEES	13,660.00	
CALIEODNIA DEDADTME	Summary of Department of General Services Fees	0.00	
CALIFORNIA DEPARTIME			
	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING			
OTHER BLANKING COOT	Summary of Preliminary Testing	0.00	
OTHER PLANNING COST			
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	13,660.00	
CONSTRUCTION MAIN CONSTRUCTION			
WAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
		0.00	
OTHER CONSTRUCTION	COSTS		
	Summary of Other Construction Costs	0.00	
INSPECTION	durantary of other defination design	0.00	
1401 2011014			
	Cummany of Ingagation		
LAROR COMPLIANCE	Summary of Inspection	0.00	
LABOR COMPLIANCE			
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
CONSTRUCTION 1ESTS			
	Summary of Construction Tests	0.00	
FURNITURE & EQUIPMEN		,	
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
OTAL JULIEN ELEMENTAR	Y FENCING	13,660.00	
COMMENT LEENILMINI			· · · · · · · · · · · · · · · · · · ·

6/12/2019, 10:56 AM

eCademy Charter at Crane So			Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERIN 10/24/2018 36070007		714 00 7	Architecture/Engineering
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees	714.00	
CALIFORNIA DEPARTMEI	Summary of Department of General Services Fees NT OF EDUCATION FEES	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	714.00	
CONSTRUCTION MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
TOTAL ECADEMY CHARTE	R AT CRANE FENCING	714.00	

6/12/2019, 10:56 AM 12 of 16

DETAILED LISTING OF PROJECT EXPENDITURES - BOND MEASURE N

	lodernization		Report Number: 9
化氯化甲基甲基甲基苯酚 医电影电影			Period Ending: 6/10/2019
PLANNING			
ARCHITECT/ENGINEE	PING FEFS		
6/30/2017 170669		4 725 00	Architect - Preliminary desig
9/6/2017 3697770			Architect - Preliminary design
9/22/2017 3698114			Architect - Preliminary design
11/21/2017 3699244			Architect - Preliminary design
11/29/2017 3699337			Architect - Preliminary design
3/28/2018 3603205	7 Teter LLP	7,112.50) Architect - Preliminary desig
6/1/2018 3604496	2 Teter LLP	190,797.99	Architect - Final design
6/30/2018 EP18046	63 Teter LLP	52,209.61	Architect - Final design
6/30/2018 EP18092	27 Teter LLP		Architect - Final design
8/22/2018 3605840			Architect - Final design
9/21/2018 3606371			Architect - Final design
10/24/2018 3607001			Architect - Final design
		•	
11/20/2018 3607545			Architect - Final design
1/4/2019 3608222			Architect - Final design
3/8/2019 3609367			Architect - Final design
3/8/2019 3609367	3 Teter LLP	9,123.33	Architect - Final design
4/3/2019 3609863	8 Teter LLP	32,386.65	Architect - Final design
4/17/2019 3610174	6 Teter LLP	23,255.74	Architect - Final design
5/15/2019 3610695	0 Teter LLP		Architect - Final design
0			
	Summary of Architect/Engineering Fees	732,305.22	
DEPARTMENT OF GEN			
10/19/2018 3606909	6 Division of State Architect	102,115.03	Plan Review Fees
	Summary of Department of General Services Fees	102,115.03	•
CALIFORNIA DEPARTM	ENT OF EDUCATION FEES		
DDEL MAINLA DV TECTILI	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING			•
	Summary of Preliminary Testing	0.00	
OTHER PLANNING COS	T .	•	
6/30/2018	Previoulsy Unallocated Costs	9,057.63	Debt Report, Legal, Consulti
12/12/2018 36079103	3 City of Turlock	1,889.00	Improvement Plan App. Fee
1/30/2019 3608680	1 California State Water Resources Control BD		Application Fee
4/19/2019 3610226			Hydrant Flow Test Fee
77.57.257.5 55.1522.5	· · · · · · · · · · · · · · · · · · ·	·	.,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
	Summary of Other Planning Cost	11,775.63	
•	TOTAL PLANNING	846,195.88	
ONSTRUCTION			
21101110011			
MAIN CONSTRUCTION			
	2 Giobal Modular, Inc.	78,442.80	Modular Classrooms (4ea.)
6/5/2019 36110982			
6/5/2019 36110982 4/24/2019 36102822	Acme Construction Co., Inc.	501,444.44	May Lease Payment
6/5/2019 36110982 4/24/2019 36102822		501,444.44 501,444.44	
6/5/2019 36110982 4/24/2019 36102822	Acme Construction Co., Inc.	501,444.44	May Lease Payment
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527;	2. Acme Construction Co., Inc. 3. Acme Construction Co., Inc. Summary of Main Construction	501,444.44 501,444.44	May Lease Payment
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION	2. Acme Construction Co., Inc. 3. Acme Construction Co., Inc. Summary of Main Construction	501,444.44 501,444.44 1,081,331.68	May Lease Payment June Lease Payment
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION 11/21/2017 36992411	2. Acme Construction Co., Inc. 3. Acme Construction Co., Inc. Summary of Main Construction I COSTS Northstar Engineering Group, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53	May Lease Payment June Lease Payment Topographic Survey
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction 4 COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84	May Lease Payment June Lease Payment Topographic Survey Boundary Survey
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. Summary of Main Construction 4 COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey
6/5/2019 36110982 4/24/2019 36102822 5/8/2019 36105273 DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898	2. Acme Construction Co., Inc. 3. Acme Construction Co., Inc. Summary of Main Construction 4. COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8. Northstar Engineering Group, Inc. 8. Northstar Engineering Group, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 36110982 4/24/2019 36102823 5/8/2019 36105273 DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. Summary of Main Construction 4 COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey
6/5/2019 36110982 4/24/2019 36102822 5/8/2019 36105273 DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898	2. Acme Construction Co., Inc. 3. Acme Construction Co., Inc. Summary of Main Construction 4. COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8. Northstar Engineering Group, Inc. 8. Northstar Engineering Group, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 3611098: 4/24/2019 3610282: 5/8/2019 3610527: DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898 4/3/2019 36098599	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. Summary of Main Construction 4 COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. 9 McClatchy Newspaper, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 3611098: 4/24/2019 3610282: 5/8/2019 3610527: DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898 4/3/2019 36098599	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. Summary of Main Construction 4 COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. 9 McClatchy Newspaper, Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP18089; 4/3/2019 36098599	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. Summary of Main Construction I COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. McClatchy Newspaper, Inc. Summary of Other Construction Costs	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP18089; 4/3/2019 36098599	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction I COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. 9 McClatchy Newspaper, Inc. Summary of Other Construction Costs Summary of Inspection	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 3611098: 4/24/2019 3610282: 5/8/2019 3610527: OTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898 4/3/2019 36098599 NSPECTION LABOR COMPLIANCE	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. Summary of Main Construction I COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. McClatchy Newspaper, Inc. Summary of Other Construction Costs	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey
6/5/2019 3611098: 4/24/2019 3610282: 5/8/2019 3610527: DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180896 4/3/2019 36098599 NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction 1 COSTS Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. 9 McClatchy Newspaper, Inc. Summary of Other Construction Costs Summary of Inspection Summary of Labor Compliance	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
6/5/2019 36110982 4/24/2019 36102822 5/8/2019 36105273 DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 13/2/2018 36026784 6/30/2018 EP180898 4/3/2019 36098599 NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS 2/22/2019 36091037	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction I COSTS Northstar Engineering Group, Inc. Summary of Other Construction Costs Summary of Inspection Summary of Labor Compliance CTE CAL Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 0.00 3,800.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
6/5/2019 3611098: 4/24/2019 3610282: 5/8/2019 3610527: DTHER CONSTRUCTION 11/21/2017 36992411 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180896 4/3/2019 36098599 NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction 1 COSTS Northstar Engineering Group, Inc. Summary of Other Construction Costs Summary of Inspection Summary of Labor Compliance CTE CAL Inc. CTE CAL Inc.	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 0.00 3,800.00 2,200.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180896 4/3/2019 36098599; NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS 2/22/2019 36091037 2/22/2019 36091037	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction Northstar Engineering Group, Inc. Summary of Other Construction Costs Summary of Other Construction Costs Summary of Labor Compliance CTE CAL Inc. CTE CAL Inc. Summary of Construction Tests	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 0.00 3,800.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
4/24/2019 36102822 5/8/2019 36105273 OTHER CONSTRUCTION 11/21/2017 36992411 11/21/2018 36026784 6/30/2018 EP180898 4/3/2019 36098599 INSPECTION LABOR COMPLIANCE CONSTRUCTION TESTS 2/22/2019 36091037	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction N COSTS Northstar Engineering Group, Inc. Northst	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 3,800.00 2,200.00 6,000.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; OTHER CONSTRUCTION 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180896 4/3/2019 36098599; NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS 2/22/2019 36091037 2/22/2019 36091037	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction Northstar Engineering Group, Inc. Summary of Other Construction Costs Summary of Other Construction Costs Summary of Labor Compliance CTE CAL Inc. CTE CAL Inc. Summary of Construction Tests	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 0.00 3,800.00 2,200.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; DTHER CONSTRUCTION 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP18089; 4/3/2019 36098599; NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS 2/22/2019 36091037 2/22/2019 36091037	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Summary of Main Construction N COSTS Northstar Engineering Group, Inc. Northst	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 3,800.00 2,200.00 6,000.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors
6/5/2019 3611098; 4/24/2019 3610282; 5/8/2019 3610527; DTHER CONSTRUCTION 11/21/2017 36992411 3/2/2018 36026784 6/30/2018 EP180898 4/3/2019 36098599 NSPECTION ABOR COMPLIANCE CONSTRUCTION TESTS 2/22/2019 36091037 2/22/2019 36091037	2 Acme Construction Co., Inc. 3 Acme Construction Co., Inc. 5 Acme Construction Co., Inc. 5 Monthstar Engineering Group, Inc. Northstar Engineering Group, Inc. Northstar Engineering Group, Inc. 8 Northstar Engineering Group, Inc. 8 McClatchy Newspaper, Inc. 5 McClatchy Newspaper, Inc. Summary of Other Construction Costs Summary of Inspection Summary of Labor Compliance CTE CAL Inc. Summary of Construction Tests NT Summary of Furniture & Equipment	501,444.44 501,444.44 1,081,331.68 5,889.53 3,420.84 14,775.47 3,064.16 1,042.61 28,192.61 0.00 3,800.00 2,200.00 6,000.00	May Lease Payment June Lease Payment Topographic Survey Boundary Survey Topographic Survey Boundary Survey Notice to Contractors

6/12/2019, 10:56 AM 13 of 16

TURLOCK UNIFIED SCHOOL	L DISTRICT, STANISLAUS COUNTY		
Osborn Two-Way Immersion	Academy - Modernization		Report Number: 9
			Period Ending: 6/10/2019
		<u> </u>	
PLANNING			
ARCHITECT/ENGINEERIN			
	Summary of Architect/Engineering Fees	0.00	
DEPARTMENT OF GENE	RAL SERVICES FEES		그 본 이 기업은 그림을 받았다.
A STATE OF THE STA		0.00	
CALIFORNIA DEDARETARE	Summary of Department of General Services Fees NT OF EDUCATION FEES	. 0.00	
CALIFORNIA DEFARTIME			
	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING			
	Summary of Preliminary Testing	0.00	
OTHER PLANNING COST	i i		
10/25/2017 36987180	Lozano Smith LLP		General Legal Counsel
11/21/2017 36992401			General Legal Counsel
12/15/2017 36997452			General Legal Counsel
1/30/2018 36021011			General Legal Counsel
2/14/2018 36023756 3/14/2018 36029003			General Legal Counsel General Legal Counsel
4/4/2018 36032998			General Legal Counsel
5/2/2018 36038509			General Legal Counsel
5/30/2018 36044272			General Legal Counsel
6/29/2018 EP180037		260.00	General Legal Counsel
6/30/2018 EP180871		907.00	General Legal Counsel
9/5/2018 36060242		446.75	General Legal Counsel
10/3/2018 36065693			General Legal Counsel
10/3/2018 36065693			General Legal Counsel General Legal Counsel
10/30/2018 36071033 12/12/2018 36079070		7 350 84	General Legal Counsel
12/12/2018 36079070			General Legal Counsel
12/12/2018 36079070			General Legal Counsel
1/11/2019 36083537	Lozano Smith LLP		General Legal Counsel
2/1/2019 36087357			General Legal Counsel
3/6/2019 36093074			General Legal Counsel
	Paddock Appraisal Service Paddock Appraisal Service		Property Appraisal Property Appraisal
	Paddock Appraisal Service		Property Appraisal
	Cogdill & Assoc, Inc.		Property Appraisal
	Cogdill & Assoc. Inc.	1,500.00	Property Appraisal
	Stanislaus Co. Clerk/Recorder	57.00	CEQA-Exemp Filing Notice
	J.B. Anderson Land Use Planning		CEQA-Compliance Docs
	J.B. Anderson Land Use Planning		CEQA-Compliance Docs
4/4/2018 36032977			Property Appraisal
4/4/2018 36032970 5/16/2018 36041672		2 000 00	Property Information Property Appraisal
6/30/2018	Previoulsy Unallocated Expenditures		Debt Report, Legal, Consulting
11/9/2018 36073434			Advertising-Notice of Hearing
	Summary of Other Planning Cost	48,917.56	-
	-	48,917.56	-
	TOTAL PLANNING	40,917.50	
CONSTRUCTION			
MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	•
	Summary of Marit Constitution	0.00	
OTHER CONSTRUCTION	COSTS		
	Summary of Other Construction Costs	0.00	- 1
INCRECTION	Schillery of Subst Schiller States		
INSPECTION			
	Summary of Inspection	0.00	
LABOR COMPLIANCE			
	Summary of Labor Compliance	0.00	.
CONSTRUCTION TESTS			
	Summary of Construction Tests	0.00	ī
FURNITURE & EQUIPME	NT		
	Summary of Furniture & Equipment	0.00	ī
			_
	TOTAL CONSTRUCTION	0.00	Contraction of the Contraction o
TOTAL OCDODUUMEDO	ON ACADEMY MODERNIZATION	48,917.56	-
TO THE USBURN INNINERSI	OH AGADEM FINODERMIZATION	40,317,30	=
and the second s			

6/12/2019, 10:56 AM 14 of 16

Turlock Junior High Schoo	I - Modernization		Report Number: 9 Period Ending: 6/10/20
PLANNING ARCHITECT/ENGINEER	RING FEES 8 FF & J Architects, INC.	17 500 00	
DEPARTMENT OF GEN	Summary of Architect/Engineering Fees	17,500.00	Topographic Survey
CALIFORNIA DEPARTI	Summary of Department of General Services Fees	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COS	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost TOTAL PLANNING	0.00	
CONSTRUCTION MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPME	Summary of Construction Tests NT	0.00	
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
TOTAL TURLOCK JUNIOR	HIGH SCHOOL MODERNIZATION	17,500.00	

DETAILED LISTING OF PROJECT EXPENDITURES - BOND MEASURE N

TURLOCK UNIFIED SCHOOL	DISTRICT, STANISLAUS COUNTY		
Walnut Elementary Eduction C	Center - Security Camera System		Report Number: 9
	그런 사회 조건들은 연극하다 하는 사람들이 없다.		Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERING	G FEES		
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	0.00	
CALIFORNIA DEPARTMEN	Summary of Department of General Services Fees	0.00	
	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING			
OTHER REANING COST	Summary of Preliminary Testing	0.00	•
OTHER PLANNING COST		0.00	
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	0.00	
CONSTRUCTION			
MAIN CONSTRUCTION	·	272.00	C
3/22/2019 36096705	AMS.NET		Security Cameras Security Cameras
5/30/2019 36110102	AMS.NET AMS.NET		Security Cameras
5/30/2019 36110102 5/30/2019 36110102	AMS.NET		Security Cameras
5/30/2019 36110102	AMS.NET	•	Security Cameras
5/30/2019 36110102	AMS.NET		Security Cameras
3/30/2013 30110102	Summary of Main Construction	41,670.17	
OTHER CONSTRUCTION	COSTS		
	Summary of Other Construction Costs	0.00	-
INSPECTION			
	The section	0.00	-
LABOR COMPLIANCE	Summary of Inspection	0.00	
EABOR COM EIANCE			
	Summary of Labor Compliance	0.00	<u>.</u>
CONSTRUCTION TESTS			
ELIDAUTUDE & FOLUDIMEN	Summary of Construction Tests	0.00	ī
FURNITURE & EQUIPME	N I		•
	Summary of Furniture & Equipment	0.00	-
	TOTAL CONSTRUCTION	41,670.17	,
TOTAL WALNUT ELEMENT	ARY SECURITY CAMERA	41,670.17	7 =

21-0000-0-хххх-0000-хххх-100-Охх						Total		
1st Sale of Bonds	\$14,700,000		2nd Sale of Bonds	\$33,300,000.0		\$48,000,00		
Proceeds Received	\$14,590,000.	30	Proceeds Received	\$33,190,000.0	0	\$47,780,00	00.00 00.00 Cost of Issu	
Org:						\$220,00	JO.UU COST OF ISSU	ance
O000 Vendor	Unallocated Costs Cost	n=14 ac an	D-1447.40		a Called		200	
Vendoi	COSI	Paid 16-17	Paid 17-18	Encumbered 18-19	Pald 18-19	Description	PO# 1836708	Boari 3
							1930468	
Government Financial Strategies	7,159,81	0.00	0.00	0.00	7,159.81	CDIAC Annual Debt	1947128 1941168	
						Report/Consulting	1938348	
							1955208	
Signs of Success	1,148.48	0.00	0.00	0.00	1,148.48	Measure O signs	195854 195113	
							174795 8	١.
VTD & Co., LLP	4,200.00	0.00	0.00	0,00	4,200.00	Annual Audit Measure O	193866 1801978	
Lozano Smith	6,449.48	0.00	0.00	0.00	6,449.48	Measure O - General Counsel	183901& 185441&	. ,
Total:	\$18,957.77	\$0.00	\$0.00	\$0.00	\$18,957.77		191076	

0001 Vendor	Pitman High School - Cost	HVAC Project Paid 16-17	Paid 17-18	Complete Encumbered 18-19	Pald 18-19	Description	PO# .	
United Inspection	18,260.00	0.00	7,000,00	0.00	11,260.00	Construction Inspections	184064	Boar 2/2
Nicro, Inc.	1,718,539.00	0.00	644,452.11	0.00	1,074,086.89	Construction Services	183991	
Nicro, Inc. Change Order	11,031.83	0.00	0.00	0.00	11,031.83	Additional Const. Services	192946	
leinfelder ozano Smith	446,50 29,50	0.00	446.50 29.50	0.00 0.00	0.00 0.00	Construction Testing	184722	
						Measure O - General Counsel	191076 - O000 FY17	
lanning Other Allocation	16,582.45	0.00	16,582.45	0.00	0.00	Previously Unallocated Cost	18	
XW & Associates-Fixed Fee	181,810.23	0.00	150,310.23	0.00	31,500.00	Architectural services	175018& 183676	5/
otal:	\$1,946,699.51	\$0.00	\$818,820.79	\$0.00	\$1,127,878.72			
and the control of th	10-1415.							
002 endor	Pitman High School (# Cost	Architecture Expe Paid 16-17	enditures to be allocate Paid 17-18	ed to 0008, 0009, 0010 & Encumbered 18-19	4 0012 at project o	ompletion) Description	PO#	
orthStar Engineering	11,045.00	0.00	11,045.00	0.00	0.00	Topographic Survey	184314	Board 3/
vision of State Architect	6,750.00	0.00	6,750.00	0.00	0.00	DSA Fee	185413	12/
vision of State Architect	35,550.00	0.00	0.00	0.00	35,550,00	DSA Fee	191015&	12/
anning Other Allocation	4,942,80	0.00	4,942.80	0.00	0.00	Previously Unallocated Cost	191825 O000 FY17-	N
rgensen & CO	2,600,00	0.00	0.00	2,600.00	0.00	Fire Sprinker DSA Design	18 192639	
Design West-T&M Fee	6,320.00	0,00	6,320.00	0.00	0.00	Architect - Preliminary Design	175337	5/16
Design West-Lump Sum Fee	0.00	0.00	0.00	106,010,94	44,840.06	Architect - Final Design-addlt		10/16
Design West-Lump Sum Fee	21,880.00	0.00	215,005.08	8,889.16	360,381.76	Architect - Final Design	183095	12/
otal:	\$89,087.80	\$0.00	\$244,062.88	\$117,500.10	\$440,771.82			
003	Turlock High School (A	rchitecture Expe	nditures to be allocate	ed to 0011 at project com	nietioni			
endor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description		Board
rden Architects-Percent Fee	570,000.00	0.00	35,228.00	263,705.19	271,066,81	Architect - Final Design	183617& 195364	1/23
rden Architects-NTE Fee	37,040.00	0.00	37,040.00	0.00	0.00	Architect - Preliminary Design	175335	5/16
ncing/PA/Security	0.00	0.00	0.00	0,00	0.00	,		-,
nning Other Allocation	1,493.76	0.00	1,493.76	0.00	0.00	Previously Unallocated Cost	0000 FY17-	N
rthstar Engineering	24,640.00	0.00	0,00	0.00	24,640.00	Topographic Survey	18 185132	4/24
tal:	\$633,173.76	\$0,00	\$73,761.76	\$263,705.19	\$295,706.81			
		ecurity Camera	ş [†] .	Phase 1 - Complete				
D4	Pitman High School - Si							
	Pitman High School - Si Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Pald 18-19	Description		Board
ndor			Paid 17-18 0.00		Pald 18-19 0.00	Description Previously Unallocated Cost	0000 FY17-	
ndor nning Other Allocation	Cost	Paid 16-17		Encumbered 18-19		Previously Unallocated Cost	0000 FY17- 18	N/
ndor nning Other Allocation nson Controls Sec. Sol.	Cost 0,00	Paid 16-17 0.00	0.00	0.00 Encumbered 18-19	0.00		0000 FY17- 18	N/
ndor nning Other Allocation nson Controls Sec. Sol. al:	Cost 0.00 87,264.16 \$87,264.16 Turlock High School - Sc	Paid 16-17 0.00 0.00 \$0.00 Sience Building	0,00 0,00 \$0.00	0.00 0.00 0.00 50.00	0.00 87,264.16	Previously Unallocated Cost Security Camera System	0000 FY17- 18	N,
ndor nning Other Allocation nson Controls Sec. Sol. al: 05	Cost 0.00 87,264.16 587,264.16 Turlock High School - Sc Cost	Paid 16-17 0.00 0.00 \$0.00 cience Building Paid 16-17	0.00 0.00 \$0.00 Paid 17-18	0.00 0.00 0.00 \$0.00 Encumbered 18-19	0.00 87,264.16 \$87,264.16 Pald 18-19	Previously Unallocated Cost	O000 FY17- 18 185616	N/
ndor nning Other Allocation unson Controls Sec. Sol. al: 05 odor nning Other Allocation	Cost 0.00 87,254,16 587,254,16 Turlock High School - Sc Cost 2,103,23	Paid 16-17 0.00 0.00 \$0.00 Since Building Paid 16-17 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23	0.00 0.00 50.00 Encumbered 18-19	0.00 87,264.16 \$87,264.16 Paid 18-19 0.00	Previously Unallocated Cost Security Camera System	0000 FY17- 18 185616	6/19 6/19
nning Other Allocation nson Controls Sec. Sol. al: 15 dor nning Other Allocation CAL INC.	Cost 0.00 87,254.16 \$87,264.16 Turlock High School - Sc Cost 2,103.23 8,200.00	Paid 16-17 0.00 0.00 \$0.00 cience Building Paid 16-17 0.00 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00	0.00 0.00 \$0.00 \$0.00 Encumbered 18-19 0.00	0.00 87,264.16 \$87,264.16 Pald 18-19 0.00 8,200.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services	O000 FY17- 18 185616 PO# B O000 FY17- 18 194495	N/ 6/19, oard N/ N/
nning Other Allocation nson Controls Sec. Sol. at: 15 dor nning Other Allocation CAL INC. sion of State Arch	Cost 0.00 87,254,16 587,254,16 Turlock High School - Sc Cost 2,103,23	Paid 16-17 0.00 0.00 \$0.00 Since Building Paid 16-17 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23	0.00 0.00 50.00 Encumbered 18-19	0.00 87,264.16 \$87,264.16 Pald 18-19 0.00 8,200.00 151,950.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services DSA Fee	O000 FY17- 18 185616 PO# B O000 FY17- 18 194495 194420	N/ 6/19 oard N/ N/ 1/23/
ndor nning Other Allocation nson Controls Sec. Sol. al: D5 ndor nning Other Allocation CAL INC. sion of State Arch artment of Conservation	Cost 0,00 87,254,16 \$87,264,16 Turlock High School - Sc Cost 2,103,23 8,200.00 151,950.00 500.00 3,600.00	Paid 16-17 0.00 0.00 \$0.00 \$0.00 Elence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00	0.00 0.00 \$0.00 Encumbered 18-19 0.00 0.00 0.00	0.00 87,264.16 \$87,264.16 Pald 18-19 0.00 8,200.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services	O000 FY17- 18 185616 PO# B O000 FY17- 18 194495 194420	N/ 6/19 oard N/ N/ 1/23/ 1/23/
nning Other Allocation nson Controls Sec. Sol. al: 25 ndor nning Other Allocation CAL INC. sion of State Arch sort of Store Arch artment of Conservation	Cost 0.00 87,254,16 587,254,16 Turlock High School - Sc Cost 2,103,23 8,200,00 151,950,00 500,00	Paid 16-17 0.00 0.00 \$0.00 \$0.00 clience Building Paid 16-17 0.00 0.00 0.00 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00	Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00	0.00 87,264.16 \$87,264.16 Pald 18-19 0.00 8,200.00 151,950.00 500.00	Previously Unallocated Cost Security Carmera System Description Previously Unallocated Cost Geotechnical Services DSA Fee USA Fee Water Use Regulation	PO # B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309	N/ 6/19 oard N/ N/ 1/23/ 1/23/
nning Other Allocation nson Controls Sec. Sol. al: 15 16 17 18 18 19 19 19 19 19 19 19 19 19 19 19 19 19	Cost 0,00 87,254,16 \$87,264,16 Turlock High School - Sc Cost 2,103,23 8,200.00 151,950.00 500.00 3,600.00	Paid 16-17 0.00 0.00 \$0.00 \$0.00 Elence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00	0.00 0.00 50.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00	0.00 87,264.16 \$87,264.16 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00	Previously Unallocated Cost Security Carmera System Description Previously Unallocated Cost Geotechnical Services DSA Fee USA Fee Water Use Regulation	PO # B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309	N, 6/19 oard N/ N/ 1/23, 1/23, N/
nning Other Allocation nson Controls Sec. Sol. al: 15 15 16 17 17 18 18 18 18 18 18 18 18 18 18 18 18 18	Cost 0.00 87,264.16 587,264.16 Turlock High School - Sc Cost 2,103.23 8,200.00 151,950.00 500.00 3,600.00 0.00	Paid 16-17 0.00 0.00 \$0.00 \$0.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 0.00	Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 87,264.16 \$87,264.15 Paid 18-19 0.00 8,200.00 151,950.00 500.00 0.00	Previously Unallocated Cost Security Carmera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee - Water Use Regulation Geologic Study	PO# B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617&	N/ 6/19 oard N/ N/ 1/23/ N/
nning Other Allocation nson Controls Sec. Sol. al: 15 15 16 17 18 18 19 19 19 19 19 19 19 19 19 19 19 19 19	Cost 0.00 87,264.16 \$87,264.16 Turlock High School - Sc Cost 2,103.23 8,200.00 151,950.00 500.00 3,600.00 0.00 1,243,522.25	Paid 16-17 0.00 0.00 \$0.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 0.00 101,750.00	Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 0.00 79,750.00	0.00 87,264.16 \$87,264.16 Pald 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00	Previously Unallocated Cost Security Carmera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee - Water Use Regulation Geologic Study	PO # B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309	N/ 6/19 oard N/ N/ 1/23/ N/
ndor Inning Other Allocation I	Cost 0.00 87,264.16 \$87,264.16 Turlock High School - Sc Cost 2,103.23 8,200.00 151,950.00 500.00 3,600.00 0.00 1,243,522.25 \$1,409,875.48	Paid 16-17 0.00 0.00 \$0.00 \$0.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 0.00 101,750.00 \$103,853.23	Encumbered 18-19 0.00 50.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 0.00 0.00 79,750.00	0.00 87,264.16 \$87,264.15 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00 638,500.00 \$802,750.00	Previously Unallocated Cost Security Carmera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee DSA Fee DSA Fee-Water Use Regulation Geologic Study Architect - Final Design	DO00 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617& 194776& 194863	N/. 6/19, 00ard N/. N/. 1/23/ N/. 1/23/
ndor Inning Other Allocation Inson Controls Sec. Sol. Ital: OS OS Odor Inning Other Allocation I CAL INC. Ission of State Arch Ission of State Arch Ission of State Arch Ission of State Arch Ission of Main Iden Architects-Percent Fee Iden Inson Main Iden Architects-Percent Fee Iden Inson Main Iden Architects Percent Fee Iden Inson Main Iden Inson M	Cost 0.00 87,254,16 587,254,16 Turlock High School - Sc Cost 2,103,23 8,200,00 151,950,00 3,600,00 0.00 1,243,522,25 \$1,409,875,48	Paid 16-17 0.00 0.00 \$0.00 \$0.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 0.00 101,750.00 \$103,853.23	Encumbered 18-19 0.00 0.00 \$0.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 0.00 79,750.00 \$79,750.00 Encumbered 18-19	0.00 87,264.16 \$87,264.16 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00 638,500.00 \$802,750.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee Water Use Regulation Geologic Study Architect - Final Design	PO# B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617& 194776& 194863	N/, 6/19, 6/
ndor nning Other Allocation nnson Controls Sec. Sol. tal: 05 05 16 17 18 18 19 19 19 19 19 19 19 19	Cost 0.00 87,264.16 \$87,264.16 Turlock High School - Sc Cost 2,103.23 8,200.00 151,950.00 500.00 3,600.00 0.00 1,243,522.25 \$1,409,875.48	Paid 16-17 0.00 0.00 \$0.00 \$0.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 0.00 101,750.00 \$103,853.23	Encumbered 18-19 0.00 50.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 0.00 0.00 79,750.00	0.00 87,264.16 \$87,264.16 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00 638,500.00 \$802,750.00	Previously Unallocated Cost Security Carmera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee DSA Fee DSA Fee-Water Use Regulation Geologic Study Architect - Final Design	DO00 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617& 194776& 194863	N/ 6/19, noord N/. 1/23/ 1/23/ 1/23/
nning Other Allocation nning Other Allocation als: D5 ndor nning Other Allocation CAL INC. Ision of State Arch Ision of Stat	Cost 0.00 87,264,16 \$87,264,16 Turlock High School - Sc Cost 2,103,23 8,200,00 151,950,00 500,00 3,600,00 0.00 1,243,522,25 \$1,409,875,48	Paid 16-17 0.00 0.00 50.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 0.00 \$0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 101,750.00 \$103,853.23	Encumbered 18-19 0.00 0.00 50.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 79,750.00 Encumbered 18-19 14,402.99	0.00 87,264.16 \$87,264.16 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00 638,500.00 9802,750.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee Water Use Regulation Geologic Study Architect - Final Design	PO# B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617& 194776& 194863	N/ 6/19, noord N/. 1/23/ 1/23/ 1/23/
nning Other Allocation Inson Controls Sec. Sol. al: 05 odor Indor Ind	Cost 0.00 87,264.16 \$87,264.16 Turlock High School - Sc Cost 2,103.23 8,200.00 151,950.00 500.00 3,600.00 0.00 1,243,522.25 \$1,409,875.48 eCademy Charter at Cra Cost 15,788.99 \$15,788.99	Paid 16-17 0.00 0.00 50.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 0.00 \$0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 101,750.00 \$103,853.23	Encumbered 18-19 0.00 0.00 50.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 79,750.00 Encumbered 18-19 14,402.99	0.00 87,264.16 \$87,264.16 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00 638,500.00 9802,750.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee Water Use Regulation Geologic Study Architect - Final Design	PO# B 0000 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617& 194776& 194863	N/ 6/19, noord N/. 1/23/ 1/23/ 1/23/
ndor nning Other Allocation nning Other Allocation nning Other Allocation and or nning Other Allocation CAL INC. Ision of State Arch Ision of Stat	Cost 0.00 87,264,16 \$87,264,16 Turlock High School - Sc Cost 2,103,23 8,200,00 151,950,00 3,600,00 0.00 1,243,522,25 \$1,409,875,48 eCademy Charter at Cra Cost 15,788,99 \$15,788,99	Paid 16-17 0.00 0.00 50.00 clence Building Paid 16-17 0.00 0.00 0.00 0.00 0.00 0.00 0.00 0.	0.00 0.00 \$0.00 Paid 17-18 2,103.23 0.00 0.00 0.00 0.00 0.00 \$101,750.00 \$103,853.23 Paid 17-18 0.00 \$0.00	Encumbered 18-19 0.00 0.00 50.00 Encumbered 18-19 0.00 0.00 0.00 0.00 0.00 79,750.00 Encumbered 18-19 14,402.99	0.00 87,264.16 \$87,264.16 \$87,264.16 Paid 18-19 0.00 8,200.00 151,950.00 500.00 3,600.00 0.00 \$802,750.00 Paid 18-19 1,386.00 \$1,386.00	Previously Unallocated Cost Security Camera System Description Previously Unallocated Cost Geotechnical Services DSA Fee DSA Fee DSA Fee Water Use Regulation Geologic Study Architect - Final Design	DO00 FY17- 18 185616 PO # B 0000 FY17- 18 194495 194420 194516 195309 183617& 194776& 194863	N/. 6/19/ 6/19/ 000rd N// 1/23/ 1/23/:

6/12/2019, 10:40 AM

Sond Measure O 21-0000-0-xxxx-0000-xxxx-100-0xxx-xx						Total		
st Sale of Bonds	\$14,700,000.00	2	nd Sale of Bonds	\$33,300,000.00		\$48,000,000.00		
roceeds Received	\$14,590,000.00	Р	roceeds Received	\$33,190,000.00		\$47,780,000.00		
)rg:								
0008	Pitman High School - Pla	yfields						
/endor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description I	PO#	Board
a Design West-Lump Sum Fee	297,000.00	0.00	0.00	0.00	0.00	See O002	183095	12/5/2017
a Design West-Addendum	104,683.00	0.00	0.00	0.00	0.00	Architect - Final Design-addlt	192893	10/16/2018
				The second second second			193008&	10/16/188
T Brayton & Sons	3,589,445.00	0.00	0.00	598,241.00	2,991,204.00	Playfield Renovations	193771	12/11/18
ield Turf USA Inc.	691,156.20	0.00	0.00	35,388.23	654,767.97	Playfield Artificial Turf	193229	11/6/2018
Beynon Sports Surfaces	356,685.00	0.00	0.00	356,685.00	0.00	Playfield Synthetic Track	193222	11/6/2018
Geinfedler.	45,000.00	0.00	0.00	28,448.00	16,552.00	Materials Testing	193223	11/6/2018
United inspection	36,272.00	0,00	0.00	0.00.	36,272.00	Inspection Services	193224	11/6/2018
Modesto Bee	1,270.30	0.00	0.00	0.00	1,270.30	Advertisement-Notice to Contr.	192050	9/4/2018
Total:	\$5,121,511.50	\$0.00	\$0.00	\$1,019,762.23	\$3,700,066.27			7.1
Org:								
0009	Pitman High School - Fir	e Alarm						
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO #	Board
Ca Design West-Lump Surn Fee	24,500.00	0.00	0.00	0.00	0.00	See 0002	183095	12/5/2017
United inspection	6,200.00	0.00	0,00	6,200.00	0.00	Inspection Services	195316	N/A
Johnson Controls Fire Protect.	613,360.19	0.00	0.00	370.096.62	243,263.57	Fire Alarm System	193502	9/4/2018
Total:	\$644,060.19	\$0.00	\$0.00	\$376,296.62	\$243,263.57			
Org:								
0010	Pitman High School - Fe							
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19		PO #	Board
Ca Design West-Lump Sum Fee	90,576.00	0.00	0.00	0.00	0.00	See O002	183095	12/5/201
Ca Design West-Addendum	0.00	0.00	0.00	0.00	0.00	See O002		10/16/201
A&A Portables Inc.	594.50	0.00	0.00	594.50	0.00	Portable Restrooms	195985	N/A
Crime Tek Security	3,000.00	0,00	0.00	3000.00	0.00	Security Services	196011	N/A
CT Brayton & Sons	1,061,953.20	0.00	0.00	857,331.14	204,622.06	PH5 Fencing & Office	195114	3/19/201
Kleinfedler	20,000.00	0.00	0.00	20,000.00	0.00	Materials Testing	195725	4/16/201
United inspection	13,568.00	0.00	0.00	13,568.00	0.00	Inspection Services	196004	4/16/201
McClatchy Newspaper Inc.	1,282.29	0.00	0.00	0.00	1,282.29	Advertisement-Notice to Contracto	194396	2/5/201
Total:	\$1,190,973.99	\$0.00	\$0.00	\$894,493.64	\$205,904.35			
Orm								
Org: 0011	Turlock High School - Re	ofing Bldgs B &	L					
Vendor	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO #	Board
Darden Architects-Percent Fee	0.00	0.00	0.00	0,00	0.00	See 0003	183617	1/23/201
McClatchy Newspaper Inc.	731.02	0.00	0.00	731.02	0.00	Advertisement-Notice to Bidders	194940	
Brazos Urethane, Inc.	981,850.00	0.00	0,00	981,850.00	0.00	Roofing Replacement	195887	5/7/201
United Inspections Inc.	7,560.00	0.00	0.00	7,560.00	0.00	Inspection Services	195829	N/A
Division of State Architect	23,600,00	0.00	0.00	0,00	23,600.00	DSA Fee	194383	1/23/201
Total:	\$1,013,741.02	\$0.00	\$0.00	\$990,141.02	\$23,600.00			
Org:	Pitman High School - Co	ilinaru Arte						
0012	Cost	Paid 16-17	Paid 17-18	Encumbered 18-19	Paid 18-19	Description	PO#	Board
Vendor		0,00	0.00	0.00	0.00	See OOO2	183095	
Ca Design West-Lump Sum Fee	94,500.00	0.00	0.00	0.00	0.00	See 0002	192893	
Ca Design West-Addendum	105,668.00				0.00		196004	
United Inspection	13,568.00	0.00	0.00	13,568.00 1,431,211.56	333,857.34	Inspection Services	195004	
CT Brayton & Sons	1,765,068.90	0.00	0.00			PHS Culinary Arts	193114	əj 19/201
Total:	\$1,978,804.90	\$0.00	\$0.00	\$1,444,779.56	\$333,857.34			
Total Balance O:	\$14,165,006.49	\$0.00	\$1,240,498.66	\$5,214,138.77	\$7,283,166.81			

533,614,993.51
Total Balance O includes estimated Architectural fees (percentage based fees) to cover the cost of current design. Those fees will increase once more information is available for 0003, 0005, 0006, 0007 and 0011.

TURLOCK UNIFIED SCHOOL DISTRICT GENERAL OBLIGATION BOND - MEASURE O Bond Issue to Date Expenditure by Funding Summary Report As of June 10, 2019

Total Expenditures by Funding	8,523,665.47	0.00	0.00	0.00	8,523,665.47
Roselawn High Fencing	1,760.00	0.00	0.00	0.00	1,760.00
eCademy Charter at Crane Fencing	1,386.00	0.00	0.00	0.00	1,386.00
Turlock High Roofing Buildings B&L	23,600.00	0.00	0.00	0.00	23,600.00
Turlock High Science Building	906,603.23	0.00	0.00	0.00	906,603.23
Turlock High Modernization	369,468.57	0.00	0.00	0.00	369,468.57
Pitman High Culinary Arts	333,857.34	0.00	0.00	0.00	333,857.34
Pitman High Fencing and Office	205,904.35	0.00	0.00	0.00	205,904.35
Pitman High Fire Alarm	243,263.57	0.00	0.00	0.00	243,263.57
Pitman High Playfields	3,700,066.27	0.00	0.00	0.00	3,700,066.27
Pitman Security Camera Sys.[Complete]	87,264.16	0.00	0.00	0.00	87,264.16
Pitman High Modernization**	684,834.70	0.00	0.00	0.00	684,834.70
Pitman High HVAC [Complete]	1,946,699.51	0.00	0.00	0.00	1,946,699.51
Unallocated Costs*	18,957.77	0.00	0.00	0.00	18,957.77
	Building GO Bond O	Capital Facilities (Developer Fees)	Special Reserve (Local Fund)	General (General Admin)	Total

Notes: (1) Unspent bond proceeds from measure O earned \$169,122 in interest, as of 6/30/2018. (2) Unspent proceeds from measures N & O, combined, earned an additional \$302,783.11 in interest, from 7/1/2018 to 3/31/2019. (3) On May 8, 2019 TUSD sold general obligation bonds with a par value of \$33,300,000, to be used to modernize high schools per TUSD Board Resolution No. 31/2015-16. The sale proceeds of \$33,190,000 were received by TUSD on May 22, 2019.

6/12/2019 11:14 AM 1 of 13

^{*}Current unallocated costs from fiscal year 2018-19 will be allocated to projects based on total project expenditures at year end per total measure O expenditures at year end .

^{**}Pitman High modernization design and planning fees will be allocated to specific projects at the completion of projects.

	OL DISTRICT, STANISLAUS COUNTY		
Current Unallocated Costs			Report Number: 9
			Period Ending: 6/10/2019
PLANNING			
ARCHITECT/ENGINEERI	NG FEES		
		0.00	
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees	0.00	
DEI ARTIMENT OF GENE	INTERIOR TEED		
	Summary of Department of General Services Fees	0.00	
CALIFORNIA DEPARTME	ENT OF EDUCATION FEES		
	Summary of California Department of Education Fees	0.00	•
PRELIMINARY TESTING	•		
	Cummon of Preliminant Tenting	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing T	0.00	
	Government Financial Strategies, Inc.	252 12	Einanaial Consulting
	Government Financial Strategies, Inc.		Financial Consulting Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Government Financial Strategies, Inc.		Financial Consulting
	Signs of Success, Inc.		TUSD Signs
10/3/2018 36065693			General Counsel
12/12/2018 36079070			General Counsel
1/11/2019 36083537		•	General Counsel
1/11/2019 36083537			General Counsel
2/1/2019 36087357			General Counsel
3/6/2019 36093074			General Counsel
4/3/2019 36098588			General Counsel
5/15/2019 36106929			General Counsel
	3 Vavrinek Trine Day & Co. LLP		Bond Audit Report
	Summary of Other Planning Cost	18,957.77	
	TOTAL PLANNING	18,957.77	•
	TOTAL I LANGING	10,007.77	
CONSTRUCTION			
MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	•
OTHER CONSTRUCTION		0.00	
	Summary of Other Construction Costs	0.00	•
INSPECTION	·		
mor zonon			
	Summary of Inspection	0.00	
LABOR COMPLIANCE			
	Summary of Labor Compliance	0.00	
CONSTRUCTION TESTS			
			•
CUDNITUDE & COURSE	Summary of Construction Tests	0.00	
FURNITURE & EQUIPME	:N I		
	Summany of Surpiture & Equipment	0.00	•
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	•
TOTAL CURRENT UNALLO	OCATED COSTS	18,957.77	
		er in the state of the state of	

DETAILED LISTING OF PROJECT EXPENDITURES - BOND MEASURE O

TURLOCK UNIFIED SCH	OOL DISTRICT, STANISLAUS COUNTY		
Pitman High School - Mod	dernization		Report Number: 9
			Period Ending: 6/10/2019
PLANNING			
ARCHITECT/ENGINEE			
	90 California Design West Architects		Architectural/Engineering
	48 California Design West Architects 65 California Design West Architects		Architectural/Engineering
6/30/2018 FP1801	73 California Design West Architects		Architectural/Engineering Architectural/Engineering
	44 California Design West Architects		Architectural/Engineering
10/3/2018 3606563	33 California Design West Architects	23,222.38	Architectural/Engineering
10/24/2018 3606994	17 California Design West Architects	46,939.77	Architectural/Engineering
	33 California Design West Architects	18,048.80	Architectural/Engineering
	61 California Design West Architects 95 California Design West Architects		Architectural/Engineering
	95 California Design West Architects		Architectural/Engineering Architectural/Engineering
	7 California Design West Architects		Architectural/Engineering
4/19/2019 3610220	2 California Design West Architects		Architectural/Engineering
5/30/2019 3611010	09 California Design West Architects		Architectural/Engineering
	Summary of Architect/Engineering Fees	626,546.90	
DEPARTMENT OF GEN			
	3 Division of State Architect		Plan Review Fee
	8 Division of State Architect		Plan Review Fee
9/5/2018 3606022	2 Division of State Architect		Plan Review Fee
CALIFORNIA DEPARTM	Summary of Department of General Services Fees TENT OF EDUCATION FEES	42,300.00	
CALII GITTIA DEI AITTI	IENT OF EDUCATION FEES		
	Summary of California Danastment of Education Face	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
FRELIMINARI TESTINO	•		•
	Summary of Preliminary Testing	0.00	
OTHER PLANNING COS		0.00	•
6/30/2018	Previoulsy Unallocated Cost	4.942.80	Debt Report, Legal, Consulting
	Summary of Other Planning Cost	4,942.80	deposit Lagua, Comoditing
	TOTAL PLANNING	673,789.70	
		010,700.70	
CONSTRUCTION			
MAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION	NCOSTS Northstar Engineering Group, Inc.	4 404 50 5	
	Northstar Engineering Group, Inc. Northstar Engineering Group, Inc.		Fopographic Survey Fopographic Survey
5,55,25,6 E1 155176			ropograpnic Survey
INCRECTION	Summary of Other Construction Costs	11,045.00	
INSPECTION			
	Summary of Inspection	0.00	
LABOR COMPLIANCE			
	Summary of Labor Compliance	0.00	
CONSTRUCTION TESTS			
FURNITURE & EQUIPME	Summary of Construction Tests	0.00	
. Order one de Edorf ME			
	Summary of Furniture & Equipment	0.00	
		0.00	
	TOTAL CONSTRUCTION	11,045.00	
TOTAL DITMAN DICE MACE	EDNIZATIONI	C04 004 7C	
TOTAL PITMAN HIGH MOD	LINIVIZATION	684,834.70	

6/12/2019 11:14 AM

Pitman High School - Securit	y Camera System		Report Number: 9 Period Ending: 6/10/2019
			renod Ending, 0/10/2013
PLANNING ARCHITECT/ENGINEERIN	IG FEES		
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees RAL SERVICES FEES	0.00	
CALIFORNIA DEPARTME	Summary of Department of General Services Fees	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	0.00	
10/30/2018 36071028	Johnson Controls Security Solutions Johnson Controls Security Solutions Johnson Controls Security Solutions	52,580.52	Security Cameras Security Cameras Security Cameras
OTHER CONSTRUCTION	Summary of Main Construction COSTS	67,204.10	
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPME	Summary of Construction Tests	0.00	-
	Summary of Furniture & Equipment	0.00	-
	TOTAL CONSTRUCTION	87,264.16	-
TOTAL PITMAN SECURITY	CAMERA SYSTEM	87,264.16	- =

Pitman High School - Play	iidius (10)eet		Report Number: 9 Period Ending: 6/10/2019
PLANNING			
ARCHITECT/ENGINEER	RING FEES		
	Summary of Architect/Engineering Fees	0.00	5
DEPARTMENT OF GEN	ERAL SERVICES FEES		
CALIFORNIA DEPARTM	Summary of Department of General Services Fees IENT OF EDUCATION FEES	0.00	5
	Summary of California Department of Education Fees	0.00	_)
PRELIMINARY TESTING	3		
	Summary of Preliminary Testing	0.00	-
OTHER PLANNING COS	ST .		
	Summary of Other Planning Cost	0.00	ī
	TOTAL PLANNING	0.00	7
CONSTRUCTION			
MAIN CONSTRUCTION			
	CT Brayton & Sons, Inc.		November Lease Payment
11/9/2018	CT Brayton & Sons, Inc. CT Brayton & Sons, Inc.		Lease Deposit
	CT Brayton & Sons, Inc.		December Lease Payment January Lease Payment
	CT Brayton & Sons, Inc.		February Lease Payment
2/13/2019 36089231	CT Brayton & Sons, Inc.		March Lease Payment
	CT Brayton & Sons, Inc.		April Lease Payment
	CT Brayton & Sons, Inc.		May Lease Payment
3/20/2019 36096132			Playfield Artificial Turf
4/17/2019 36101673 5/30/2019 36110117			Playfield Artificial Turf Playfield Artificial Turf
	Summary of Main Construction	3,645,971.97	
OTHER CONSTRUCTION 10/19/2018 36069116		1,270.30	Notice to Contractors
	Summary of Other Construction Costs	1,270.30	
INSPECTION			
12/19/2018 36081139	United Inspection Inc.	3,712.00	Construction Inspections
3/8/2019 36093676	United Inspection Inc.		Construction Inspections
	United Inspection Inc.		Construction Inspections
	United Inspection Inc.		Construction Inspections
	United Inspection Inc. United Inspection Inc.		Construction Inspections Construction Inspections
	United Inspection Inc.		Construction Inspections
	Summary of Inspection	36,272.00	Construction inspections
LABOR COMPLIANCE			
	Summary of Labor Compliance	0,00	
CONSTRUCTION TESTS	·		
12/12/2018 36079068			Materials Testing
1/11/2019 36083535		•	Materials Testing
3/6/2019 36093071 3/6/2019 36093071			Materials Testing
3/20/2019 36096149			Materials Testing Materials Testing
4/17/2019 36101688			Materials Testing
5/30/2019 36110124			Materials Testing
	Summary of Construction Tests	16,552.00	
FURNITURE & EQUIPME	V. I		
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	3,700,066.27	
OTAL PITMAN HIGH PLAY	FIELDS	3,700,066.27	
		5,, 55,000,27	
· .			

6/12/2019 11:14 AM 5 of 13

Pitman High School - Fire Alar			Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERING	G FEES		
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	0.00	
CALIFORNIA DEPARTMEN	Summary of Department of General Services Fees	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COST	Surnmary of Preliminary Testing	0.00	
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	0.00	
CONSTRUCTION MAIN CONSTRUCTION			
2/27/2019 36091713	Johnson Controls Security Solutions Summary of Main Construction	243,263.57	Security Cameras
OTHER CONSTRUCTION (210,200.01	
INSPECTION	Summary of Other Construction Costs	0.00	-
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	-
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	-
	Summary of Furniture & Equipment	0.00	-
	TOTAL CONSTRUCTION	243,263.57	.
TOTAL PITMAN HIGH FIRE	ALARM	243,263.57	- -

6/12/2019 11:14 AM 6 of 13

Pitman High School - Fenci	ng and Office Modernization	Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERI	NG FEES	
DEPARTMENT OF GENE	Summary of Architect/Engineering Fees ERAL SERVICES FEES	0.00
CALIFORNIA DEPARTME	Summary of Department of General Services Fees ENT OF EDUCATION FEES	0.00
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00
OTHER PLANNING COST	Summary of Preliminary Testing	0.00
	Summary of Other Planning Cost TOTAL PLANNING	0.00
CONSTRUCTION MAIN CONSTRUCTION 4/10/2019 36100100 4/12/2019 5/8/2019 36105308	CT Brayton & Sons, Inc. CT Brayton & Sons, Inc. CT Brayton & Sons, Inc.	102,311.28 May Lease payment -0.50 Lease Deposit 102,311.28 June Lease Payment
OTHER CONSTRUCTION 4/3/2019 36098599	COSTS McClatchy Newspaper, Inc.	204,622.06 1,282.29 Notice to Contractors
INSPECTION	Summary of Other Construction Costs	1,282.29
LABOR COMPLIANCE	Summary of Inspection	0.00
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00
FURNITURE & EQUIPMEN	Summary of Construction Tests T	0.00
	Summary of Furniture & Equipment	0.00
	TOTAL CONSTRUCTION	205,904.35
OTAL PITMAN HIGH FENCI	NG AND OFFICE MODERNIZATION	205,904.35

6/12/2019 11:14 AM

7 of 13

Pitman High School - Culinary	DISTRICT, STANISLAUS COUNTY		Report Number: 9
Plunan High School - Culinary	Alb		Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERIN	G FEES		
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	0.00	
CALIFORNIA DEPARTME	Summary of Department of General Services Fees NT OF EDUCATION FEES	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost	0.00	
	TOTAL PLANNING	0.00	•
CONSTRUCTION MAIN CONSTRUCTION 4/10/2019 36100100 4/12/2019 5/8/2019 36105308	CT Brayton & Sons, Inc. CT Brayton & Sons, Inc. CT Brayton & Sons, Inc. Summary of Main Construction	-0.50	May Lease Payment Lease Deposit June Lease Payment
OTHER CONSTRUCTION	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	-
LABOR COMPLIANCE	Summary of Inspection	0.00	<u>-</u>
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	ī
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	Ī
	Summary of Furniture & Equipment	0.00	,
	TOTAL CONSTRUCTION	333,857.34	Ī
TOTAL PITMAN HIGH CULI	NARY ARTS	333,857.34	<u>-</u>

Turlock High School - Mode	ernization		Report Number: 9
			Period Ending: 6/10/2019
PLANNING	선택하다는 사람들이 되는 것으로		
ARCHITECT/ENGINEER	ING FEES		경상의 아이랑 아이 되었다.
9/1/2017 36977194		1.840.00	Architectural Services
9/13/2017 36978756			Architectural Services
10/11/2017 36984242	2 Darden Architects Inc.	460.00	Architectural Services
1/5/2018 36016301	Darden Architects Inc.	24,972.75	Architectural Services
2/2/2018 36021792		8,387.25	Architectural Services
6/8/2018 36046153			Architectural Services
6/30/2018 EP18092		•	Architectural Services
9/21/2018 36063669			Architectural Services
12/19/2018 36081022 12/19/2018 36081022			Architectural Services
1/16/2019 36084179			Architectural Services
3/8/2019 36093612		50,531.50	Architectural Services Architectural Services
4/5/2019 36099322			Architectural Services
4/26/2019 36103360			Architectural Services
4/26/2019 36103360			Architectural Services
5/17/2019 36107686			Architectural Services
5/17/2019 36107686			Architectural Services
	Summary of Architect/Engineering Fees	343,334.81	
DEPARTMENT OF GENE		343,334.61	
	Summary of Department of General Services Fees	0.00	
CALIFORNIA DEPARTME	ENT OF EDUCATION FEES		
	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING		0.00	
	Common of Desires, Tastina	- 0.00	
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
6/30/2018	Previoulsy Unallocated Cost	1 /03 76	Debt Report, Legal, Consulting
0,00,2010			Debt Report, Legal, Consulting
	Summary of Other Planning Cost	1,493.76	
	TOTAL PLANNING	344,828.57	
ONSTRUCTION MAIN CONSTRUCTION			
WAIN CONSTRUCTION			
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION			
9/21/2018 36063698	Northstar Engineering Group, Inc.		lipographic Survey
3/8/2019 36093654	Northstar Engineering Group, Inc.	2,032.80	Fopographic Survey
	Summary of Other Construction Costs	24,640.00	
INSPECTION			
	Summary of Inspection	0.00	
LABOR COMPLIANCE			
	Summary of Labor Compliance	0.00	
CONSTRUCTION TESTS			
FURNITURE & FOLURATION	Summary of Construction Tests	0.00	
FURNITURE & EQUIPMEN	II		
·	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	24,640.00	
OTAL TURLOCK HIGH MOI	DERNIZATION	369,468.57	

6/12/2019 11:14 AM 9 of 13

DETAILED LISTING OF PROJECT EXPENDITURES - BOND MEASURE O TURLOCK UNIFIED SCHOOL DISTRICT, STANISLAUS COUNTY Turlock High School - Science Building

TURLOCK UNIFIED SCHOO Turlock High School - Science	DL DISTRICT, STANISLAUS COUNTY	<u> </u>	Report Number: 9
Turlock Flight School - Scienc	e building		Period Ending: 6/10/2019
PLANNING	<u>일으로</u> 그는 그는 이용해졌다면서 있다.		이 그는 말으로 가지 않았습니?
ARCHITECT/ENGINEERIN		E0 07E 00	Applituational Complete
	Darden Architects Inc.		Architectural Services
	Darden Architects Inc.	•	Architectural Services
	Darden Architects Inc.	•	Architectural Services
	Darden Architects Inc.		Architectural Services Architectural Services
	Darden Architects Inc.	•	Architectural Services Architectural Services
	Darden Architects Inc.	•	Architectural Services
	Darden Architects Inc.		
5/17/2019 36107686	Darden Architects Inc.		Architectural Services
	Summary of Architect/Engineering Fees	740,250.00	
DEPARTMENT OF GENE	RAL SERVICES FEES		
2/15/2019 36090047	Division of State Architect		Plan Review Fee
2/27/2019 36091701	Division of State Architect	500.00	Plan Review Fee
	Summary of Department of General Services Fees	152,450.00	
CALIFORNIA DEPARTME	NT OF EDUCATION FEES		
			-
	Summary of California Department of Education Fees	0.00	
PRELIMINARY TESTING			
		0.00	-
OTHER PLANNING COST	Summary of Preliminary Testing	0.00	
6/30/2018	Previoulsy Unallocated Cost	2,103.23	Debt Report, Legal, Consulting
0.00.20.0	Summary of Other Planning Cost	2,103.23	
		894,803.23	_
	TOTAL PLANNING	094,003.23	
CONSTRUCTION			
MAIN CONSTRUCTION			
		0.00	-
	Summary of Main Construction	0.00	•
OTHER CONSTRUCTION		2 000 00	Caalasia Chada
	Department of Conservation		Geologic Study Geotechnical Services
5/30/2019 36110113	CTE CAL Inc.		-
	Summary of Other Construction Costs	11,800.00	1
INSPECTION			
	Summary of Inspection	0.00	_)
	Saminary of mepotition		
LABOR COMPLIANCE			
			_
	Summary of Labor Compliance	0.00)
CONSTRUCTION TESTS			
			_
	Summary of Construction Tests	0.00)
FURNITURE & EQUIPME	NT		
		0.00	.
	Summary of Furniture & Equipment	0.00	,
	TOTAL CONSTRUCTION	11,800.00	,
TOTAL TURLOCK HIGH SO	CIENCE BUILDING	906,603.23	3
TOTAL TOTALOGIC HIGH OF			=

DETAILED LISTING OF PROJECT EXPENDITURES - BOND MEASURE O TURLOCK UNIFIED SCHOOL DISTRICT, STANISLAUS COUNTY Turlock High School - Roofing Buildings B & L

Turlock High School - Roc	fing Buildings B & L		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEEI	RING FEES		
	Summary of Architect/Engineering Fees IERAL SERVICES FEES 8 Division of State Architect	0.00	
	Summary of Department of General Services Fees ## Summary OF EDUCATION FEES	23,600.00	Plan Review Fee
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COS	Summary of Preliminary Testing	0.00	
	Summary of Other Planning Cost TOTAL PLANNING	0.00	
CONSTRUCTION MAIN CONSTRUCTION			
OTHER CONSTRUCTION	Summary of Main Construction COSTS	0.00	
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	
FURNITURE & EQUIPME	Summary of Construction Tests	0.00	
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
TOTAL TURLOCK HIGH RO	OFING BUILDINGS B & L	23,600.00	

11 of 13


6/12/2019 11:14 AM


eCademy Charter at Crane Sc	nool - Fencing	Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEERING	3 FEES	
10/24/2018 36070007	SKW & Associates	1,386.00 Architecture/Engineering
DEPARTMENT OF GENER	Summary of Architect/Engineering Fees AL SERVICES FEES	1,386.00
CALIFORNIA DEPARTMEN	Summary of Department of General Services Fees	0.00
	Summary of California Department of Education Fees	0.00
PRELIMINARY TESTING		
OTHER PLANNING COST	Summary of Preliminary Testing	0.00
	Summary of Other Planning Cost	0.00
	TOTAL PLANNING	1,386.00
CONSTRUCTION MAIN CONSTRUCTION		
	Summary of Main Construction	0.00
OTHER CONSTRUCTION		
INSPECTION	Summary of Other Construction Costs	0.00
LABOR COMPLIANCE	Summary of Inspection	0.00
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00
FURNITURE & EQUIPMEI	Summary of Construction Tests	0.00
	Summary of Furniture & Equipment	0.00
	TOTAL CONSTRUCTION	0.00
TOTAL ECADEMY CHARTE		1,386.00

Roselawn High School - Fe	encing		Report Number: 9 Period Ending: 6/10/2019
PLANNING ARCHITECT/ENGINEER 10/24/2018 3607000		1.760.00	Architecture/Engineering
DEPARTMENT OF GEN	Summary of Architect/Engineering Fees ERAL SERVICES FEES	1,760.00	
CALIFORNIA DEPARTM	Summary of Department of General Services Fees	0.00	
PRELIMINARY TESTING	Summary of California Department of Education Fees	0.00	
OTHER PLANNING COS	Summary of Preliminary Testing T	0.00	
	Summary of Other Planning Cost	0.00	
CONSTRUCTION MAIN CONSTRUCTION	TOTAL PLANNING	1,760.00	
	Summary of Main Construction	0.00	
OTHER CONSTRUCTION	COSTS		
INSPECTION	Summary of Other Construction Costs	0.00	
LABOR COMPLIANCE	Summary of Inspection	0.00	
CONSTRUCTION TESTS	Summary of Labor Compliance	0.00	·
FURNITURE & EQUIPMEN	Summary of Construction Tests	0.00	
	Summary of Furniture & Equipment	0.00	
	TOTAL CONSTRUCTION	0.00	
OTAL ROSELAWN HIGH FE	ENCING	1,760.00	
	·		


Trock United School District

Measures N & O Series 2019 General Obligation Bond Sale Results





Learning Today... Leading Tomorrow



Government Financial Strategies

Presented by Rich Malone May 21, 2019

Tonight's Agenca

- Competitive Bid Process
- Results for the District and District's Taxpayers
- Next Steps



Several GFOA Best Practices Utilized

The District has been an avid user of Government bonds, including: several of them were utilized in this year's issuance of Finance Officers Association (GFOA) best practices,



- Use of Independent Financial Advisor
- Competitive Process to Select Underwriter
- Managed the Cost of Debt Issuance
- Implementing and Using a Debt Management Policy
- Using Credit Rating Agencies
- Call Features Incorporated into the New Issuance*

to allow for more efficient and cost-effective refinancing opportunities in the future * Incorporating call features into the new issuance included aligning the call dates on the 2019 bonds to be the same as the 2017 bonds,



Turlock Unified School District - Page 3

Refresher on Strategies Initiated in 2017

(as presented to the Board on May 2, 2017)

Considerations Prior to Sale

- Credit Rating Strategy:
- Recent changes to Moody's rating criteria indicated a likely "Aa3" rating (one step above S&P's expected rating).
- Expected cost of Moody's rating was \$5k more.
- Higher rating expected to save us \$250k.
- Therefore, we decided to pursue a credit rating from Moody's.
 Risk Management Strategy:
- ▶ Interest rates were rising and we assumed that we'll continue to face rising interest rates as a matter of risk management . . .
- It's better to issue the first series with a longer term, and then if interest rates allow, shorten the terms of the later bond series, to reduce overall interest costs.
- Therefore, we decided that the first series be issued with a 29 year term, and subsequent series be issued with 29 year terms or less.

urlock Unified School District- Page 3

Post-Election and Pre-Sale Terms of Bonds

2016 2017 2018 2018 2020 2021 2022 2023 2024 2025 2026 2027 2026 2027 2028 2029 2029 2029	Sining 2021	Senis 2019	Briss 2017 Et Sept com	Series 2021	Series 2019	Series 2017
	2 Market and Control of the Control		CONTROL OF THE PROPERTY OF THE	27 year term	29 year term	29 year term


Credit Rating Process

rianglest In preparation for the sale of bonds, the bonds were evaluated for a credit rating by one of the main credit rating agencies*:


MOODY'S INVESTORS SERVICE

- Moody's <u>maintained</u> rating of "Aa3" for both District-wide and SFID bonds.
- The following reasons were cited:
- Well sized and expanding tax base
- Solid financial position
- Moderate debt and retirement costs
- Unlimited tax pledge



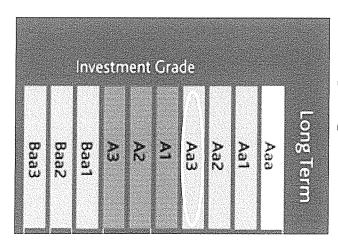

Panning Assumed Rising Interest Rates

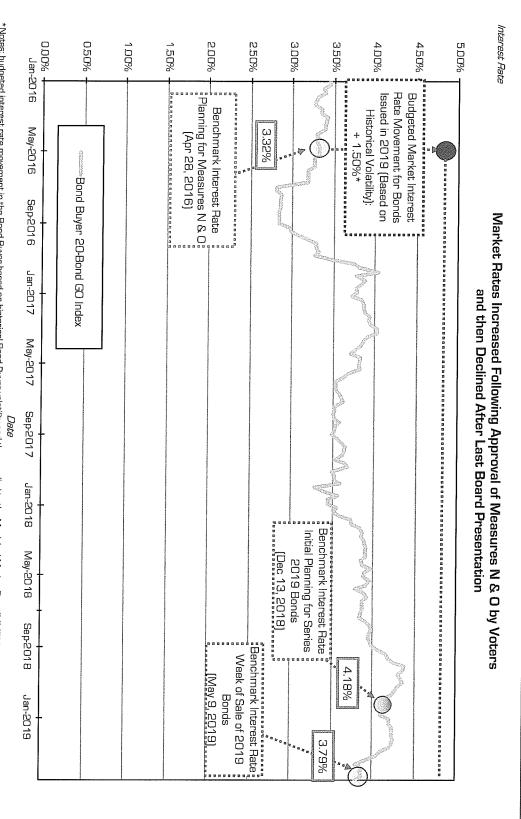

^{*}Notes: budgeted interest rate movement in the Bond Buyer based on historical Bond Buyer volatility and then applied to the Municipal Market Data (MMD) interest rate scale. The Bond Buyer 20-Bond Index consists of 20 general obligation bonds that mature in 20 years and is compiled every Thursday. The average rating of the 20 bonds is roughly equivalent to Moody's investors Service's Aa2 rating and Standard & Poor's Rating Service AA.

Codates Since February 5 Board Presentation

- Interest rates are higher than than they were, but not higher than
- As interest rates fell below the assumed level, bond financial implemented prior to the sale of the Series 2017 bonds issued" bonds consistent with the risk management strategy plan was adjusted to shorten the duration of the "to be
- Originally, intention was to sell Measure O bonds on May 7 and Measure N bonds on May 8
- ▶ Shortly before the week of May 6, it was discovered that Los approximately \$630 million of bonds on May 7 Angeles Unified School District was planning to sell
- Measure O bonds sale date was moved to May 8 to avoid having potential bidders distracted

Updated Ierm of Bonds

Measure O (HS)


While Interest Rates have Increased, Greater Than Assumed AV Growth has Permitted a Reduction of Issuances & Shortening of Overall Term

Updated Plan

Series 2021 Series 2019 Series 2017 Original Plan Series 2021 Series 2019 Series 2017 25 year term Fiscal Year Beg July 1 25 year term 29 year term 27 year term 28 year term


Measure N (SFID)

While Interest Rates have Increased, Our Timing Adjustments have Decreased, Enabling a Changing of the Structure & Shortening of Term

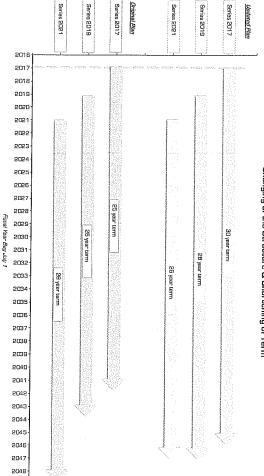

Competitive Bio Process


- The competitive bid process was held on May 8, 2019.
- Bidding on Measure O concluded at 8:05 a.m.
- Bidding on Measure N concluded at 9:05 a.m.



Comp

- Internet bidding platform:
- Used to notify potential bidders and to accept bids
- Also posted in The Bond Buyer industry newspaper.
- Any bank or underwriter was allowed to bid.
- Bidding allowed within flexible parameters
- More competition > better results for the District

Bioding Came Trom Across The U.S.

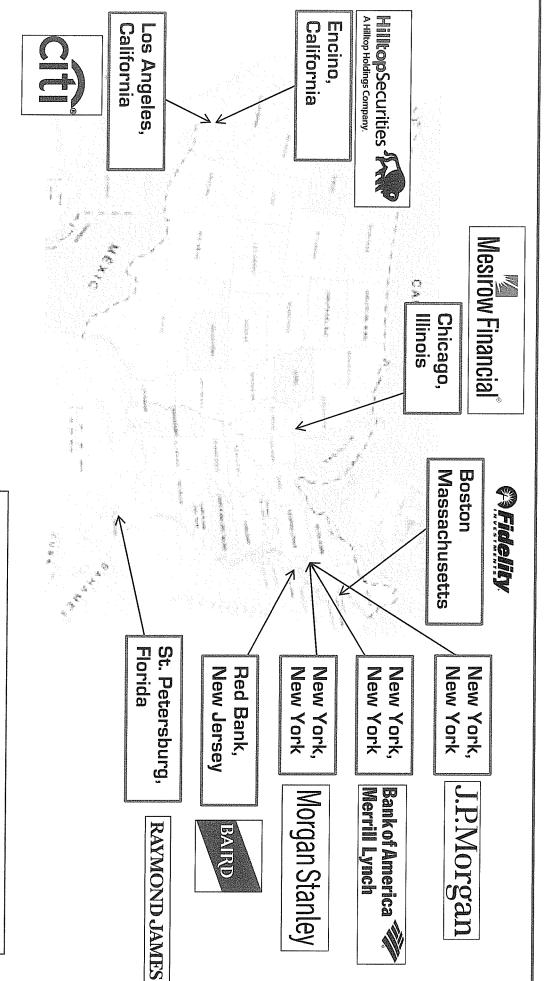


Note: location represents location of the office from where the bid was submitted.


0

U.O. Results

Measure O (HS)

Measure N (SFID)

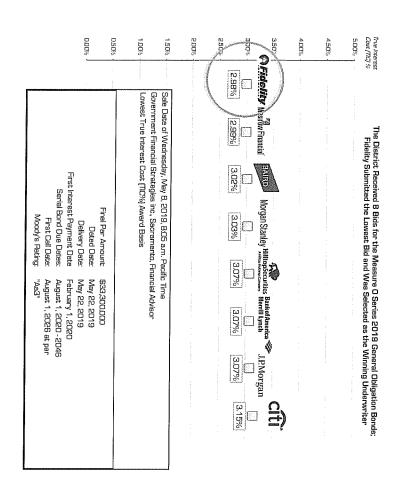

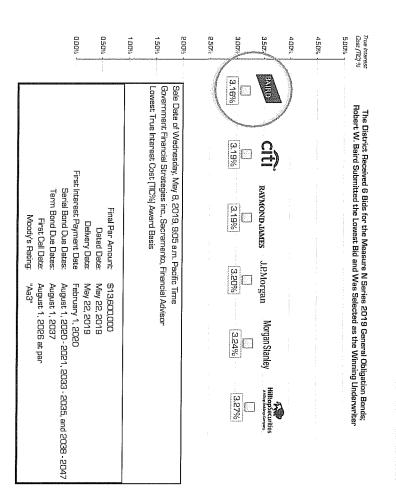


Note: in 2017, the District received 8 bids for Measure 0 bonds, with Raymond James submitting the winning bid of 3.67%, and Fidelity did not submit a bid.

Note: in <u>2017</u>, the District received 8 bids for Measure N bonds, with Bank of America submitting the winning bid of 3.70%, and Robert W. Baird submitted the fourth place bid.

Dolar Difference in Bios

Measure O (HS)

Measure N (SFID)

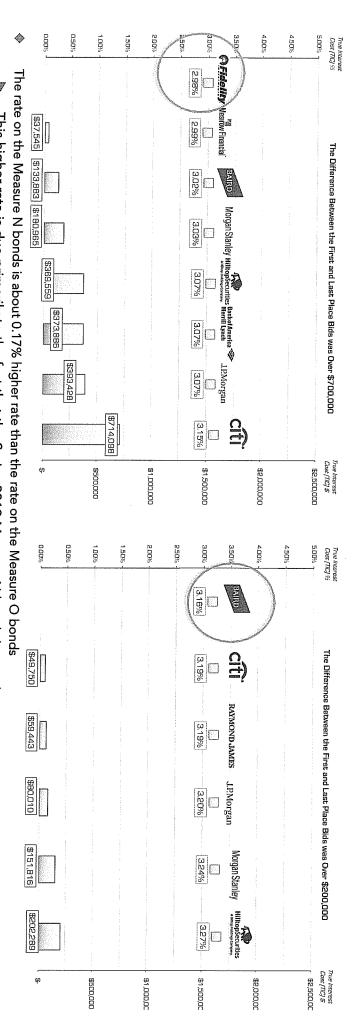

- This higher rate is due primarily to the fact that the Series 2019 Measure N bonds have a longer average life (20.1 years) than the Series 2019 Measure O bonds (17.4 years), as we need to leave room to optimize the structure of the planned third series of Measure N bonds
- lower than the winning bid on the Measure O bonds, most likely reflecting a desire by Baird to beat the Measure O winning bid Interestingly, rates on the long end of the winning bid for the Measure N bonds (which were bid after the Measure O bonds) were actually 1 - 2 basis points
- Baird was the third place bidder on the Series 2019 Measure O bonds, approximately 0.03% higher than the Measure O winning bid from Fidelity
- higher than Baird's bid While Fidelity did not bid on the Measure N bonds, their partner, Raymond James, did bid on the Measure N bonds and finished in third place about 0.03%

Vore Tunos Tor Tacilies

Measure O


	Interest & Sinking Fund	Market	Underwriter's Discount	Cost o	GO Bor	
Building Fund	nking Fund	Market Premium	s Discount	Cost of Issuance	GD Bonds Issued	<u>Buc</u>
\$32,425,000	(\$145,000)	\$0	(\$580,000)	(\$150,000)	\$33,300,000	Budgeted Amount
\$33,190,000	(\$1,053,141)	\$1,277,755	(\$224,614)	(\$110,000)	\$33,300,000	Actual Amount
\$765,000	(\$908,141)	\$1,277,755	\$355,386	\$40,000	\$	Change

Measure N

	Budgeted Amount	Actual Amount	Change
GO Bonds Issued	\$13,600,000	\$13,600,000	S
Cost of Issuance	(\$150,000)	(\$103,000)	\$47,000
Underwriter's Discount	(\$240,000)	(\$138,370)	\$101,630
Market Premium	\$0	\$157,937	\$157,937
Interest & Sinking Fund	(\$145,000)	(\$19,567)	\$125,433
Building Fund	\$13,065,000	\$13,497,000	\$432,000

Notes: budgeted figures from Board information presentation dated February 5, 2019. Cost of issuance includes financial advisor, legal counsel, credit rating agency, and other misc. expenses. Market premium (original issue premium) is the premium that investors are willing to pay above the face value of the bonds. State law requires that market premium be deposited into the Interest & Sinking Fund, and used for Bond debt service, to the benefit of taxpayers.


Veasure O Projected and End Inree Years LOVIOS IX S24

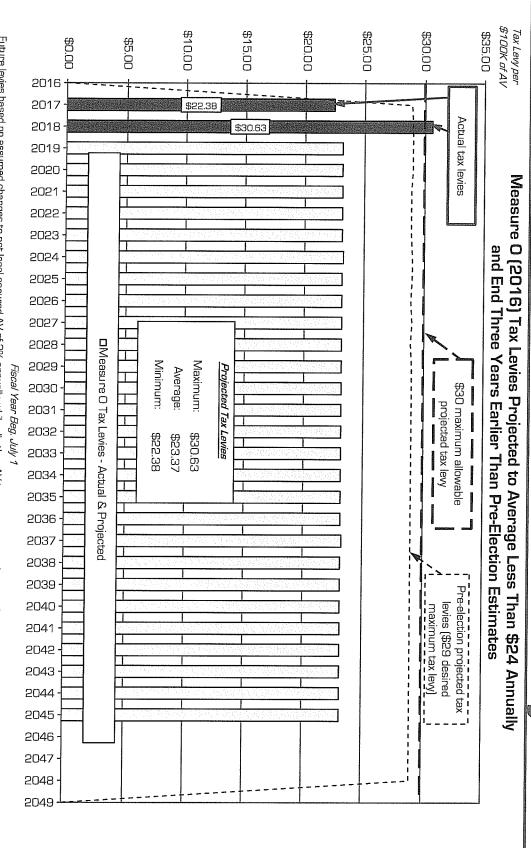

Future levies based on assumed changes to net local secured AV of 3% annually, while all other AV types are assumed to remain unchanged.

0.65

Measure N Projected Tax Levies < \$25 End Two Years

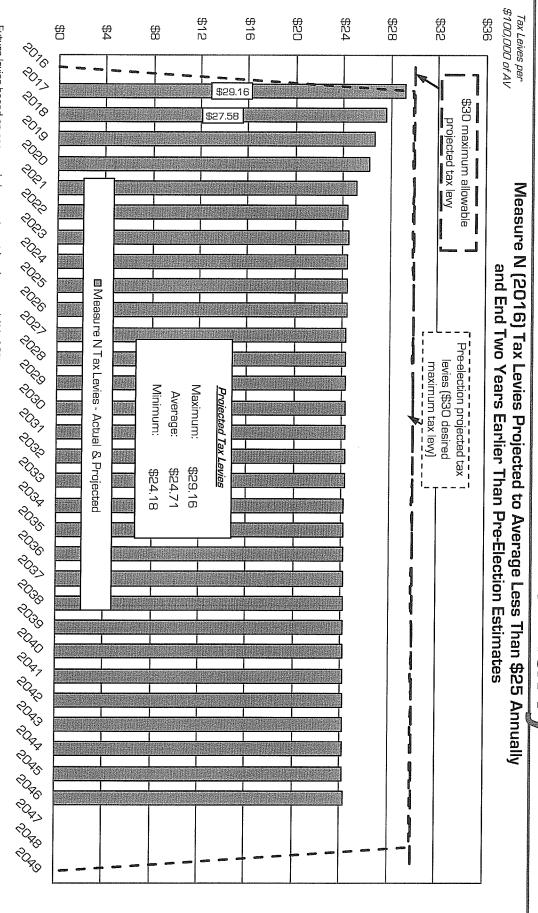


Future levies based on assumed changes to net local secured AV of 3% annually, while all other AV types are assumed to remain unchanged.

Ó

Conclusion

√ More bonds issued more quickly




 \checkmark Lower taxes and for fewer years



√ More funds for facilities





Next Steps

Congratulations!



- Bond funds will be deposited tomorrow (May 22nd) and available to spend toward facilities.
- Planning for final sale of Measure N bonds in two years (2021).
- Questions?



Detailed Costs of Issuance

Measure O (HS)

General Obligation Bonds, Election of 2016, Series 2019 (Stanislaus County and Merced County, California) TURLOCK UNIFIED SCHOOL DISTRICT

Parker & Covert LLP, Bond C.

Total Costs

Costs of Issuance

\$58,750.00	 Government Financial Strategies inc., Financial Advisor
\$1,500.00	Professional Services: Dut-of-Pocket Expenses:
\$15,000.0D \$800.0D	Bond Counsel Fees: Out-of-Pocket Expenses:

\$29,000.00

Amtec, Verification Agent	California Municipal Statistics, Research:	lpreo, Electronic Bidding:	Annual Administration Expenses:	Annual Administration Fee;	One Time Costs of Issuance Custodian Fee:	Acceptance Fee/Expenses:	Zions Bancorporation, National Association, Paying Agent
\$250.00	\$1,375.00	\$1,450.00	\$0.00	\$350.00	\$250.00	\$350.00	

\$110,000.00

\$925.00

TOTAL COSTS OF ISSUANCE

Other/Contingency

Measure N (SFID)

SCHOOL FACILITIES IMPROVEMENT DISTRICT NO. 1 General Obligation Bonds, Election of 2016, Series 2019 (Stanislaus County and Merced County, California) TURLOCK UNIFIED SCHOOL DISTRICT

Costs of Issuance

Total Costs	Description

\$15,000.00 \$800.00

Out-of-Packet Expenses:	Professional Services:	 Government Financial Strategies inc., Financial Advisor

id below)	•Other Issuance Expenses (break out listed below) Zions Paroconnoration, Matinnal Association Paving Apart
у	 Moody's Investors Service, Rating Agency Professional Services:
	Out-ofPacket Expenses:
	Professional Services:

TOTAL COSTS OF ISSUANCE \$103,000.00	TOTAL COS
Other/Contingency \$875.00	Other/
Amtec, Verification Agent \$250.00	Amtec,
California Municipal Statistics, Research: \$1,425.00	Californ
preo, Electronic Bidding: \$1,450.00	lpreo, E
Annual Administration Expenses:	Алп
Annual Administration Fee: \$350,00	Ann
One Time Costs of Issuance Custodian Fee:	One
Acceptance Fee/Expenses: \$350.00	Acc
Zions Bancorporation, National Association, Paying Agent	Zions E

Measures N & O Citizens' Oversight Committees Annual Report to the Public¹ June 20, 2019

Measure N

As approved by voters on November 8, 2016:

"To upgrade and repair elementary schools with local funding that cannot be taken by the State, shall Turlock Unified School District provide new classrooms/instructional technology, including necessary infrastructure, for core academics including math, science, reading/writing; modernize classrooms to meet health/safety codes; improve campus safety/security; repair, construct, acquire, equip, classrooms, sites, facilities; by issuing \$40,800,000 of bonds at legal rates, with independent citizen oversight, no money for administrators, and all funds used for Turlock Schools?"

The complete bond project list is in Exhibit A to the Board of Trustees' Resolution Number 30-2015-16.

Measure O

As approved by voters on November 8, 2016:

"To upgrade and repair high schools with local funding that cannot be taken by the State, shall Turlock Unified School District provide science, technology/engineering labs; provide new classrooms/instructional technology, including necessary infrastructure, for core academics; modernize facilities to meet health/safety codes; improve campus safety/security; repair, construct, acquire, equip, classrooms, sites, facilities; by issuing \$48,000,000 of bonds at legal rates, with independent citizen oversight, no money for administrators, and all funds used for Turlock Schools?"

The complete bond project list is in Exhibit A to the Board of Trustees' Resolution Number 31-2015-16.

¹ The Committees were assisted by Mike Trainor, Assistant Superintendent Business Services, Martell Taylor, Facilities Planner and Safety Director, and Bridget Shelton, Facilities Secretary, and District Financial Advisor Government Financial Strategies.

Citizens' Oversight Committee Members

Name	Measure N	Measure O	Member Representation		
Bettencourt, Patrick	Yes	Yes	PTA and parent of child enrolled in District		
Carlson, Harry	Yes	Yes	Active in senior citizens' organization		
Elliott, Lacy	Yes	Yes	PTA and parent of child enrolled in District		
Folly, David	Yes	Yes	PTA and parent of child enrolled in District		
Soderstrom, Steve	No	Yes	Active member in the District business community, & parent of a child enrolled in the District		
Tribble, Bryan	Yes	Yes	Active member in the District business community		

Meetings/Tours

Date	Topic(s)	Materials Reviewed	Location
Sep 21, 2017	Update on projects Scheduling	Expenditure reports	District Office
Dec 14, 2017	Update on projects	Expenditure reports	District Office
Mar 15, 2018	Organization Update on projects CDIAC reporting Financial and performance audits	Expenditure reports CDIAC annual report Financial and performance audits	District Office
Jun 21, 2018	Update on projects Committee organization FY 2016-17 annual report	Expenditure reports Committee organization from GFSi	District Office
Sep 13, 2018	Update on projects Committee organization	Expenditure reports	District Office
Jan 3, 2019	Tour "B" building View camera system Update on projects Update on future bond sales	Expenditure reports Bond plan and schedule	Pitman High School Library
Mar 21, 2019	Tour of Pitman HS projects Update on bond sale Financial and performance audits	Expenditure reports Financial and performance audits	Pitman High School Library
Jun 20, 2019	Update on projects Bond sale information Develop 2019-20 work plan Develop and approve 2017-18 annual report	Expenditure reports Bond sale presentation as given to the Board on May 21, 2019	District Office

Citizens' Oversight Committee Web Site

The Citizens' Oversight Committee web page includes meeting notices, agenda, minutes, and materials reviewed. This web page can be found at: http://turlockusd-ca.schoolloop.com/measurenando

Conclusion

Based on the financial and performance audits, and other material shared and reviewed during past meetings, the Committees have concluded that expenditures have only been "for the construction, reconstruction, rehabilitation, or replacement of school facilities, including the furnishing and equipping of school facilities, or the acquisition or lease of real property for school facilities" and that no funds were used for any "teacher and administrator salaries and other school operating expenses", and in accord with Measures N & O.

Measures N & O

Citizens' Oversight Committees

Annual Work Plan for Fiscal Year 2019-20

June 20, 2019

Measure N

As approved by voters on November 8, 2016:

"To upgrade and repair elementary schools with local funding that cannot be taken by the State, shall Turlock Unified School District provide new classrooms/instructional technology, including necessary infrastructure, for core academics including math, science, reading/writing; modernize classrooms to meet health/safety codes; improve campus safety/security; repair, construct, acquire, equip, classrooms, sites, facilities; by issuing \$40,800,000 of bonds at legal rates, with independent citizen oversight, no money for administrators, and all funds used for Turlock Schools?"

The complete bond project list is in Exhibit A to the Board of Trustees' Resolution Number 30-2015-16.

Measure O

As approved by voters on November 8, 2016:

"To upgrade and repair high schools with local funding that cannot be taken by the State, shall Turlock Unified School District provide science, technology/engineering labs; provide new classrooms/instructional technology, including necessary infrastructure, for core academics; modernize facilities to meet health/safety codes; improve campus safety/security; repair, construct, acquire, equip, classrooms, sites, facilities; by issuing \$48,000,000 of bonds at legal rates, with independent citizen oversight, no money for administrators, and all funds used for Turlock Schools?"

The complete bond project list is in Exhibit A to the Board of Trustees' Resolution Number 31-2015-16.

Measures N & O Citizens' Oversight Committee Members

Name	Measure N	Measure O	Member Representation		
Bettencourt, Patrick	Yes	Yes	PTA and parent of child enrolled in District		
Carlson, Harry	Yes	Yes	Active in senior citizens' organization		
Elliott, Lacy	Yes	Yes	PTA and parent of child enrolled in District		
Folly, David	Yes	Yes	PTA and parent of child enrolled in District		
Soderstrom, Steve	No	Yes	Active member in the District business community, & parent of a child enrolled in the District		
Tribble, Bryan	Yes	Yes	Active member in the District business community		

Meetings/Tours


<u>Date</u>	Topic(s)	Materials Reviewed	<u>Location</u>
Thursday, June 20, 2019 5:30 p.m.	Update on projects Bond sale information Develop 2019-20 work plan Develop and approve 2017-18 annual report	2018-19 Expenditure reports Bond sale presentation as given to the Board on May 21, 2019	District Office
Thursday, September 5, 2019 5:30 p.m.	Update on projects	Expenditure reports	Dutcher Middle School H6
Thursday, December 12, 2019 5:30 p.m.	Update on projects	Expenditure reports	District Office
Thursday, March 19, 2020 5:30 p.m.	Financial and performance audits Update on projects	Financial and performance audits Expenditure reports	District Office
Thursday, June 18, 2020 5:30 p.m.	Expenditure reports, status of projects, organization, FY 2018-19 annual report	Expenditure reports, annual report	District Office

^{*}Meeting dates and locations are subject to change, as approved by a majority of members of the Overisght Committees.

Citizens' Oversight Committees Web Site

The Citizens' Oversight Committee web page includes meeting notices, agenda, minutes, and materials reviewed. This web page can be found at: http://turlockusd-ca.schoolloop.com/measurenando

All activities of the Citizens' Oversight Committees will be in accordance with the Strict Accountability in Local School Construction Bonds Act of 2000, and the adopted by-laws (available on the Citizens' Oversight Committee Web Site).



BOND MEASURES N & O CITIZENS' OVERSIGHT COMMITTEES 2018-2019 MEETING SCHEDULE

DATE	TIME	LOCATION		
3/15/2018	5:30pm - 6:30pm	DO102		
6/21/2018	5:30pm - 6:30pm	DO102		
9/13/2018	5:30pm - 6:30pm	DO102		
1/3/2019	5:30pm - 6:30pm	PHS		
3/21/2019	5:30pm - 6:30pm	PHS		
6/20/2019	5:30pm - 6:30pm	DO102		
9/5/2019	5:30pm - 6:30pm	Dutcher H6		
12/12/2019	5:30pm - 6:30pm	DO102		

		• .
		<i>,</i>
		· ·
