

# Douglas MacArthur Modernization *Project Update*

Virtual Community Meeting  
Office of Capital Programs, Planning, and Design  
June 13, 2023



Interpretation

ES

PARA ESPAÑOL,  
SELECCIONE “Español”

AM

ለአማርኛ “Amharic”  
የሚለው ይምረጡ

AR

لسماع الترجمة باللغة  
العربية، اختر “Arabic”



# Agenda

- Construction Progress
- Transition Planning
- Next Steps and Communications
- Q & A





# New Douglas MacArthur Elementary School

## Facility Highlights:

- Grade Levels: Pre-K - 5
- Building Capacity: 840 Students
- Building SF: 154,221 SF
- Classrooms: 35 K -5 classrooms, 2 art rooms, 2 music rooms, 1 multi-purpose room
- Cafeteria with stage, Full-size gymnasium
- Parking Spaces: 84 Underground and 11 Surface
- Sustainability and Energy Efficiency Goals: LEED Gold and Net Zero Energy (ACPS first building with NZE goal)
- RPCA office and Outdoor Bathrooms: RPCA programs and community use after school hours



# Construction Progress





# Construction Progress Photos







# Construction Progress Photos







# Construction Progress Photos







# Construction Progress Photos









# Construction Progress Photos







# Construction Progress Photos

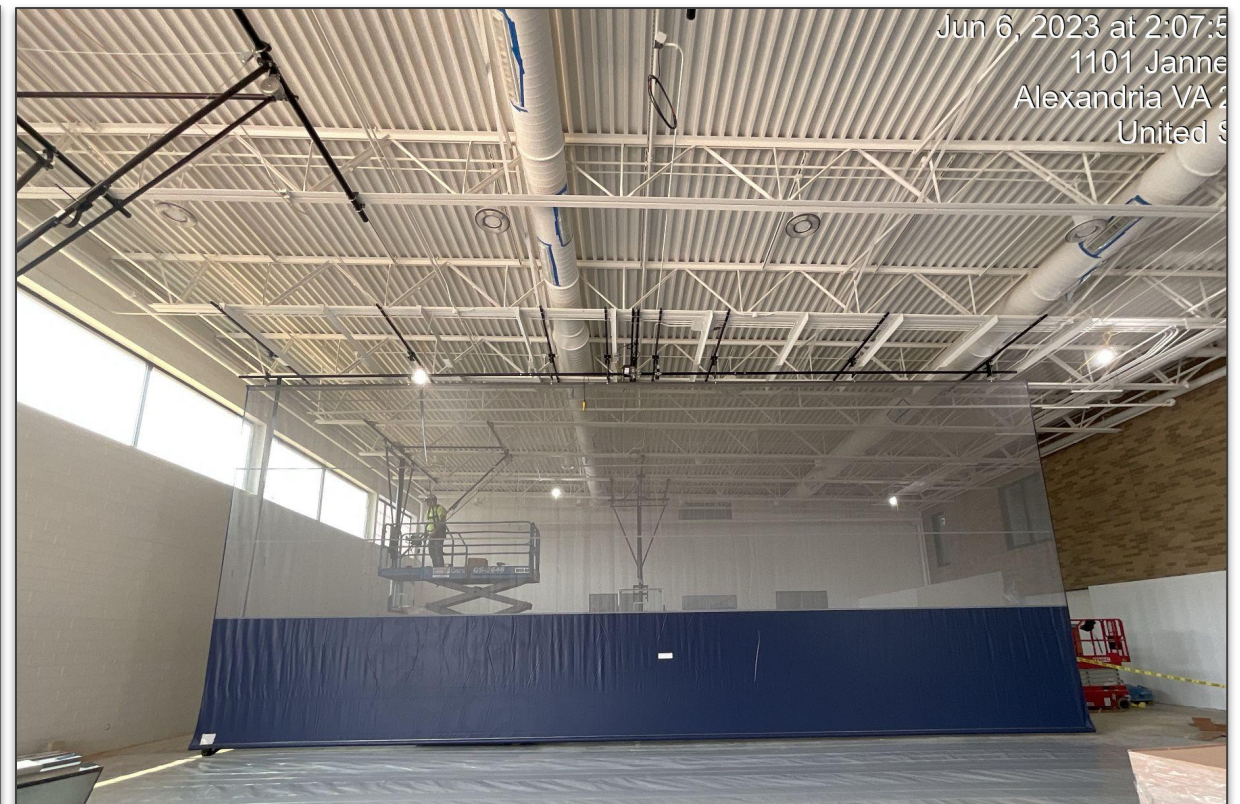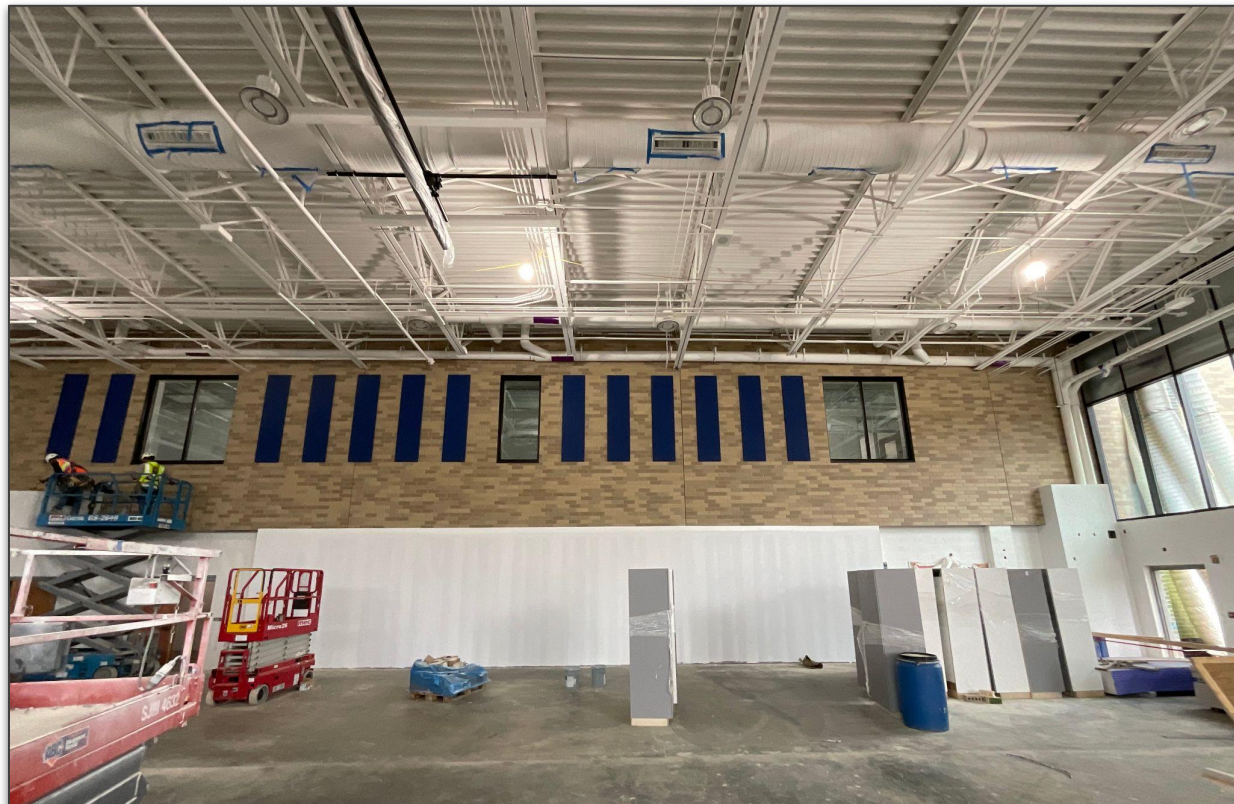





# Construction Progress Photos







# Construction Progress Photos





# Construction Progress Photos







# Construction Progress Photos







# Construction Progress Photos








# Construction Progress Photos







# Detailed Project Timeline to Finish

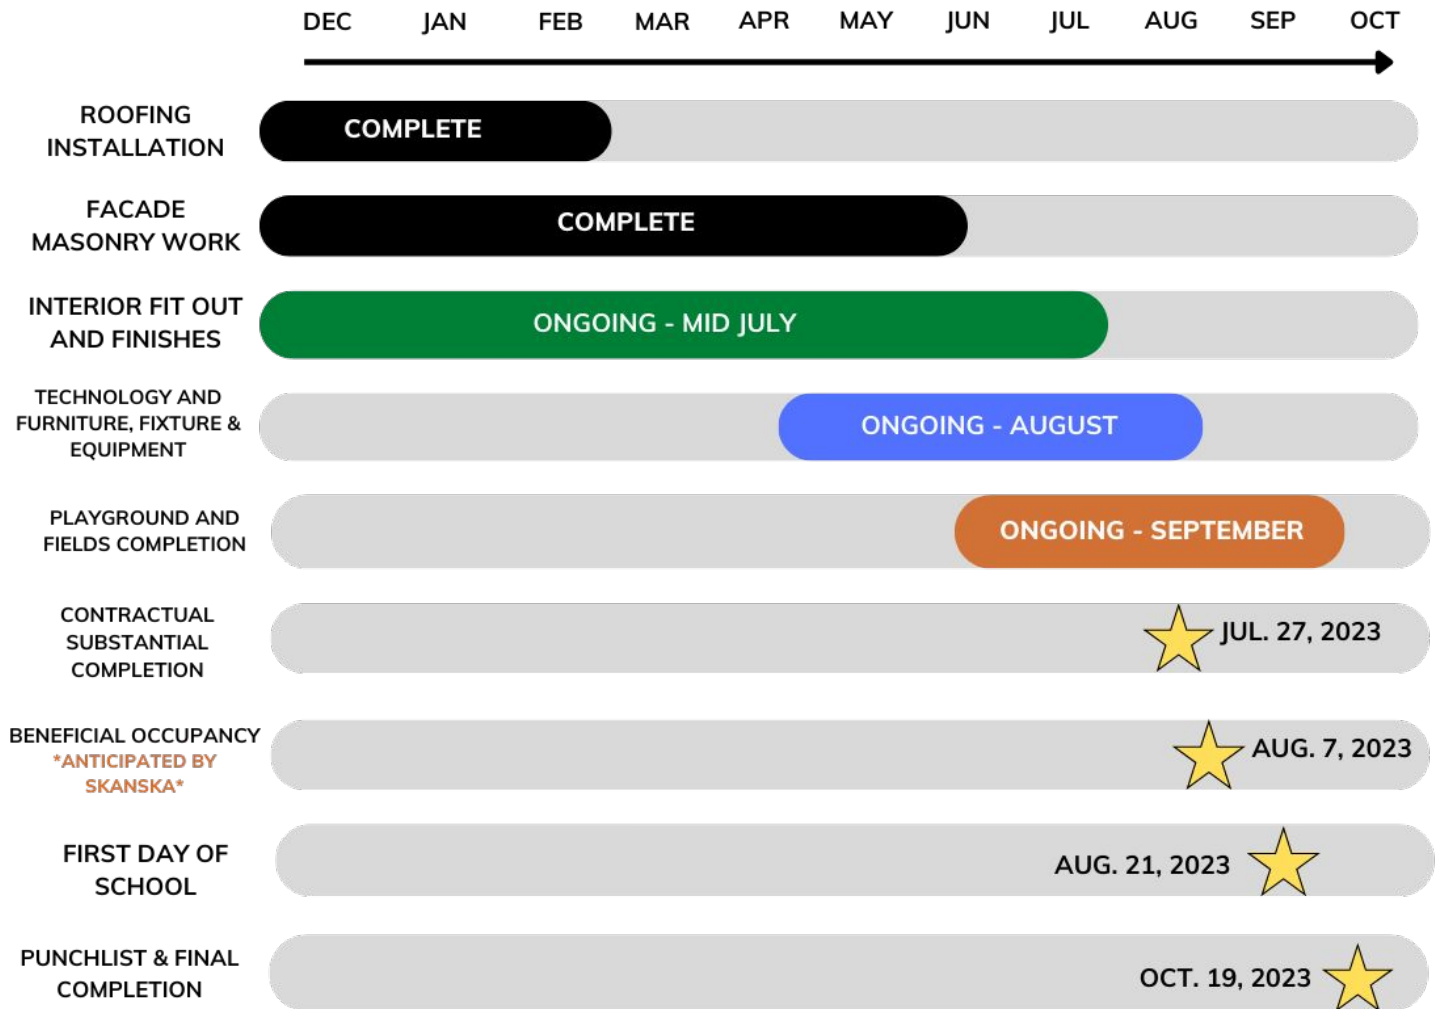



# Critical Activities

|  |                  |
|--|------------------|
| • Permanent Power  | • June 30, 2023  |
| • Exterior Paving  | • July 05, 2023  |
| • Building Facade/<br>Enclosure                          | • July 07, 2023  |
| • Functional Sprinkler<br>System - Stocking Permit       | • July 13, 2023  |
| • Interior Finishes                                      | • July 19, 2023  |
| • Life Safety Systems - Temp<br>Certificate of Occupancy | • August 7, 2023 |




# Delayed Activities

|    |                      |                      |
|----|----------------------|----------------------|
| 01 | Playground           | • August 19, 2023    |
| 02 | Synthetic Turf Field | • September 25, 2023 |
| 03 | Solar PV Array       | • Early 2024         |



# Transition Timeline

\*Despite Skanska’s anticipated delay, the following occupancy schedule is still being pursued:

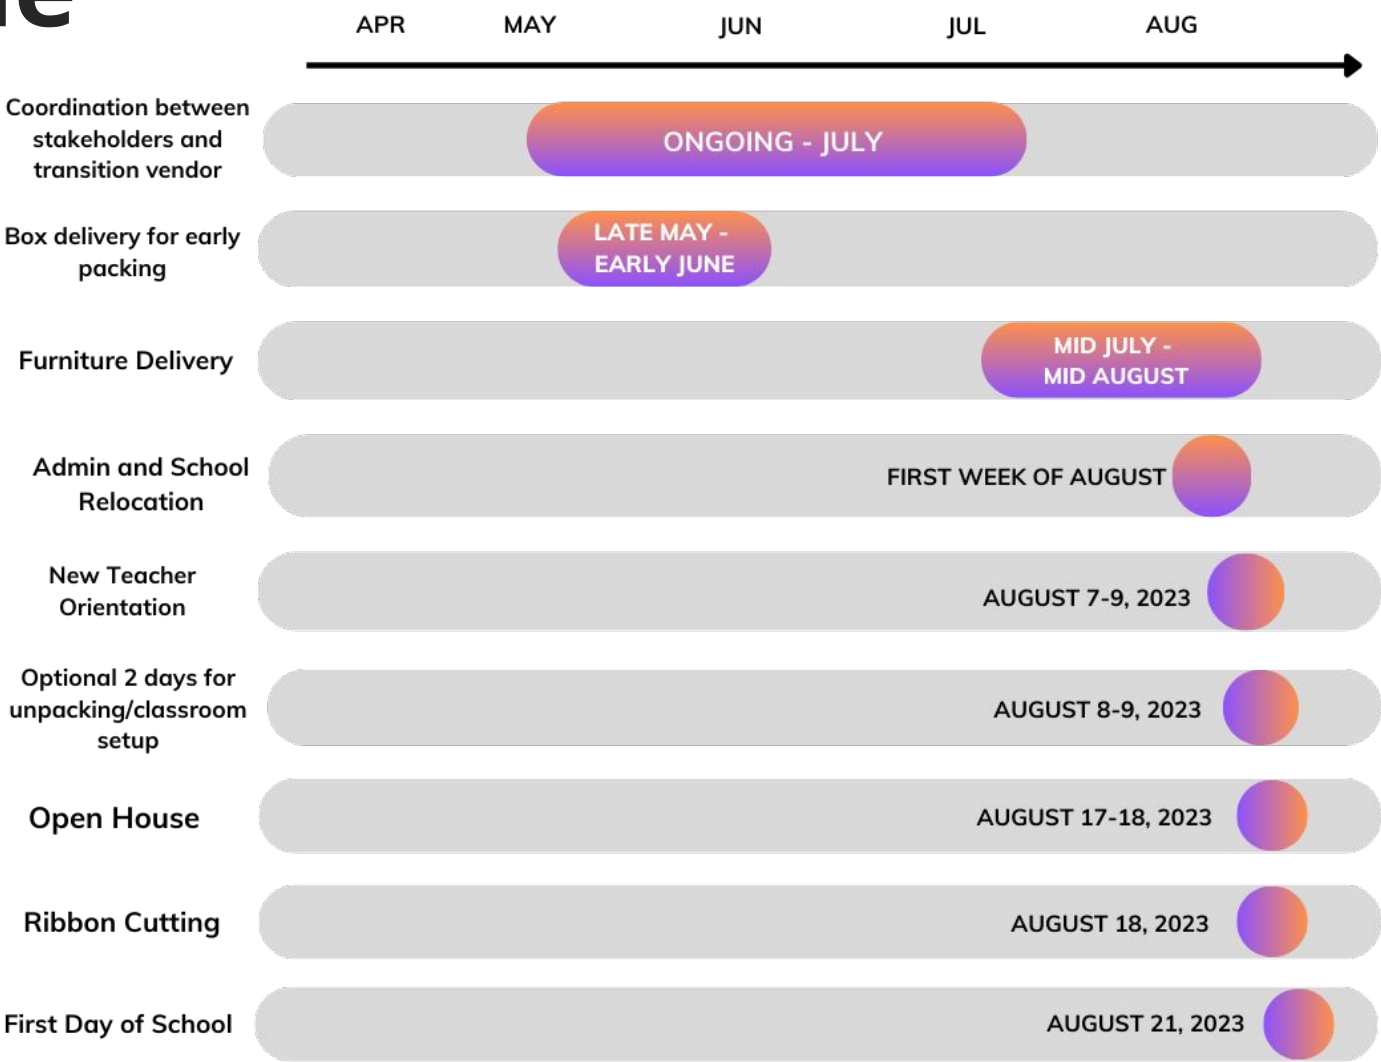



# Next Steps and Communication

- **Construction Phase:** Ongoing
- **Community Meeting:** Mid-July
- **Communications:**
  - ◆ Information communicated on the [Douglas MacArthur Modernization Page](#).
  - ◆ Sign up for our [CIP Newsletter](#)
  - ◆ Email: [newmacarthur@acps.k12.va.us](mailto:newmacarthur@acps.k12.va.us)



# Contacts

Erika Gulick, Executive Director for Facilities

[erika.gulick@acps.k12.va.us](mailto:erika.gulick@acps.k12.va.us)

Azuka Bartlett, Director of Capital Programs, Planning, and Design

[azjargal.bartlett@acps.k12.va.us](mailto:azjargal.bartlett@acps.k12.va.us)

Paul Youmbi, Construction Project Manager

[paul.youmbi@acps.k12.va.us](mailto:paul.youmbi@acps.k12.va.us)

Arte'a Funderburk, CIP Communications Specialist

[artea.funderburk@acps.k12.va.us](mailto:artea.funderburk@acps.k12.va.us)





# Questions?



**Interim Superintendent**  
Dr. Melanie Kay-Wyatt

**School Board**  
Meagan L. Alderton, Chair  
Jacinta Greene, Vice Chair

Willie F. Bailey, Sr.  
Kelly Carmichael Booz  
Abdel-Rahman Elnoubi

Christopher Harris  
Tammy Ignacio

Michelle Rief  
Ashley Simpson Baird
