


BOND UPDATE #209

6.16.23



Here's what is going on with our bond projects.

Enjoy!
Kristi

1. The finishing touches on the Grandstands' press box should be completed over the next couple of weeks.
2. Fencing work continues around the Athletic Field area and should be finished in the next few weeks.
3. Crews have laid the asphalt for the track. The next step is to apply the rubberized surface, and it will almost be complete!
4. Good progress has been made on the long jump, javelin, shot put, and discus areas. These should be finished over the next few weeks.
5. The masonry block has been installed on the exterior of the Athletic Field's ticket booth. Crews will now apply the final finishes.
6. The new CTE Wing's roofing is almost complete, along with the exterior sheathing. Interior framing work is now more than 90% finished, and the concrete slab has been poured in the mechanical mezzanine area.
7. The brick columns around the posts under the canopy (which will connect the Athletic and Academic wings) are now complete, and the area is ready to receive decorative fencing. This will create a nice courtyard area while providing a secure perimeter throughout the school day.
8. Crews continue to install curbing and gutters around the new parking areas. These areas are scheduled to have asphalt installed during the month of August.
9. The Bond Oversight Committee will hold their next meeting at 6 p.m. on Tuesday at Mountain View.
10. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://www.ferndalesd.org/bond-2019)
11. Below is the FHS project timeline as of May 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

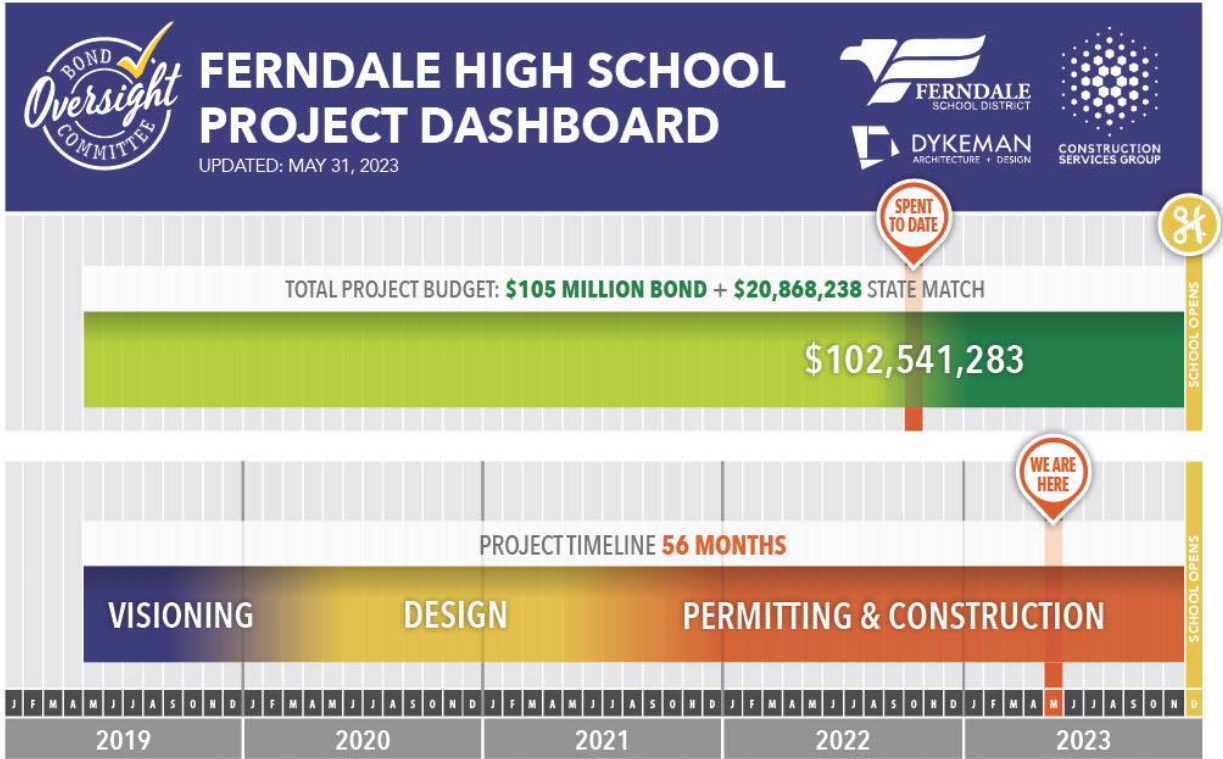

12. Below is a map showing the various components of the new FHS campus and when they'll be completed.

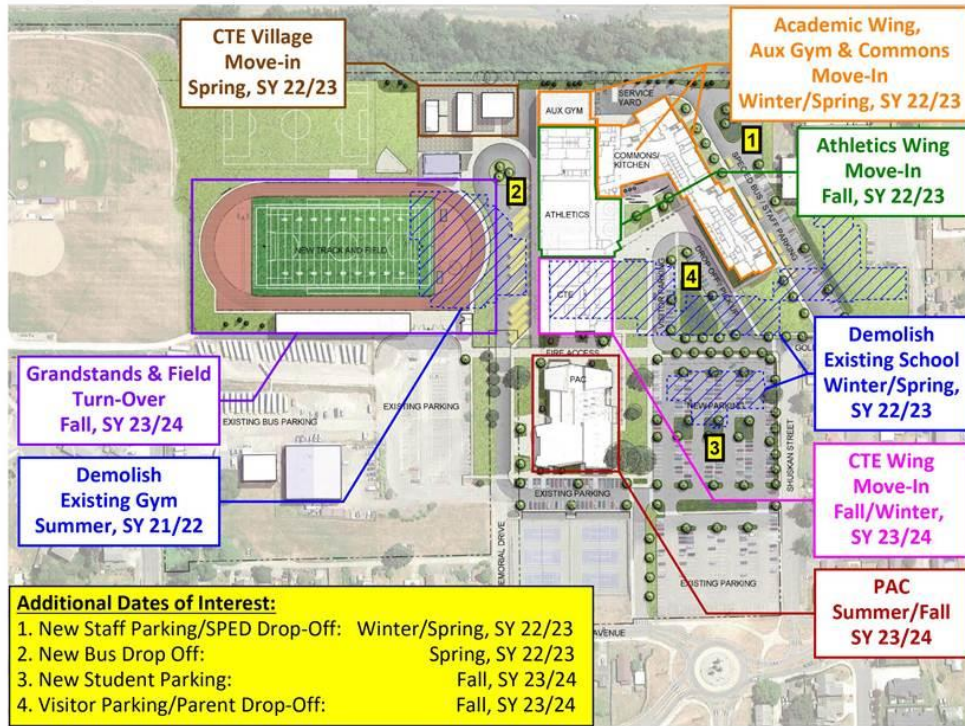

FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Exterior wall sheathing, framing and the mechanical mezzanine are completed for the CTE Wing



Masonry column wraps in the courtyard area are complete and ready for decorative fencing



The masonry at the new Athletic Field ticket booth is complete and ready for final finishes



Retaining wall construction at the south end of the new parking area



The new parent drop-off loop receiving curbs and gutters in preparation for asphalt



Asphalt installed on the track
