

THE NEW WRIGHT CITY HIGH SCHOOL

159 Roelker Rd.

Wright City, MO 63390




ONGOING SITE ACTIVITIES

(MAY – JUNE 2023)

- ▶ Grading and Excavation
 - ▶ Site Utilities
 - ▶ Footings and Foundations
 - ▶ Site Concrete
 - ▶ Steel Erection
 - ▶ Underground MEP
 - ▶ Storm Shelter Foundations
 - ▶ Retaining Walls
- 
- A series of three parallel white diagonal lines extending from the bottom right towards the top right of the slide, adding a modern, geometric design element.

LOOKING FORWARD

- ▶ Underground Utilities
 - ▶ Grading/Excavating East Half of the Property
 - ▶ Casting Slabs
 - ▶ Tilt Up Concrete
 - ▶ Underground MEP Rough In
 - ▶ Masonry
 - ▶ Steel Erection
 - ▶ Truss Placement
- 
- A series of white diagonal lines of varying lengths and thicknesses, located in the bottom right corner of the slide, creating a modern, abstract graphic element.

SITE STORM STRUCTURES



ONGOING SITE UTILITIES (WATER)



NORTH BUS PARKING




SOUTH ENTRANCE



FOUNDATIONS AND STEM WALLS



UNDERGROUND MEP

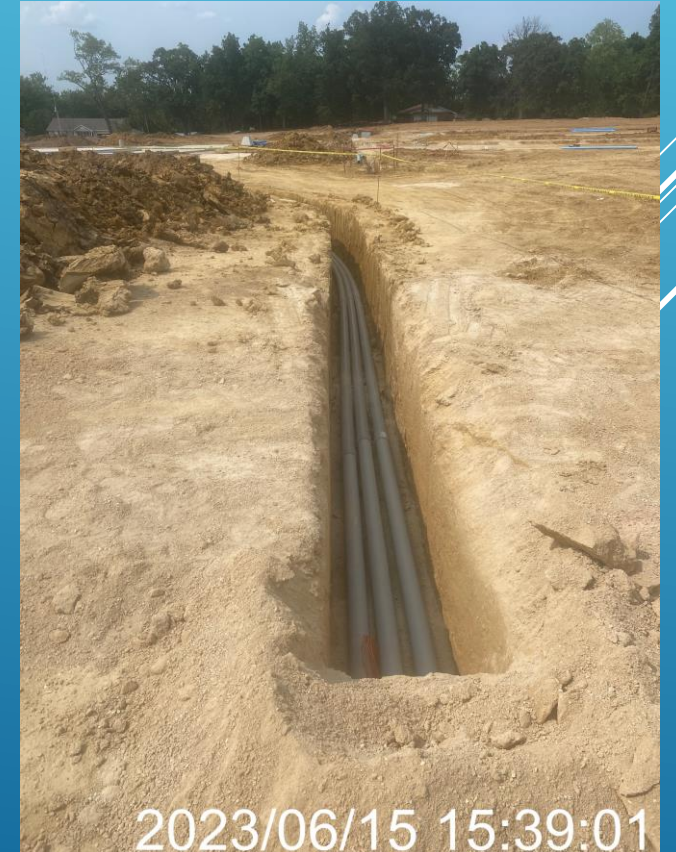


STEEL ERECTION




STORM SHELTER FOUNDATIONS



RETAINING WALL PREPARATION AND INSTALLATION

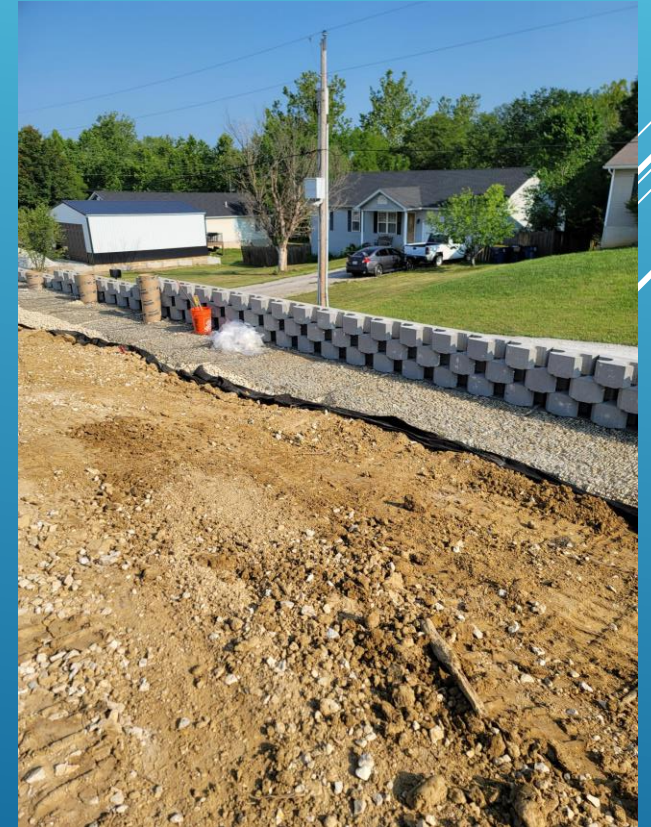

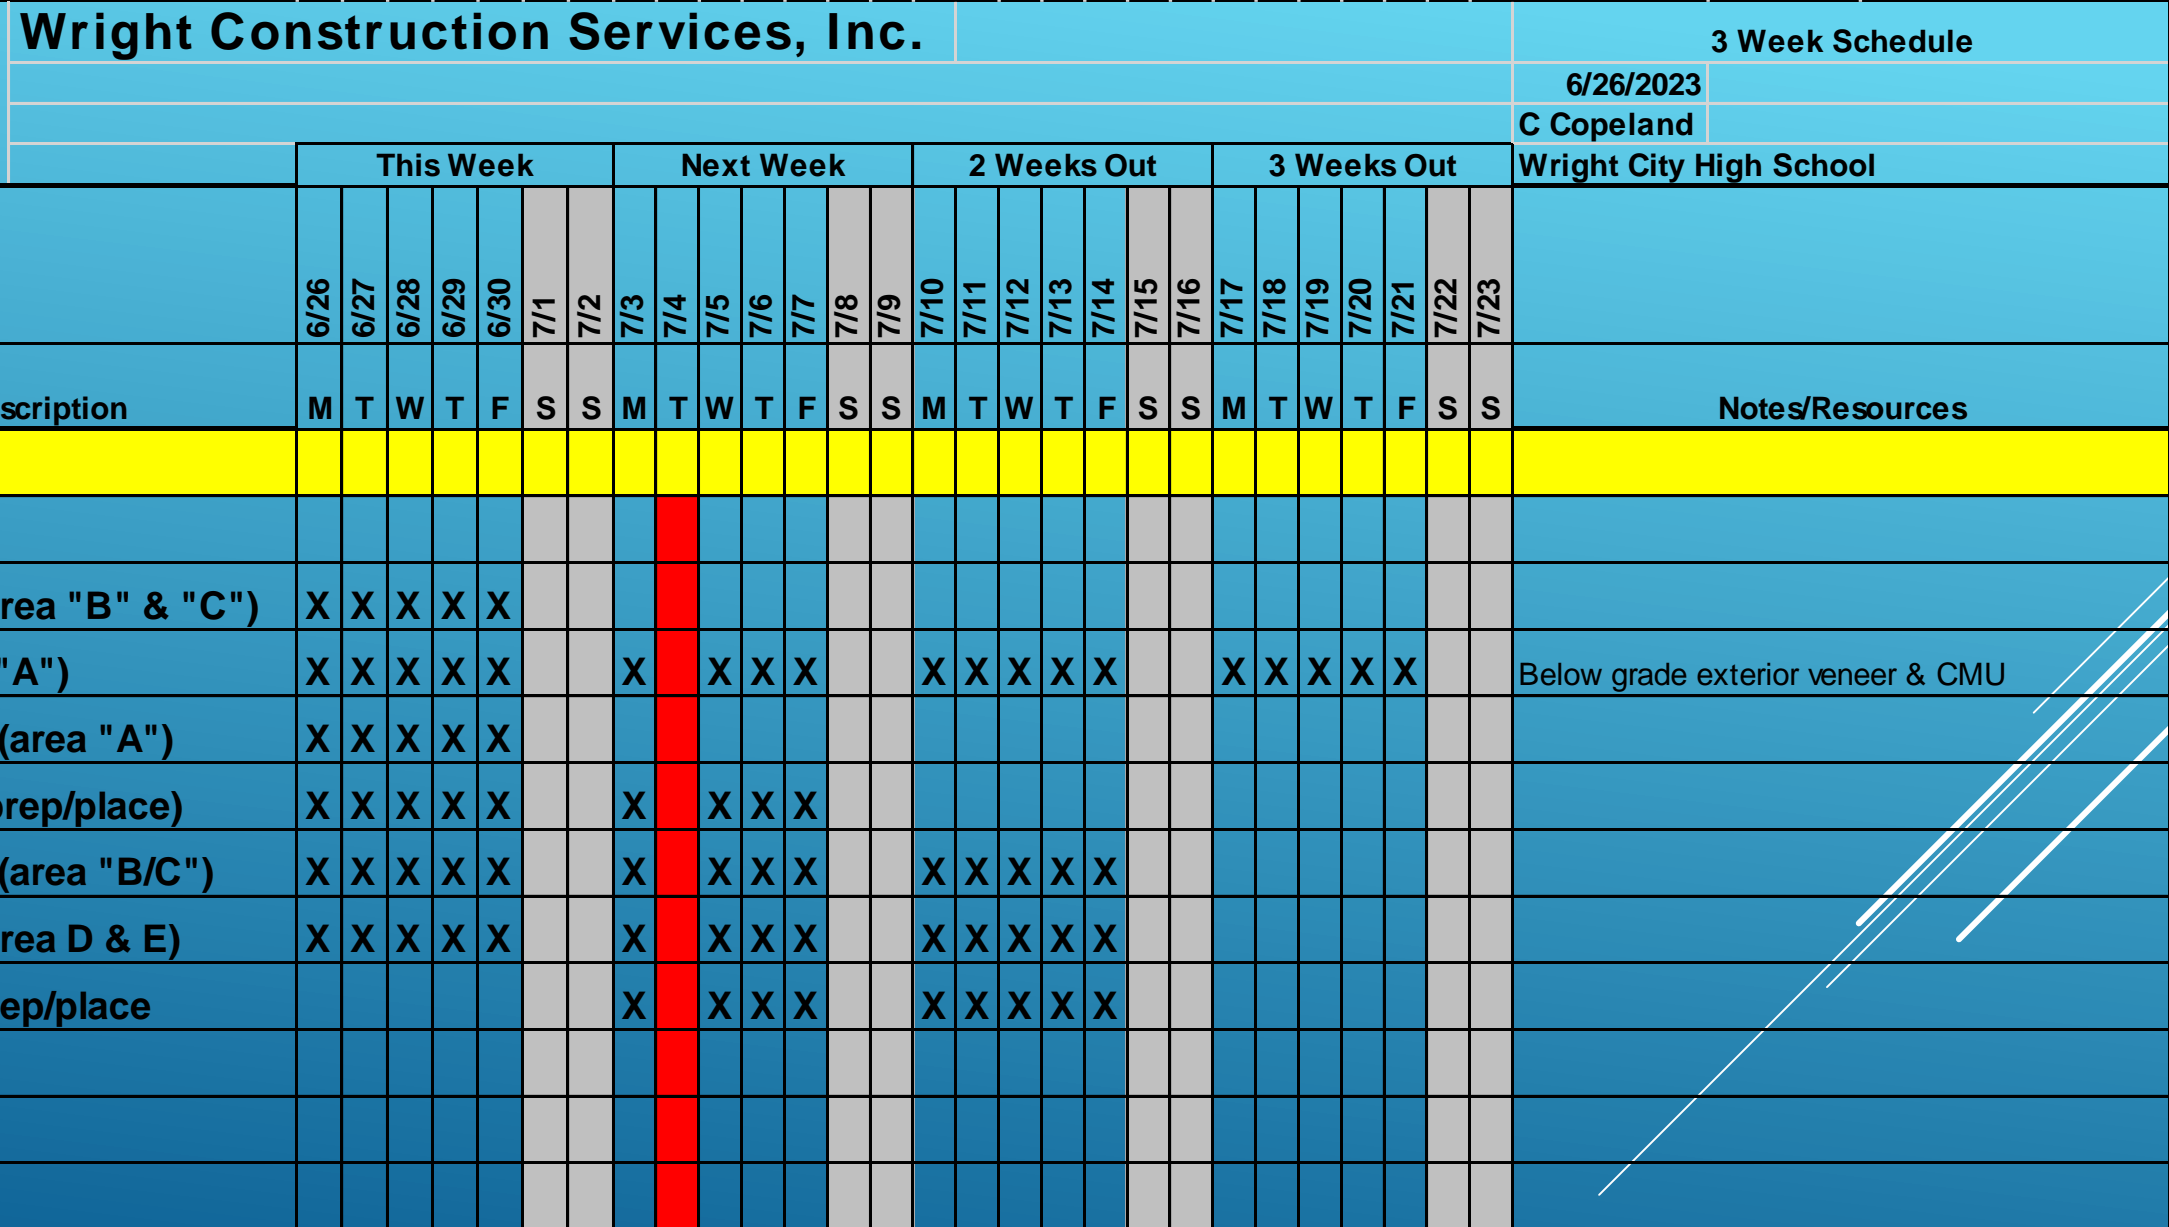

Wright Construction Services, Inc.

3 Week Schedule


6/26/2023

C Copeland

Wright City High School

Wright City High School		This Week							Next Week							2 Weeks Out							3 Weeks Out							Wright City High School
		6/26	6/27	6/28	6/29	6/30	7/1	7/2	7/3	7/4	7/5	7/6	7/7	7/8	7/9	7/10	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	
Work Description		M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	Notes/Resources
Sitework																														Sitework weather dependent
Grading		X	X	X	X	X			X		X	X	X			X	X	X	X	X										All areas working East towards creek
North retaining wall #6		X	X	X																										
Retaining walls #8 & #9					X	X			X																					Cotner residence immediately after #6
North retaining wall #7											X	X	X			X	X	X	X	X										
Fire Service Entry				X	X	X																								
Storm structures (South)									X		X	X	X																	Awaiting delivery (south property line) TBD
Site water (South main line)		X	X						X		X	X	X			X	X	X	X	X										After South Storm completes
Site water (East main line)		X	X	X	X	X			X		X	X	X			X	X	X	X	X										After South Storm completes
Water North easement		X	X	X	X	X																								
Phase 1 water service																														pending PWSD approval of Phased service
Box Culvert at Creek																														Pending ACOE Permit

Gender	Age Group	Percentage of Respondents
Male	18-24	~85%
	25-34	~75%
	35-44	~65%
	45-54	~55%
	55-64	~45%
	65-74	~35%
	75+	~25%
Female	18-24	~75%
	25-34	~65%
	35-44	~55%
	45-54	~45%
	55-64	~35%
	65-74	~25%
	75+	~15%

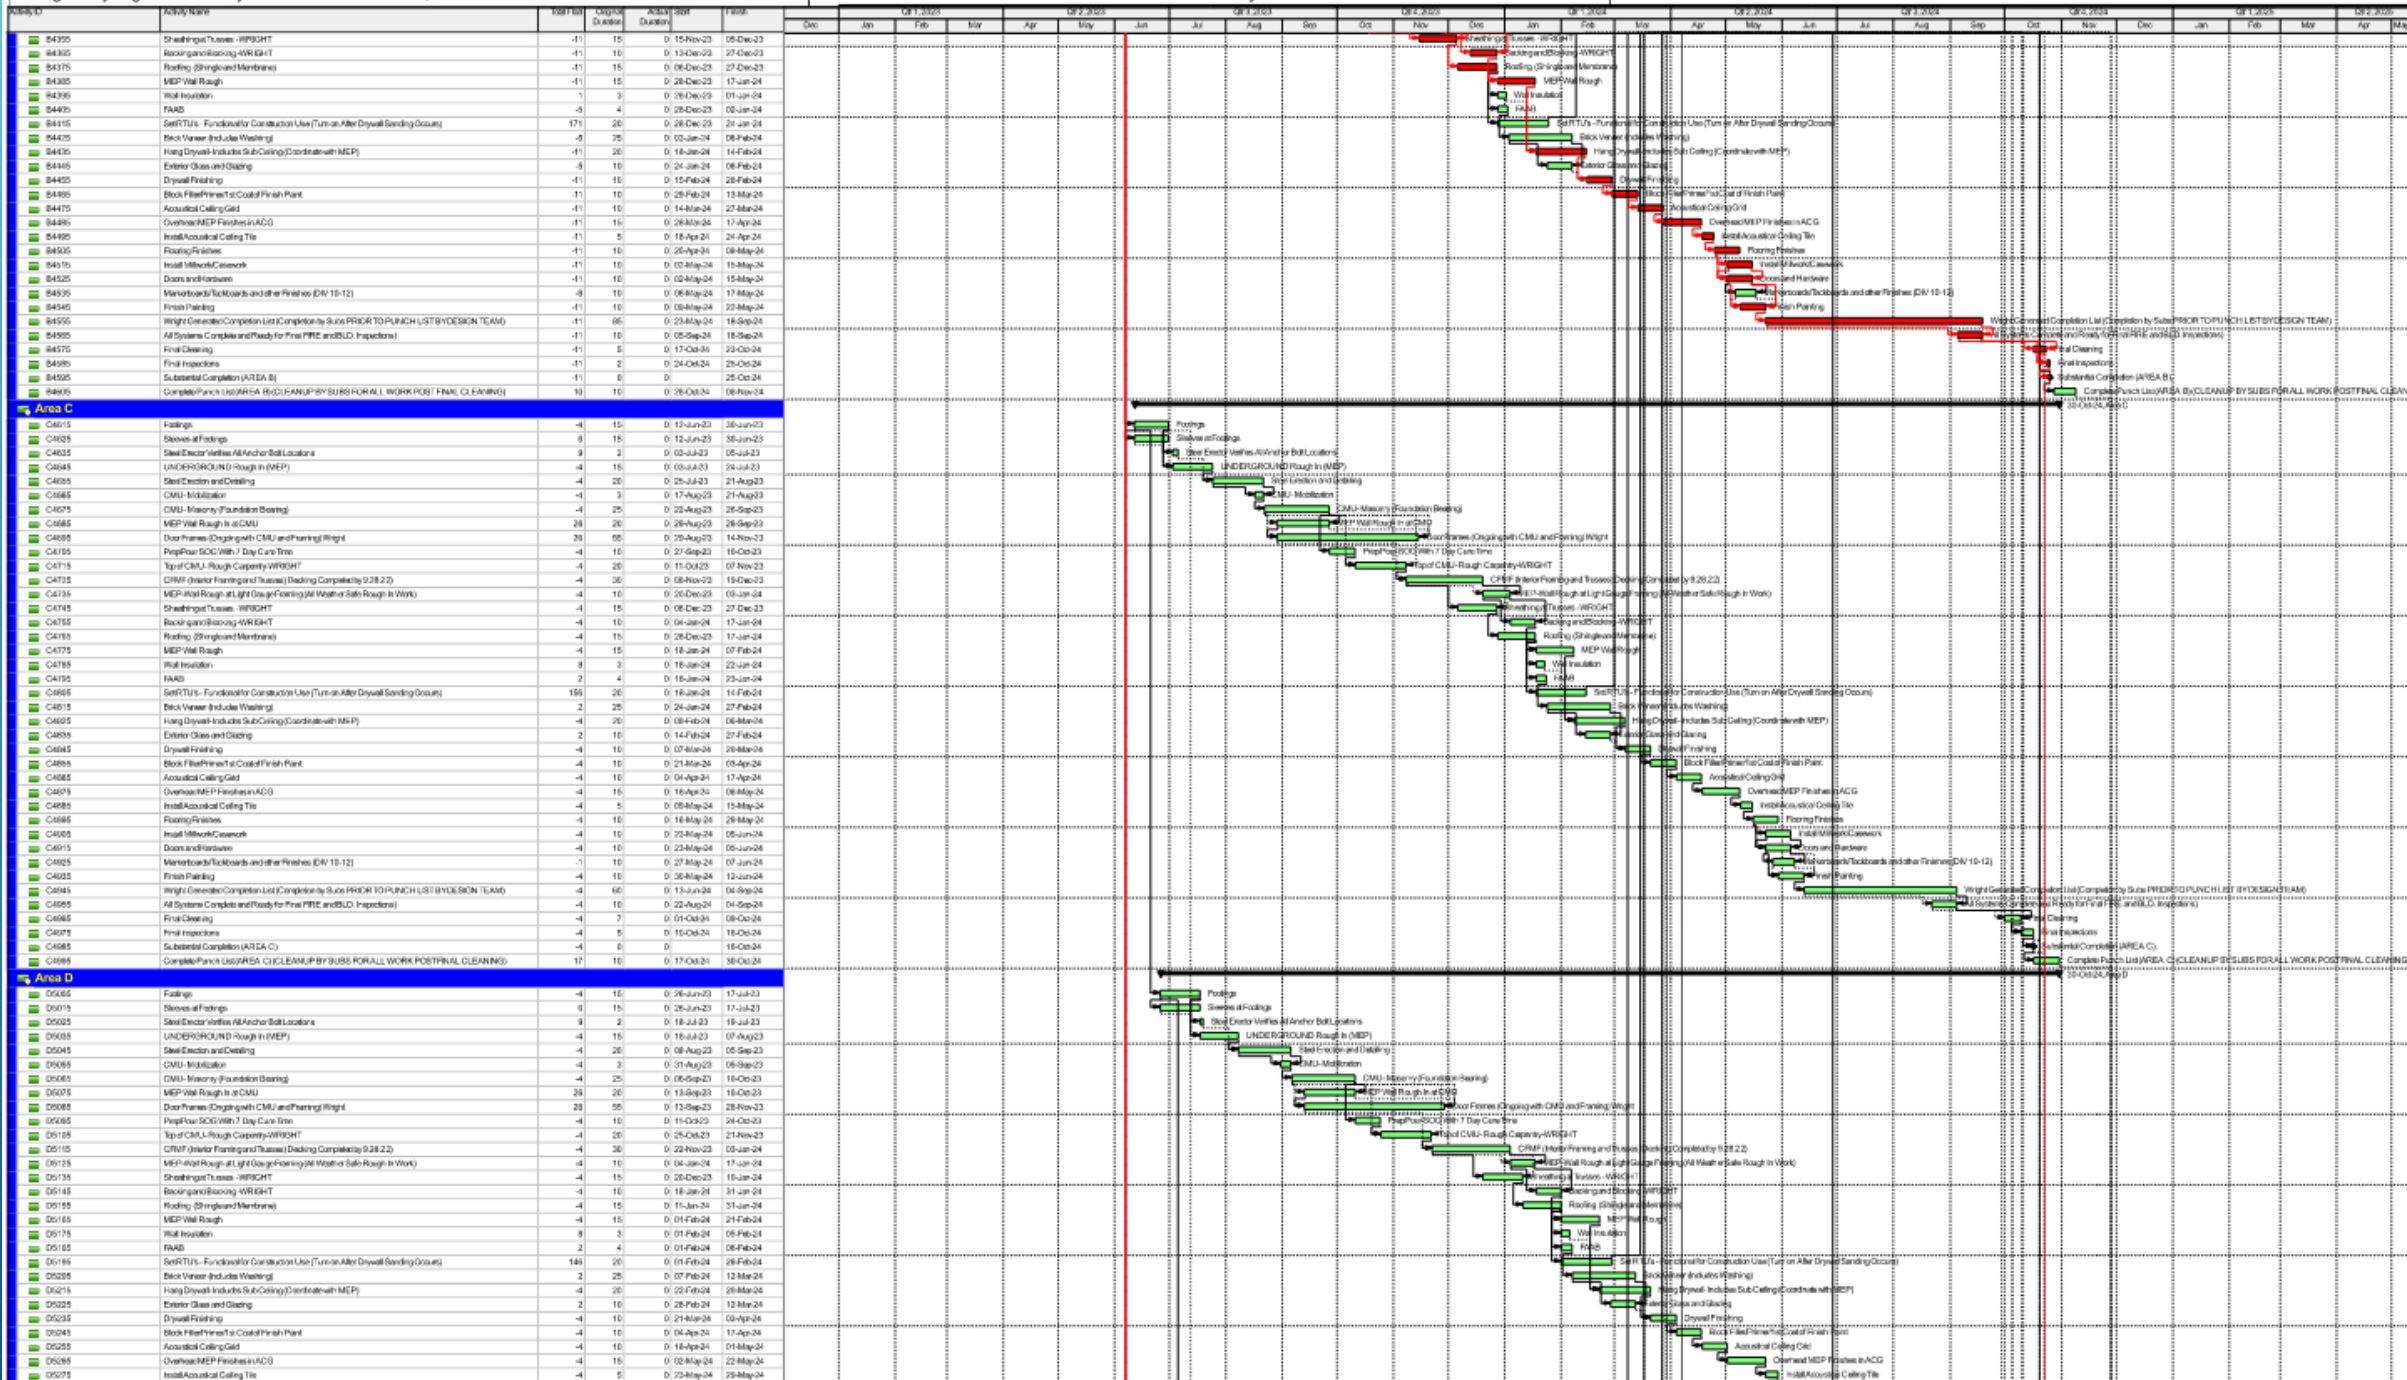

Area E


Task ID	Task Name	Duration	Start Date	End Date
E0020	Paving/Finishes	4	10	01-Jul-23
E0055	Install Milwork/Casework	4	10	01-Jul-23
E0058	Doors and Hardware	4	10	01-Jul-23
E0011	Manwork/Thickboards and other Finishes (DN 10-12)	4	10	01-Jul-23
E0023	Finish Painting	4	10	01-Jul-23
E0039	Weight Concrete Completion List (Complete by Sub PRIOR TO PUNCH LIST BY DESIGN TEAM)	4	10	01-Jul-23
E0048	All Systems Complete and Ready for Final PFI and BLD Inspections	4	10	01-Jul-23
E0088	Final Cleaning	4	10	01-Jul-23
E0088	Final Inspections	4	10	01-Jul-23
E0088	Substantial Completion (AREA D)	4	10	01-Jul-23
E0088	Complete Punch List (AREA D) (CLEANUP BY SUBS FOR ALL WORK POST FINAL CLEANING)	17	10	01-Jul-23

Area F

Task ID	Task Name	Duration	Start Date	End Date
F0020	Paving (VEE JV)	4	10	01-Jul-23
F0055	Install Milwork/Casework	4	10	01-Jul-23
F0058	Doors and Hardware	4	10	01-Jul-23
F0011	Manwork/Thickboards and other Finishes (DN 10-12)	4	10	01-Jul-23
F0023	Finish Painting	4	10	01-Jul-23
F0039	Weight Concrete Completion List (Complete by Sub PRIOR TO PUNCH LIST BY DESIGN TEAM)	4	10	01-Jul-23
F0048	All Systems Complete and Ready for Final PFI and BLD Inspections	4	10	01-Jul-23
F0088	Final Cleaning	4	10	01-Jul-23
F0088	Final Inspections	4	10	01-Jul-23
F0088	Substantial Completion (AREA E)	4	10	01-Jul-23
F0088	Complete Punch List (AREA E) (CLEANUP BY SUBS FOR ALL WORK POST FINAL CLEANING)	25	10	01-Jul-23

Area G

Task ID	Task Name	Duration	Start Date	End Date
G0020	Paving	4	10	01-Jul-23

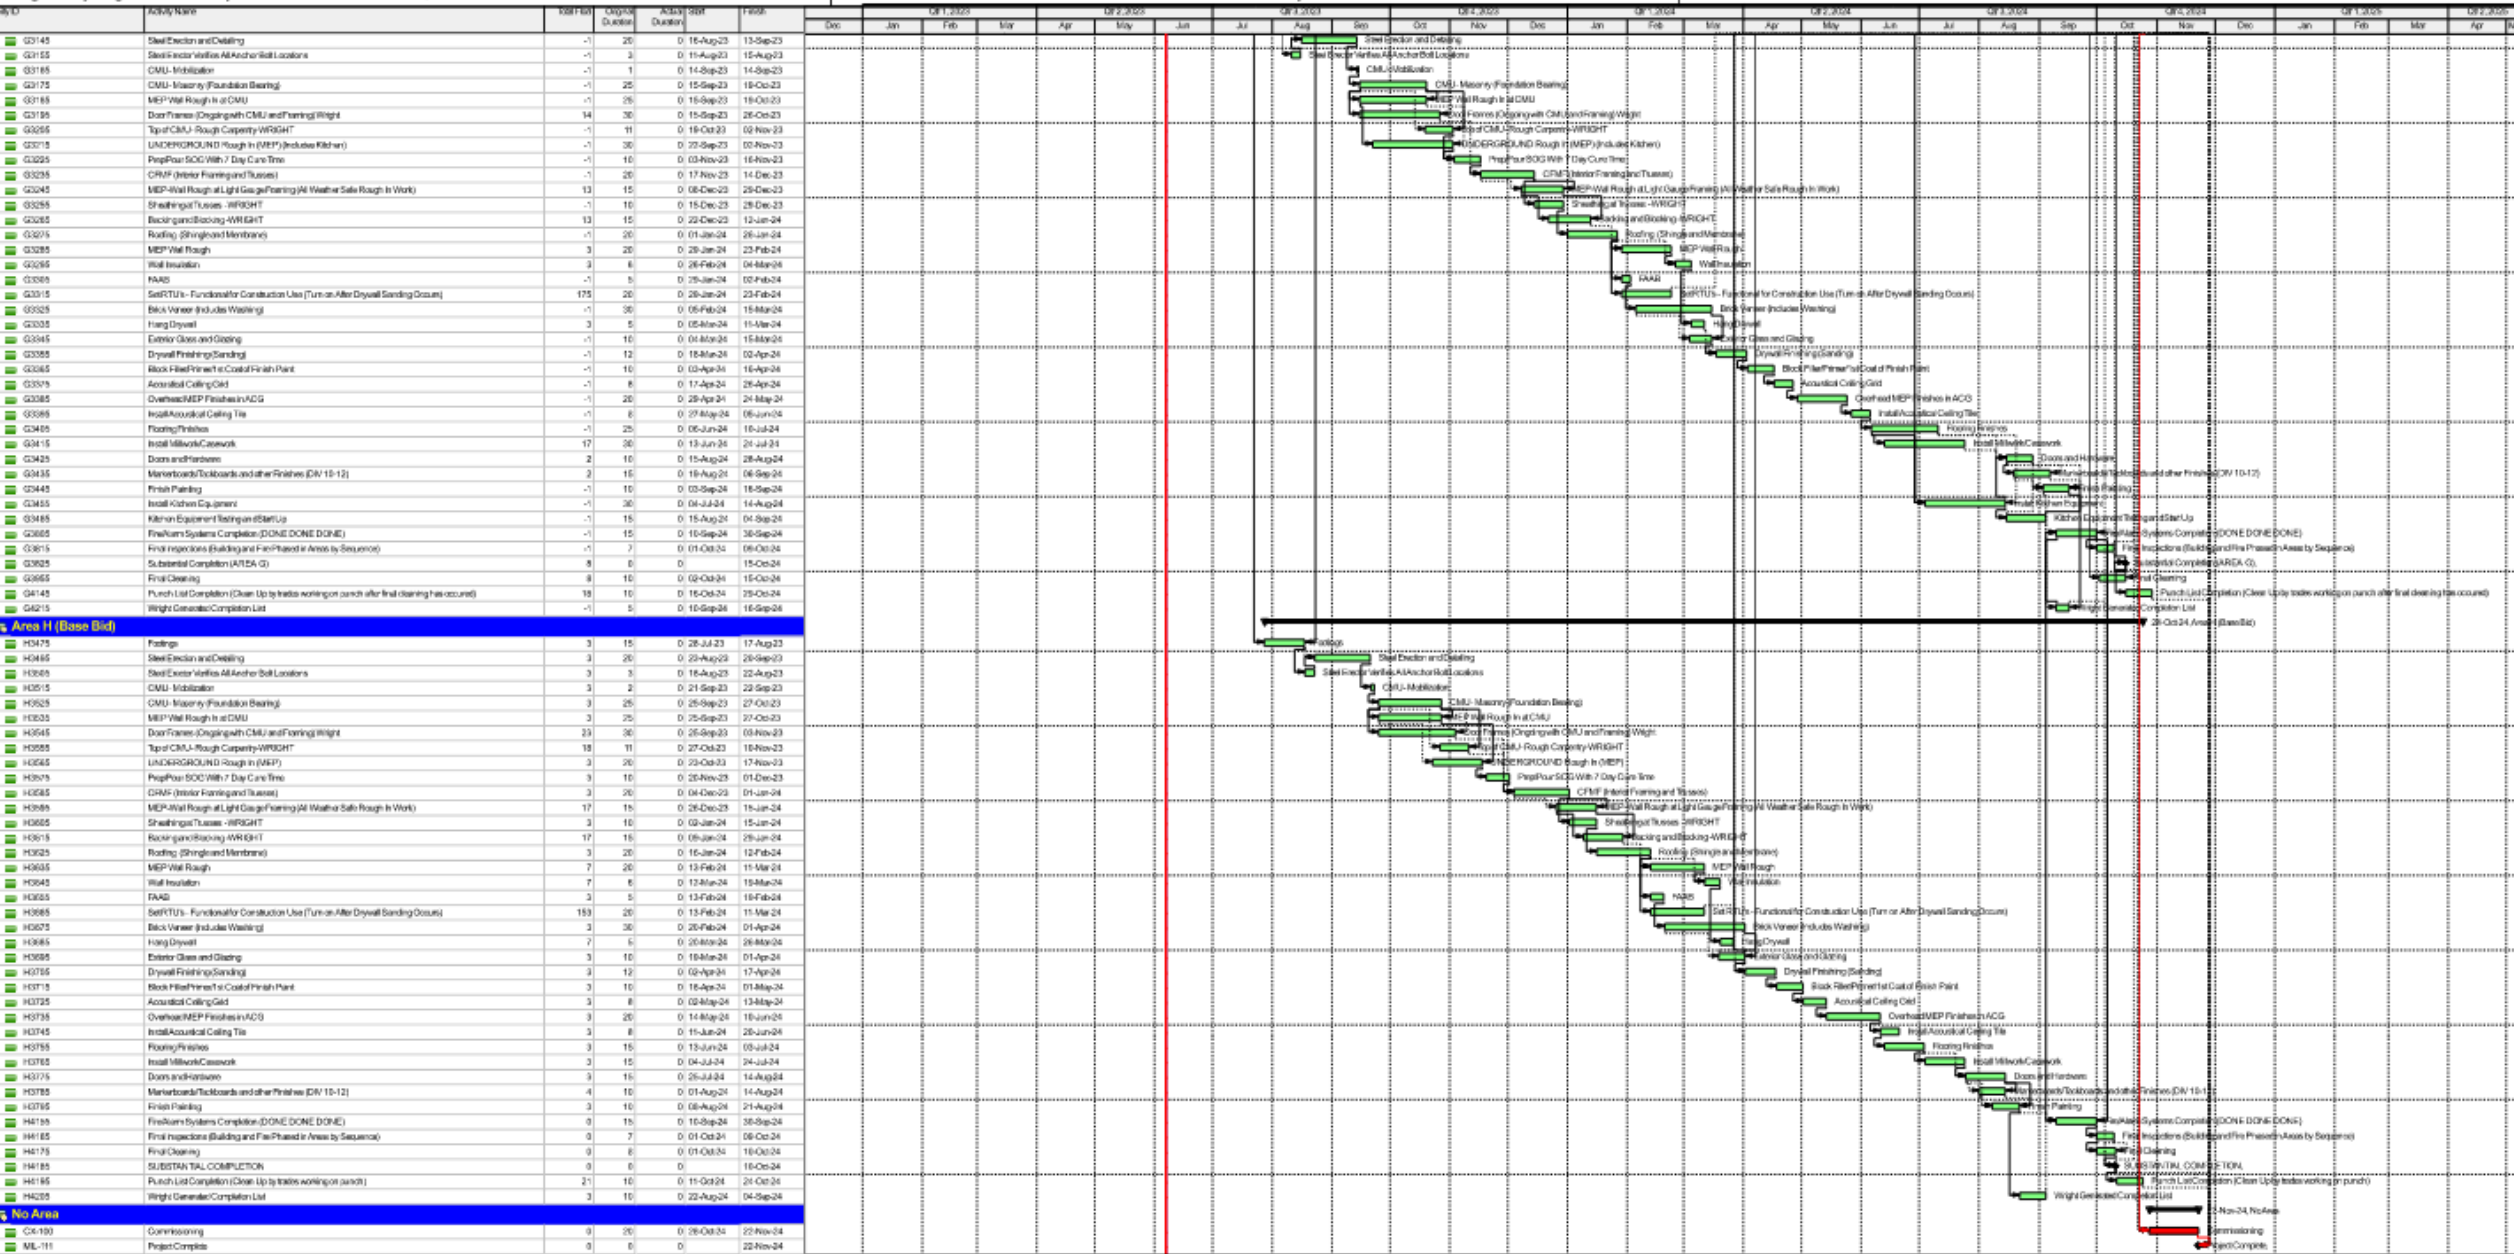

CLOSING

- ▶ Questions or Comments from the Board of Education?

