

## Legend for Areas of Construction –

A - 9<sup>th</sup> Grade    B – Commons    C – Admin    D – Science    E – Cafeteria/Dining    F – Fine Arts    G – Fine Arts/Aud  
H – Kitchen    J – Arena/Boys Athletics    K- Girls Athletics    L – Aux Gym/Storm Shelter    M – Boys Athletics  
N – Weight Room    P – 12<sup>th</sup> Grade    Q – Classrooms    R – Chemistry Labs    S- Science Labs  
T – Open above Commons    U – Fine Arts    V – Upper Auditorium Classrooms    W – Above Arena

## WORK IN PROGRESS

For the period covering 4/22/23 through 4/28/23, the following site activities were observed:

- Completed learning stair concrete pour
- Roofing Area G in progress
- Catwalk steel erection Area G
- Drywall tape and float Area A
- Continued CMU in Areas G,J, N & L
- Formed Athletics Transformer Pad

## LOOK A HEAD

The following activities are projected to be in progress over the next two weeks:

- Pour Athletics Transformer Pad
- Steel erection Area G
- Roofing Areas H & J
- Primer paint Area C & D
- Drywall close-up Area S
- Continue MEP rough-in Areas F & G

## SITE AERIAL

Available via Dropbox Link

<https://bartlettcocke.box.com/s/jpdk10l5om2jawi4vpybn2cu6dwo04nq>



Learning Stair Concrete



Block Filling and OH MEP Area F




Area C Drywall Priming



Entry Canopy



Area K Fireproofing

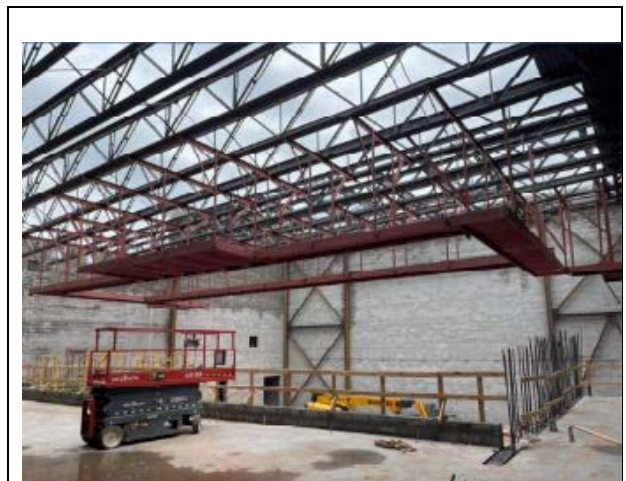

Auditorium Catwalk Steel

