

BOND UPDATE #214


7.21.23

Here's what is going on with our bond projects.


Enjoy!

Kristi

1. The final stormwater systems will soon be installed along Golden Eagle Drive and Shuksan Street. When this is finished, the area will be ready for the final asphalt installation.
2. Curbs, gutters, sidewalks and light poles continue to be installed in the main parking area in preparation for crews laying asphalt in August.
3. Crews are now planting grass on the practice sports field east of the main Athletic Field. The practice field should be ready for student use in the fall of 2024.
4. Preparation work has begun on the exterior of the Performing Arts Center and weight room building. These buildings will eventually be painted to match the rest of the new campus.
5. Seismic upgrade work and new fire alarm installation continues in the Performing Arts Center. This work will be complete in the PAC's classroom portion by the time school opens on August 30.
6. Windows have now been installed in the Grandstands' ticket booth.
7. Crews will install the rubberized track surface over the next couple of weeks.
8. The Ferndale School Board will receive an update on bond-related items at their next regular meeting at 6 p.m. Tuesday at Mountain View.
9. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://www.ferndalesd.org/Bond-2019)
10. Below is the FHS project timeline as of May 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

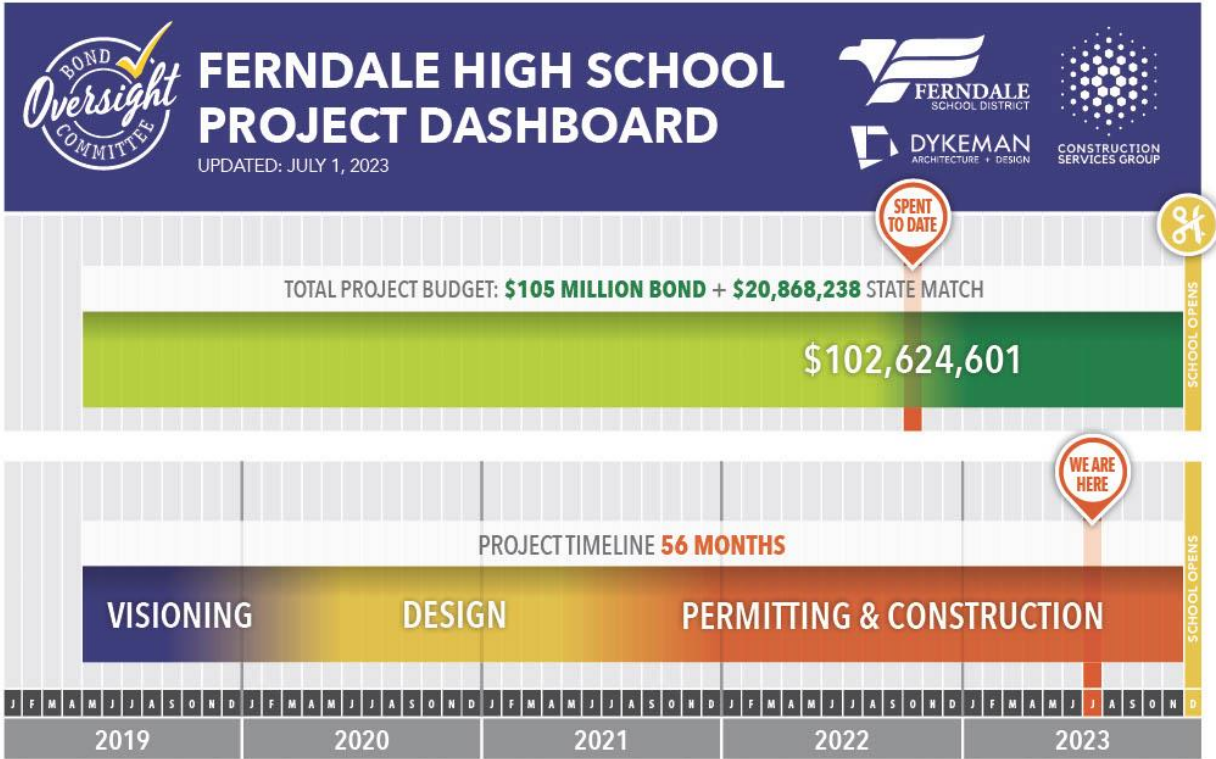

11. Below is a map showing the various components of the new FHS campus and when they'll be completed.

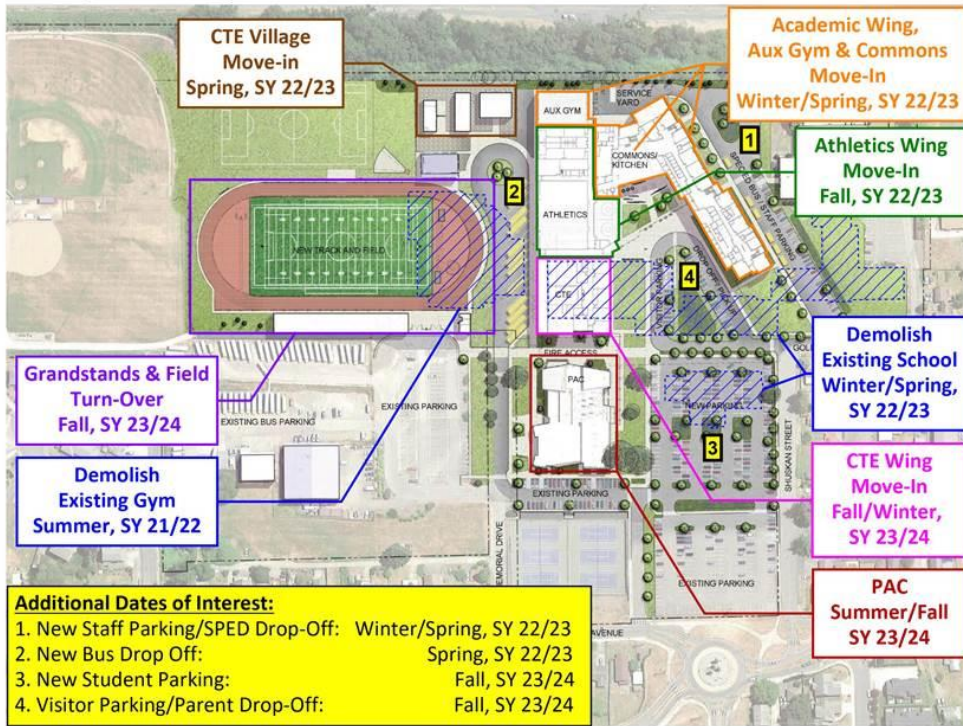

FHS Move-In Plan



If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



The outside of the new CTE Wing will be complete once masonry is installed



Ductwork installation in the new CTE Wing



Parking lot pre-asphalt preparation work continues



Final flooring installation in the main kitchen's coolers



Prep work for the rubberized track surface
