

New Middle School @ Polo Club



Week Ending July 14, 2023

New Middle School @ Polo Club


➤ Completed Work:

- Continue to prep slab in area D
- Continue CMU in Area A and B
- Continue MEP in Area A, C underground in Area B and D
- Curb and gutters completed on east side
- Set roof joist and installed decking in Area F locker room
- Continue to install ICF in Area A

➤ Upcoming Work/Look Ahead:

- Set steel in Area A for hollow core
- Continue ICF in Area A
- Continue MEP in Area A, C and D
- Continue to lay CMU in Area A
- Install hollow core in Area A
- Asphalt to start on east side at curbed areas
- Pour rest of slab in area D
- **Geothermal Drilling Continues (can be loud)**

Key Plan

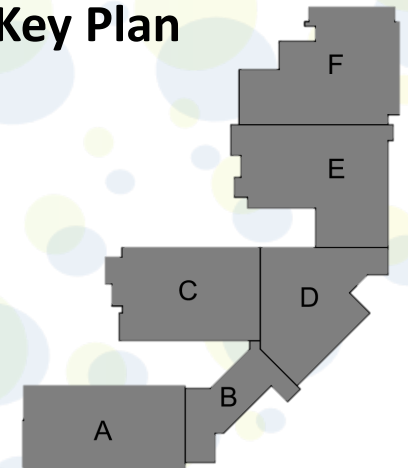

Area A – Stala Frame Setting



Week Ending July 14, 2023

Area B - Main Entry Column Install



Week Ending July 14, 2023

Area B-Main Entry Slab Prep



Week Ending July 14, 2023

Area B - Slab Poured and ICF Started



Week Ending July 14, 2023

Area B-Stala Frame Setting



Week Ending July 14, 2023

Area E - Mezzanine Hollow Core Grouted



Week Ending July14, 2023

Area F - Gym Locker Room Joist Install



Week Ending July 14, 2023

Site – Curbs and Gutter Install



Week Ending July 14, 2023

Front Entry/Media Center Rendering



Week Ending July 14, 2023
